

Agreement No. CE 60/2017 (EP) Environmental Team for Tung Chung New Town Extension (East) – Design and Construction Monthly Environmental Monitoring & Audit Report for May 2024

#### PREPARED FOR



Civil Engineering and Development Department

DATE 14 June 2024

REFERENCE 0445700



#### DOCUMENT DETAILS

DOCUMENT TITLE	Agreement No. CE 60/2017 (EP) Environmental Team for Tung Chung New Town Extension (East) – Design and Construction
DOCUMENT SUBTITLE	Monthly Environmental Monitoring & Audit Report for May 2024
PROJECT NUMBER	0445700
Date	14 June 2024
Version	01
Author	KS
Client name	Civil Engineering and Development Department

#### DOCUMENT HISTORY

			ERM APPR	OVAL TO ISSUE		
VERSION	REVISION	AUTHOR	REVIEWED BY	NAME	DATE	COMMENTS
1	N/A	KS	RC	CAR	06.14.2024	N/A



# Agreement No. CE 60/2017 (EP) Environmental Team for Tung Chung New Town Extension (East) – Design and Construction

Monthly Environmental Monitoring & Audit Report for May 2024

Craig Reid Partner

ERM-Hong Kong, Limited 2507 One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong T +852 2271 3000

© Copyright 2024 by The ERM International Group Limited and/or its affiliates ('ERM'). All Rights Reserved. No part of this work may be reproduced or transmitted in any form or by any means, without prior written permission of ERM.





# **Tung Chung New Town Extension**

# Environmental Certification Sheet for Environmental Permit No. EP-519/2016

#### **Reference Document/Plan**

Document/Plan to be Certified:	Monthly Environmental Monitoring & Audit Report for May 2024 (Revision 1)
Date of Report:	14 June 2024

#### **Reference EP Condition**

Environmental Permit Condition:

Condition 3.5

The Permit Holder shall submit 4 hard copies and 1 electronic copy of Monthly EM&A Reports for the construction stage of the Project to the Director, within 2 weeks after the end of the reporting month. The monthly EM&A Reports shall include an executive summary of all environmental audit results, together with actions taken in the event of non-compliance (exceedances) of the environmental quality performance limits (Action and Limit Levels), complaints received and emergency events relating to violation of environmental legislation (such as illegal dumping and landfilling). The submissions shall be certified by the ET Leader and verified by the IEC as having complied with the requirements as set out in the updated EM&A Manual before submission to the Director. Additional copies of the Monthly EM&A Reports shall be provided upon request by the Director.

#### **ET Certification**

I hereby certify that the above referenced document/plan complies with the above referenced condition of EP-519/2016

Kelvin So Environmental Team Leader

felino

Date:

14 June 2024



Your Ref.

Our Ref. 198377-0850

Date 14 June 2024

Sustainable Lantau Office Civil Engineering and Development Department 13/F, North Point Government Offices 333 Java Road, North Point Hong Kong

Attention: Mr. Rafael TANG / Mr. K.T. WO

Dear Sir,

#### Agreement No. CE 59/2017 (EP) Independent Environmental Checker for Tung Chung New Town Extension – Investigation Monthly Environmental Monitoring & Audit Report for May 2024 for TCE

We refer to the Monthly Environmental Monitoring & Audit Report for May 2024 for Tung Chung New Town Extension (East) (TCE) dated June 2024 and certified by the Environmental Team (ET) Leader of TCE on 14 June 2024. Please note the submission is hereby verified, in accordance with the requirement stipulated in Condition 3.5 of EP-519/2016.

Should you have any query, please feel free to contact the undersigned at 2608 7314 (<u>chuawo@binnies.com</u>) or our Edward Lau at 3894 9695 (<u>lauky@binnies.com</u>).

Yours faithfully, for and on behalf of BINNIES HONG KONG LIMITED

UL

MANUEL CHUA INDEPENDENT ENVIRONMENTAL CHECKER

cc: ET Leader / TCE – ERM (Attn: Mr. Kelvin So) [by Email: <u>kelvin.so@erm.com</u>] PM / TCE – AECOM (Attn: Mr. Chris Cheung) [by Email: <u>crec1@tce-aecom.com</u>]

(a)

binnieshk@binnies.com

 Binnies Hong Kong Limited
 43/F, AIA Kowloon Tower, 100 How Ming Street, Kwun Tong, Kowloon, Hong Kong 賓尼斯工程顧問有限公司
 香港九龍觀塘巧明街 100 號友邦九龍大樓 43 樓

+852 2601 3988



Member of the Association of Consulting Engineer of Hong Kong

By Post



+852 2601 1000

# CONTENTS

EXEC	CUTIVE SUMMARY	I
BREA	CHES OF ACTION AND LIMIT LEVELS FOR AIR QUALITY	II
BREA	CHES OF ACTION AND LIMIT LEVELS FOR NOISE	II
BREA	CHES OF ACTION AND LIMIT LEVELS FOR WATER QUALITY	II
ECO-	SHORELINE MONITORING	II
SOFT	SHORE ECOLOGICAL MONITORING	II
ENVI	RONMENTAL COMPLAINTS, NON-COMPLIANCE & SUMMONS	II
REPO	ORTING CHANGE	II
KEY I	ISSUES FOR THE COMING MONTH	II
1.	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	SCOPE OF THE EM&A REPORT	2
1.3	ORGANIZATION STRUCTURE	2
1.4	SUMMARY OF CONSTRUCTION WORKS	4
1.5	SUMMARY OF EM&A PROGRAMME REQUIREMENTS	7
1.6	STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE ENVIRONMENTAL	PERMIT 9
1.7	STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS	9
2.	EM&A RESULTS FOR TUNG CHUNG EAST	10
2.1	AIR QUALITY	10
2.2	<ul> <li>2.1.1 Monitoring Requirements and Equipment</li> <li>2.1.2 Monitoring Schedule for the Reporting Month</li> <li>2.1.3 Results and Observations</li> <li>NOISE MONITORING</li> </ul>	10 10 10 11
	<ul><li>2.2.1 Monitoring Requirements and Equipment</li><li>2.2.2 Monitoring Schedule for the Reporting Month</li><li>2.2.3 Results and Observations</li></ul>	11 12 12
2.3	WATER QUALITY MONITORING	12
2.4	COMPENSATION WOODLAND MONITORING	13
2.5	PRESERVED/TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE MONI	ITORING 13
2.6	<ul> <li>2.5.1 Preserved Plant Species of Conservation Importance</li> <li>2.5.2 Transplanted Plant Species of Conservation Importance</li> <li>ECO-SHORELINE MONITORING</li> </ul>	13 13 14
2.7	SOFT SHORE ECOLOGICAL MONITORING	14
2.8	EM&A SITE INSPECTION	14
2.9	WASTE MANAGEMENT STATUS	17
2.10	LANDSCAPE AND VISUAL MONITORING	17



2.11	IMPLEM	ENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	20
2.12		RY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL CUTIONS	20
3.	FUTUR	E KEY ISSUES	22
3.1	CONSTR	RUCTION PROGRAMME FOR THE COMING MONTH	22
3.2	MONITO	DRING SCHEDULE FOR THE COMING MONTH	27
4.	CONCL	USION AND RECOMMENDATION	28
ANN	EX A	PROJECT ORGANISATION	
ANN	EX B	ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE	
ANN	EX C	STATUS OF SUBMISSIONS AND IMPLEMENTATION STATUS OF MITIGATION MEASURES UNDER EP	
ANN	EX D	STATUS OF STATUTORY ENVIRONMENTAL REQUIREMENS	
ANN	EX E	AIR QUALITY	
ANN	EX E1	CALIBRATION CERTIFICATES FOR AIR QUALITY	
ANN	EX E2	MONITORING SCHEDULE FOR AIR QUALITY	
ANN	EX E3	MONITORING RESULTS FOR AIR QUALITY	
ANN	EX E4	EVENT AND ACTION PLAN FOR AIR QUALITY	
ANN	EX F	NOISE	
ANN	EX F1	CALIBRATION CERTIFICATES FOR NOISE	
ANN	EX F2	MONITORING SCHEDULE FOR NOISE	
ANN	EX F3	MONITORING RESULTS FOR NOISE	
ANN	EX F4	EVENT AND ACTION PLAN FOR NOISE	
ANN	EX G	COMPENSATION WOODLAND MONITORING	
ANN	EX H	PRESERVED/TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANC	CE
ANN	EX H1	PRESERVED PLANT SPECIES OF CONSERVATION IMPORTANCE	
ANN	EX H2	TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE	
ANN	EX I	ECO-SHORELINE MONITORING	
ANN	EX J	LANDSCAPE AND VISUAL MONITORING	
ANN	EX J1	EXAMPLES OF LANDSCAPE AND VISUAL MITIGATION MEASURES	
ANN	EX J2	EVENT AND ACTION PLAN FOR LANDSCAPE AND VISUAL MITIGATION MEASURES	
ANN	EX K	CUMULATIVE STATISTICS ON EXCEEDANCES, ENVIRONMENTAL COMPLAINTS NOTIFICATION OF SUMMONS AND STATUS OF PROSECUTIONS	»,
ANN	EX L	MONITORING SCHEDULE FOR THE NEXT REPORTING PERIOD	



LIST OF TAB	BLES	
TABLE 1.1	CONTACT INFORMATION OF KEY PERSONNEL	2
TABLE 1.2	MAJOR ACTIVITIES IN THE REPORTING PERIOD	4
TABLE 1.3	SUMMARY OF STATUS FOR THE ENVIRONMENTAL ASPECTS UNDER THE UPDATED EM&A MANUAL	7
TABLE 2.1	ACTION AND LIMIT LEVELS FOR 1-HOUR TSP	10
TABLE 2.2	AIR QUALITY MONITORING DETAILS	10
TABLE 2.3	SUMMARY OF 1-HOUR TSP MONITORING RESULTS IN THE REPORTING PERIOD	11
TABLE 2.4	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE	11
TABLE 2.5	NOISE MONITORING DETAILS	11
TABLE 2.6	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS IN THE REPORTING PERIOD	12
TABLE 2.7	KEY OBSERVATIONS IDENTIFIED DURING THE SITE INSPECTION IN THIS REPORTING MONTH	15
TABLE 2.8	QUANTITIES OF DIFFERENT WASTE GENERATED AND IMPORTED FILL MATERIALS	17
TABLE 2.9	IMPLEMENTATION STATUS OF LANDSCAPE AND VISUAL MITIGATION MEASURES	18
TABLE 2.10	MONITORING PROGRAMME FOR LANDSCAPE AND VISUAL	19
TABLE 3.1	MAJOR ACTIVITIES FOR THE NEXT REPORTING PERIOD	23

#### LIST OF FIGURES

FIGURE 1.1	LOCATION OF CONTRACT NO. NL/2017/03 – TUNG CHUNG NEW TOWN EXTENSION – RECLAMATION AND ADVANCE WORKS (CONTRACT 1)
FIGURE 1.2	LOCATION OF CONTRACT NO. NL/2020/02 - TUNG CHUNG NEW TOWN EXTENSION - SALT WATER SUPPLY SYSTEM (CONTRACT 2)
FIGURE 1.3	LOCATION OF CONTRACT NO. NL/2020/03 – TUNG CHUNG NEW TOWN EXTENSION – MAJOR INFRASTRUCTURE WORKS IN TUNG CHUNG EAST (CONTRACT 3)
FIGURE 1.4	LOCATION OF CONTRACT NO. NL/2020/02 – TUNG CHUNG NEW TOWN EXTENSION – TAI HO INTERCHANGE (CONTRACT 7)
FIGURE 2.1	CONSTRUCTION DUST MONITORING STATION LOCATION
FIGURE 2.2	CONSTRUCTION AIRBORNE NOISE MONITORING STATION LOCATION



#### ACRONYMS AND ABREVIATIONS

Acronyms	Description
C&D	Construction and Demolition
САР	Contamination Assessment Plan
CEDD	Civil Engineering and Development Department
CWD	Chinese White Dolphin
DCM	Deep Cement Mixing
DO	Dissolved Oxygen
EIA	Environmental Impact Assessment
EIAO	Environmental Impact Assessment Ordinance
EIS	Ecologically Important Stream
EM&A	Environmental Monitoring and Audit
EP	Environmental Permit
EPD	Environmental Protection Department
ER	Engineer's Representative
ERM	ERM-Hong Kong, Limited
ET	Environmental Team
HVS	High Volume Sampler
IEC	Independent Environmental Checker
PDA	Planned Development Area
PME	Powered Mechanical Equipment
QPME	Quality Powered Mechanical Equipment
RAP	Remediation Action Plan
RR	Remediation Report
RTTM	Real Time Tracking and Monitoring
SS	Suspended Solid
ТСВ	Tung Chung Bay
TCE	Tung Chung East
TCNTE	Tung Chung New Town Extension
TCW	Tung Chung West
The Project	Tung Chung New Town Extension (East)
THW	Tai Ho Wan
TSP	Total Suspended Particulate
Updated EM&A Manual	Updated Environmental Monitoring and Audit Manual for Tung Chung New Town Extension prepared by ERM under Agreement No. CE 60/2017 (EP) and deposited to EPD under Environmental Permit No. EP-519/2016



# EXECUTIVE SUMMARY

Tung Chung New Town Extension (TCNTE) is one of the major initiatives under the Government's multi-pronged approach to increase land supply to meet Hong Kong's mediumto long-term needs for housing, economic and social developments. The Environmental Impact Assessment (EIA) Report for TCNTE (Register No. AEIAR-196/2016) was approved on 8 April 2016 and the Environmental Permit (EP) No. EP-519/2016, covering the construction and operation of TCNTE, was granted on 9 August 2016. The EIA Report and EP cover both Tung Chung East (TCE) and Tung Chung West (TCW). ERM-Hong Kong, Limited (ERM) is commissioned to undertake the role of Environmental Team (ET) for the construction and operation of TCE Project ("the Project") in accordance with the requirements specified in the EP, Updated Environmental Monitoring and Audit (EM&A) Manual, EIA Report of the TCNTE project and other relevant statutory requirements.

The construction of the Contract No. NL/2017/03 - Tung Chung New Town Extension – Reclamation and Advance Works ("Contract 1") at TCE commenced on 9 July 2018.

The construction of the Contract No. NL/2020/02 - Tung Chung New Town Extension – Salt Water Supply System ("Contract 2") at TCE commenced on 4 September 2021.

The construction of the Contract No. NL/2020/03 - Tung Chung New Town Extension – Major Infrastructure Works in Tung Chung East ("Contract 3") at TCE commenced on 5 November 2021.

The construction of the Contract No. NL/2020/07 - Tung Chung New Town Extension – Tai Ho Interchange ("Contract 7") at TCE commenced on 15 March 2022.

This is the Monthly EM&A report presenting the EM&A works carried out during the period from 1 to 31 May 2024 for the TCE Project in accordance with the Updated EM&A Manual.

A summary of monitoring and audit activities conducted in the reporting period is listed below:

Air Quality Monitoring	6 sessions			
Noise Monitoring	6 sessions			
Preserved Plant Species Monitoring	1 session			
Transplanted Plant Species Monitoring	1 session			
Environmental Site Inspection				
Contract 1	4 sessions			
Contract 2	5 sessions			
Contract 3	5 sessions			
Contract 7	4 sessions			
Environmental Management Meeting				
Contract 1	1 session			

•	Contract 2	1 session
•	Contract 3	1 session

Contract 7
 1 session



Environmental auditing works, including weekly site inspections of construction works conducted by the ET, audit of implementation of Complaint Management Plan, Eco-shoreline Implementation Plan, Detailed Preservation and/or Translocation of Plant Species of Conservation Importance, Detailed Compensatory Woodland Planting Plan and Waste Management Plan were conducted in the reporting period. Based on the audit results and the observation for the reporting period, environmental pollution control and mitigation measures for the Project were properly implemented.

# BREACHES OF ACTION AND LIMIT LEVELS FOR AIR QUALITY

No exceedance of Action and Limit Levels was recorded for construction air quality monitoring in the reporting period.

### BREACHES OF ACTION AND LIMIT LEVELS FOR NOISE

No exceedance of Limit Levels was recorded for construction noise monitoring in the reporting period. However, one (1) Action Level was triggered from one (1) environmental complaint related to noise nuisance in the reporting period.

### BREACHES OF ACTION AND LIMIT LEVELS FOR WATER QUALITY

Water quality monitoring was suspended in the reporting period.

#### ECO-SHORELINE MONITORING

The construction of vertical eco-shoreline, mangrove eco-shoreline and rocky eco-shoreline has been substantially completed. Wet season monitoring was conducted during the reporting period.

#### SOFT SHORE ECOLOGICAL MONITORING

No post-construction soft shore ecological monitoring at Tung Chung Bay and Tai Ho Wan was scheduled during the reporting period.

### ENVIRONMENTAL COMPLAINTS, NON-COMPLIANCE & SUMMONS

There was no notification of summons or prosecution recorded in the reporting period.

One (1) environmental complaint related to Contract 1, One (1) environmental complaint related to Contract 2 and two (2) environmental complaints related to Contract 3 were received in the reporting period. Investigations were conducted for the environmental complaints in accordance with the complaint handling process as stated in the Complaint Management Plan.

#### **REPORTING CHANGE**

There was no reporting change in the reporting period.

### KEY ISSUES FOR THE COMING MONTH

Potential environmental impacts arising from the upcoming construction activities in the next reporting period of June 2024 are mainly associated with dust emission, noise from plant operation during normal working hours and restricted hours, handling and storage of C&D



materials generated from construction activities, efficiency of wastewater and drainage management and tree protection. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures. The ET will also recommend to the Contractor about the environmental toolbox topics on the abovementioned key issues for the coming month.



# 1. INTRODUCTION

# 1.1 BACKGROUND

Tung Chung New Town Extension (TCNTE) is one of the major initiatives under the Government's multi-pronged approach to increase land supply to meet Hong Kong's medium-to long-term needs for housing, economic and social developments. The Environmental Impact Assessment (EIA) Report for TCNTE (Register No. AEIAR-196/2016) was approved on 8 April 2016 and the Environmental Permit (EP) No. EP-519/2016, covering the construction and operation of TCNTE, was granted on 9 August 2016. The EIA Report and EP cover both Tung Chung East (TCE) and Tung Chung West (TCW).

ERM-Hong Kong, Limited (ERM) is commissioned to undertake the role of Environmental Team (ET) for the construction and operation of TCE Project ("the Project") in accordance with the requirements specified in the EP, Updated Environmental Monitoring and Audit (EM&A) Manual <sup>(1)</sup>, EIA Report of the TCNTE project <sup>(2)</sup> and other relevant statutory requirements.

The TCNTE comprises the following elements:

- (a) TCE Project
  - Reclamation of the seabed by a non-dredged method at TCE to form a total of about 130 hectares of land;
  - 2. Construction of about 4.9 kilometers of seawalls, with an eco-shoreline, three drainage box culvert outfalls, three circulation drains and a seawater intake at TCE;
  - 3. Provision of infrastructure for Tung Chung Area 58, including construction of a single two-lane road with a footpath and the associated utility works;
  - 4. Construction of proposed open space;
  - Construction of roads, footpaths, cycle tracks and the associated junction / road improvement works;
  - 6. Engineering infrastructure works covering drainage, sewerage, waterworks (including a fresh water service reservoir, a salt water service reservoir and a salt water pumping station), common utility tunnels and landscaping works; and
  - 7. Implementation of environmental mitigation measures and environmental monitoring and audit programme for the works.
- (b) TCW Project
  - 1. Site formation works at TCW;
  - 2. Construction of proposed open space;
  - 3. Construction of the River Park including a visitor centre at TCW; and
  - 4. Construction of sustainable urban drainage systems at TCW.

<sup>(2)</sup> Arup (2015). Environmental Impact Assessment Report for Tung Chung New Town Extension. Deposited to EPD under Register No. AEIAR-196/2016



<sup>&</sup>lt;sup>(1)</sup> ERM (2018a). Updated Environmental Monitoring and Audit Manual for Tung Chung New Town Extension. Deposited to EPD under EP-519/2016

The locations of Contracts 1, 2, 3 and 7 are shown in *Figure 1.1 to 1.4*. The construction and the reclamation related marine works of Contract 1 commenced on 9 and 13 July 2018, respectively. The construction of Contracts 2, 3 and 7 commenced on 4 September 2021, 5 November 2021 and 15 March 2022, respectively.

### 1.2 SCOPE OF THE EM&A REPORT

This is the Monthly EM&A Report for the TCE Project which summarises the key findings of the EM&A programme during the reporting period from 1 to 31 May 2024 for the construction works.

# 1.3 ORGANIZATION STRUCTURE

The organization structure of the Project is shown in *Annex A*. The key personnel contact names and contact details are summarized in *Table 1.1* below.

Party	Position	Name	Telephone				
Environmental Team (ET)	ET Leader	Kelvin So	3894 9504				
(ERM-Hong Kong, Limited)	Deputy ET Leader	Raymond Chow	2271 3281				
Independent Environmental	IEC	Manuel Chua	3894 9807				
Checker (IEC) (Binnies Hong Kong Limited)	Deputy IEC	Edward Lau	3894 9695				
Contract No. NL/2017/03 - Works (Contract 1)	Contract No. NL/2017/03 - Tung Chung New Town Extension – Reclamation and Advance Works (Contract 1)						
Civil Engineering and Development Department	Marine Conservation Officer	Wo King Tai	3894 9707				
Engineer's Representative	Principal Resident Engineer	Frankie Fan	3894 9603				
(ER) (AECOM Asia Company	Chief Resident Engineer	Chris Cheung	3894 9604				
Limited)	Resident Engineer	Victor Chan	3894 9666				
	Senior Inspector of Works	C K Liu	3894 9733				
Contractor	Site Agent	David Wong	9653 8635				
(Build King - SCT Joint Venture)	Civil Division Head	Marco Chan	9257 7033				
Venturey	Environmental Officer	Issac Wong	9873 8968				
	24-hour Complaint Hotline	-	5976 1853				
Contract No. NL/2020/02 - (Contract 2)	Tung Chung New Town Extension	on – Salt Water Sup	oply System				
Civil Engineering and	Senior Engineer	Patrick C Y Yeung	2231 4435				
Development Department	Electrical & Mechanical Engineer	Samson K L Yip	2231 4460				
Engineer's Representative	Principal Resident Engineer	Frankie Fan	3894 9603				
(ER)	Senior Resident Engineer	Sunny Ng	3894 9605				
(AECOM Asia Company Limited)	Senior Resident Engineer	Vincent Leung	3894 9645				
	Resident Engineer	Amen Fung	3894 9676				

#### TABLE 1.1 CONTACT INFORMATION OF KEY PERSONNEL



Contractor

Corporation)

(China Geo-Engineering

Site Agent

Senior Inspector of Works

Construction Team Leader

**Construction Manager** 

**Environmental Officer** 

Wong Ting Yu

Edward Mok

Fung Ka Bao

C K Chung

Ambrose Kwong


3894 9706


6198 7787


6498 4306


5401 5720

9120 1489

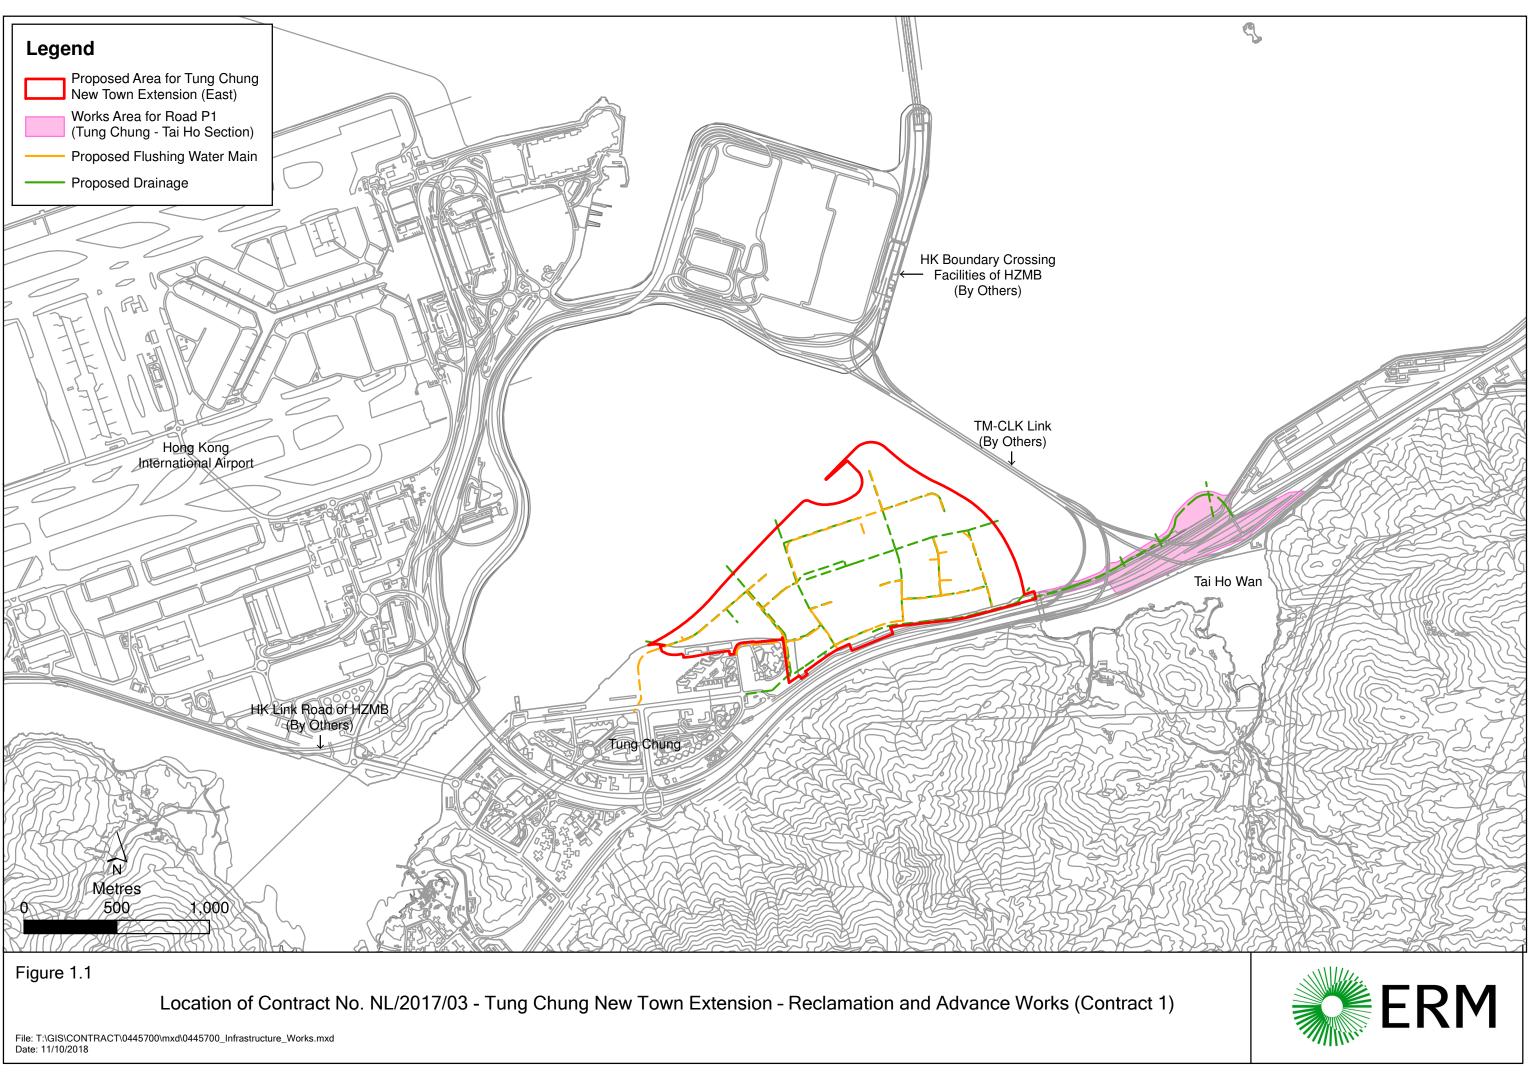

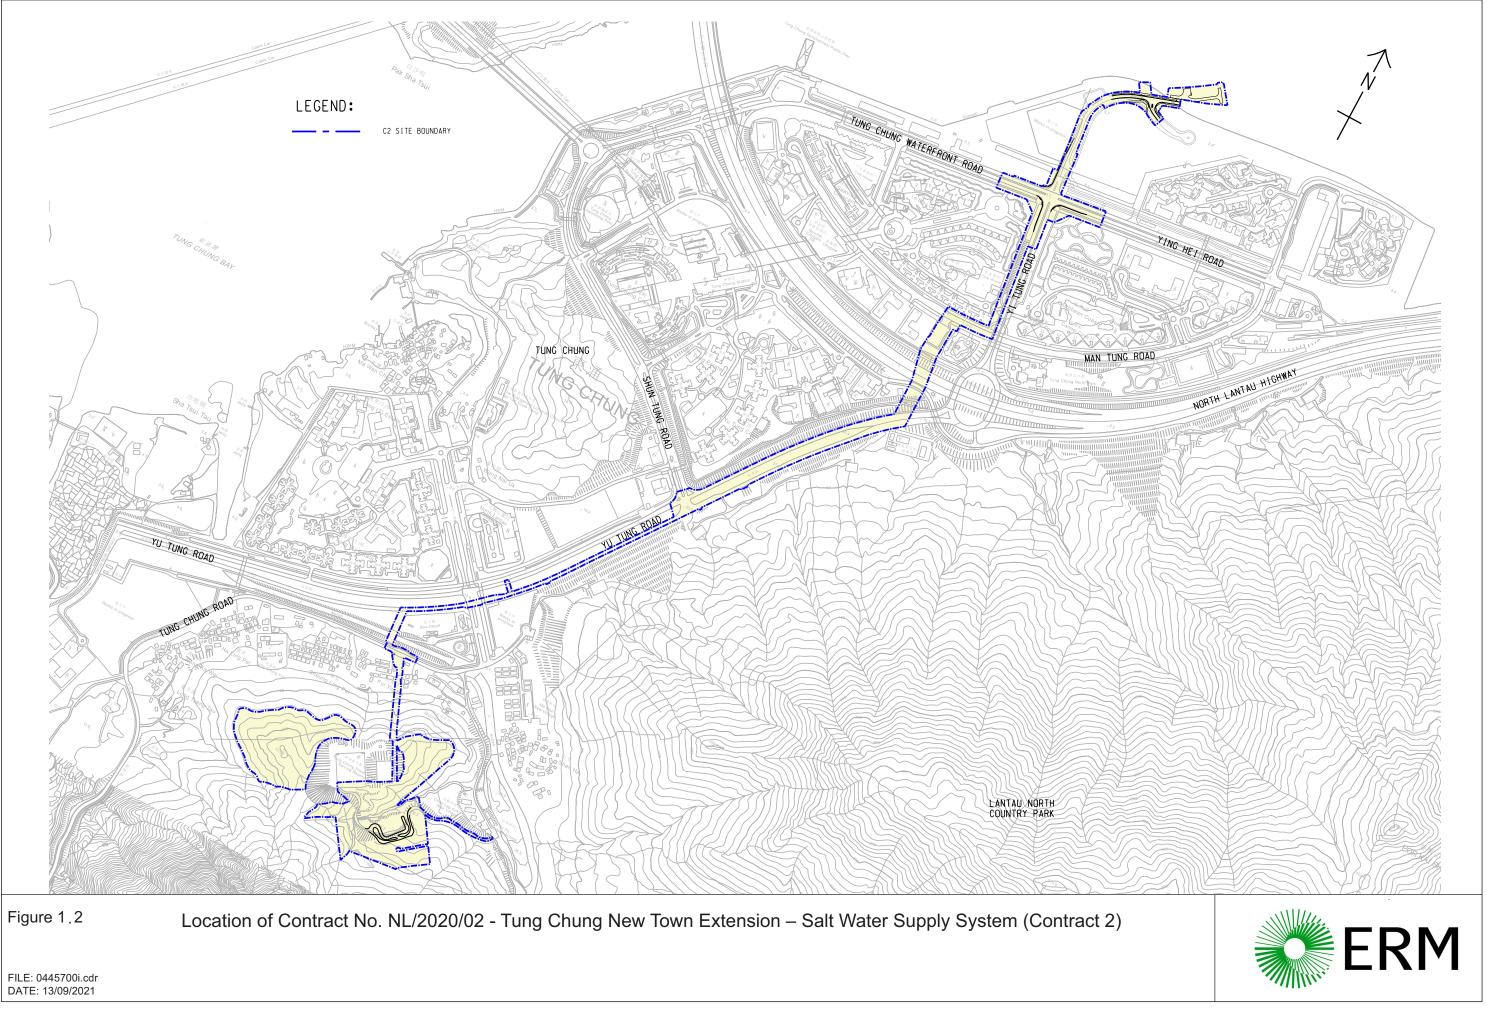

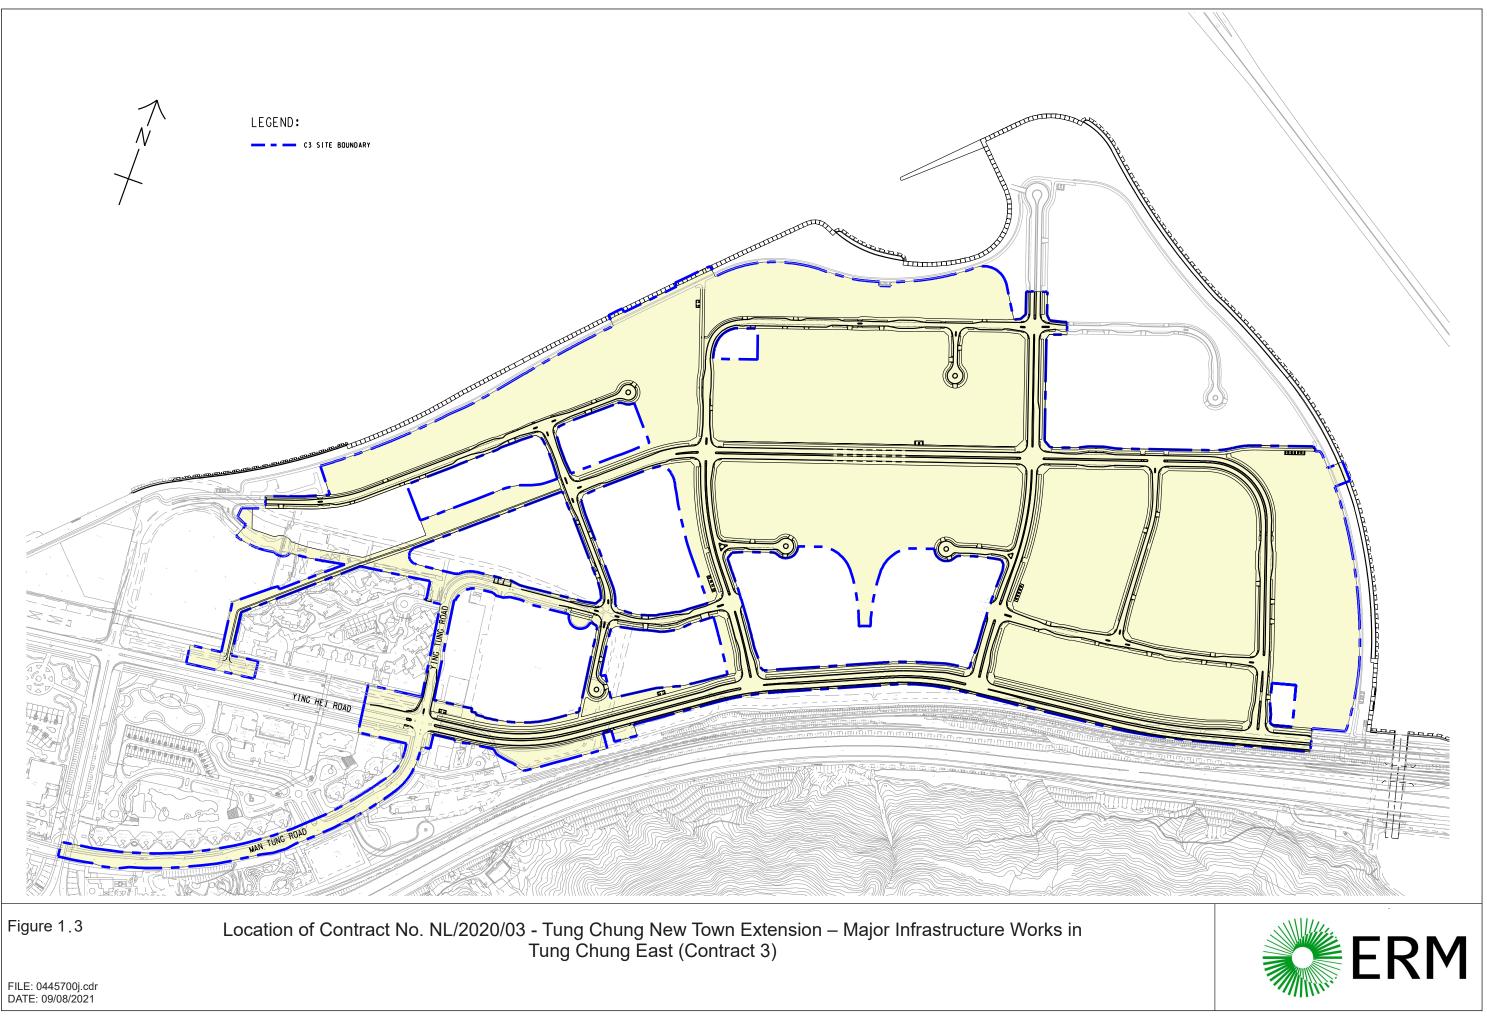

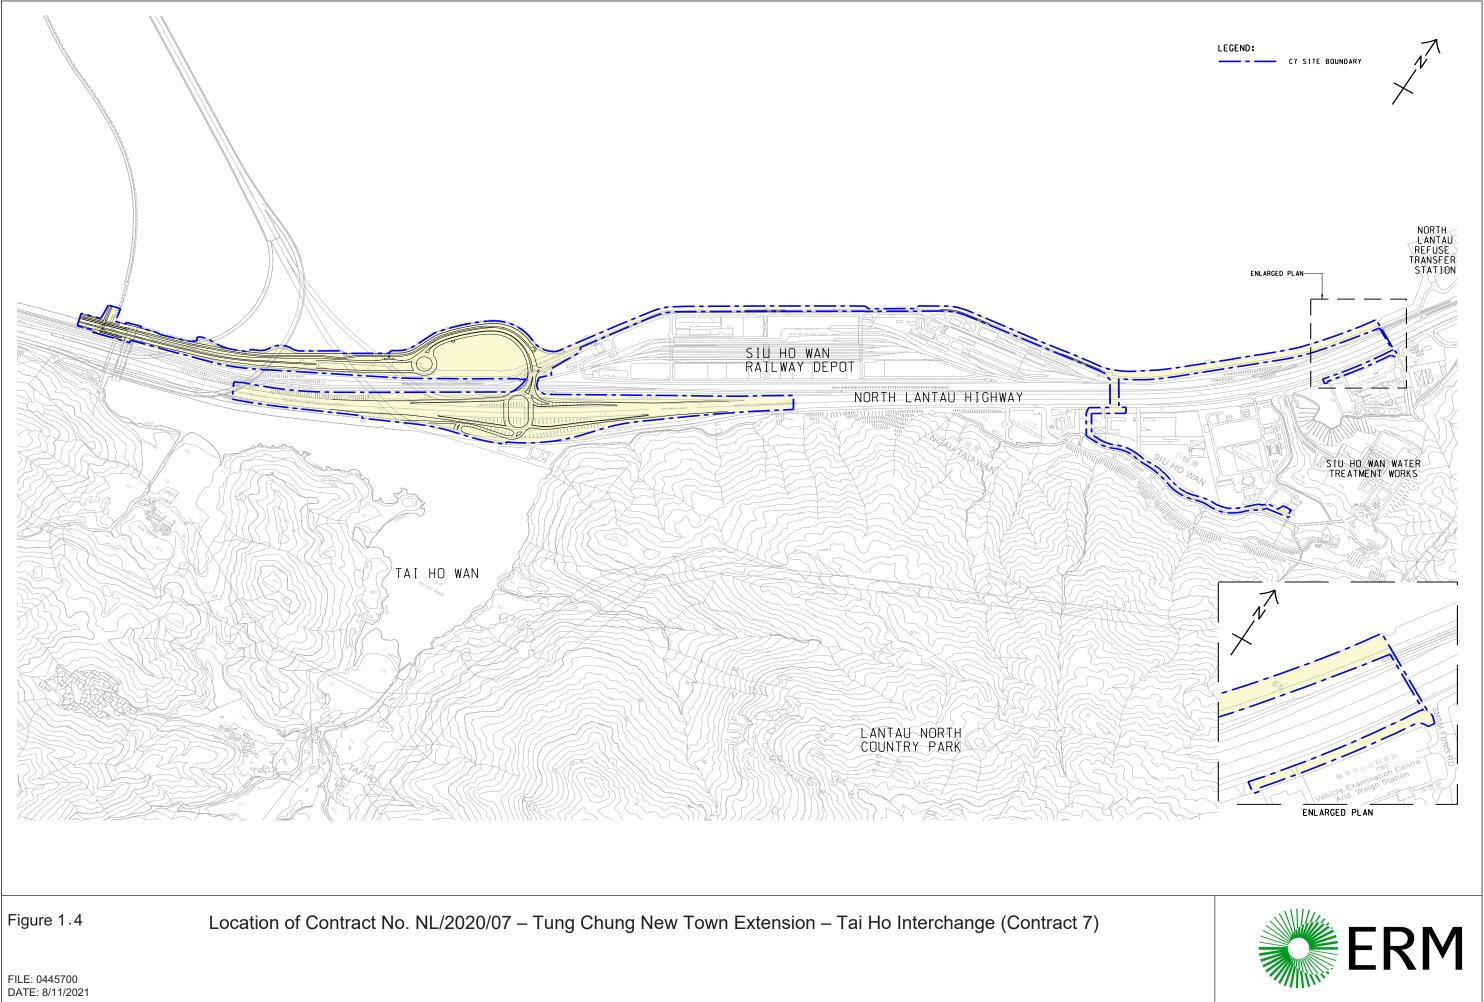

Contract No. NL/2020/03 - Tung Chung New Town Extension - Major InfrastructureWorks in Tung Chung East (Contract 3)Civil Engineering and Development DepartmentSenior EngineerEddie W C Lam2231 4443Senior EngineerPhoebe Tang2231 4447EngineerTimothy H M Chan2231 4473Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerGloria Tang3894 9663Resident EngineerGloria Tang3894 9663Resident EngineerAlvis Li3894 9659Resident EngineerAlvis Li3894 9558Resident EngineerAlvis Li3894 9559Resident EngineerAlvis Li3894 9559Senior Inspector of WorksDouglas Ng3894 9579Senior Inspector of WorksDouglas Ng3894 9579Build King Civil Engineering Limited)Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract 7)Senior Resident EngineerS H Leung2231 4442Civil Engineering and Development DepartmentSenior Resident EngineerFrankie Fan3894 9654Civil Engineering and Development DepartmentSenior Resident EngineerFrankie Fan3894 9654Contract 7)Senior Resident EngineerKlvin Kwan3894 9654Civil Engineering Limited)Senior Resi	Party	Position	Name	Telephone
Works in Tung Chung East (Contract 3)Civil Engineering and Development DepartmentSenior EngineerEddie W C Lam2231 4443Senior EngineerPhoebe Tang2231 4443EngineerTimothy H M Chan2231 4443EngineerColin K C Wong2231 4443Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9643Resident EngineerGloria Tang3894 9643Senior Resident EngineerDavid Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAnson Yip3894 9559Senior Inspector of WorksDouglas Ng3894 9559Schortzatt No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharge (Contract 7)Senior EngineerFinakie FanCivil Engineering and Development DepartmentSenior Resident EngineerFrankie Fan3894 9663Senior Resident EngineerKingsley Ho3894 9556Resident EngineerSenior Resident EngineerFrankie Fan3894 9650Contract 7)Senior Resident EngineerFrankie Fan3894 9653Civil Engineering and Development DepartmentSenior		24-hour Complaint Hotline	-	5976 1853
Civil Engineering and Development DepartmentSenior EngineerEddie W C Lam2231 4445Senior EngineerPhoebe Tang2231 4423EngineerColin K C Wong2231 4417Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9633Senior Resident EngineerDavid Li3894 9639Senior Resident EngineerDavid Li3894 9639Senior Resident EngineerDavid Li3894 9639Senior Resident EngineerDavid Li3894 9639Resident EngineerDavid Li3894 9639Senior Resident EngineerAlvis Li3894 9639Resident EngineerAlvis Li3894 9639Senior Resident EngineerDavid Li3894 9639Resident EngineerAlvis Li3894 9639Senior Inspector of WorksDouglas Ng3894 9559Resident EngineerAlvis Li3894 9559Senior Inspector of WorksDouglas Ng3894 9559Senior Inspector of WorksDouglas Ng3894 9559Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau917 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai HO Intercharter (ER) (AECOM Asia Company Limited)Senior Resident EngineerS H LeungCivil Engineering and Development DepartmentSenior Resident EngineerS H Leung2231 4443	Contract No. NL/2020/03 -	Tung Chung New Town Exten	sion – Major Infrastr	ucture
Development DepartmentSenior EngineerPhoebe Tang2231 4423EngineerTimothy H M Chan2231 4473EngineerColin K C Wong2231 4473Engineer's RepresentativePrincipal Resident EngineerWing Chen3894 9003(ER)Chief Resident EngineerGloria Tang3894 9630(AECOM Asia CompanySenior Resident EngineerDavid Li3894 9650Resident EngineerDavid Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9559Resident EngineerAnson Yip3894 9559Senior Resident EngineerAnson Yip3894 9559Senior Inspector of WorksDouglas Ng3894 9559Senior Inspector of WorksDouglas Ng3894 9579(Build King Civil EngineeringSite AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho IntercharberFrankie FanCivil Engineering and Development DepartmentSenior Resident EngineerS H LeungEngineer's Representative (ER) (AECOM Asia Company Limited)Senior Resident EngineerS H LeungContract or (Build King Civil Engineering Benior Resident EngineerS H Leung3894 9552Senior Resident EngineerKelvin Kwan3894 9655 </td <td>Works in Tung Chung East</td> <td>(Contract 3)</td> <td></td> <td></td>	Works in Tung Chung East	(Contract 3)		
Senior Ingineer Brance Findeber Brance Science	Civil Engineering and	Senior Engineer	Eddie W C Lam	2231 4445
EngineerColin K C Wong2231 4417EngineerWing Chen3894 9704Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Chief Resident EngineerGloria Tang3894 9639Senior Resident EngineerDavid Li3894 9650Resident EngineerDavid Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9559Senior Inspector of WorksDouglas Ng3894 9579Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Construction Team LeaderKen Yau9197 2219Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract 7)Senior EngineerS H Leung2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 44424Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9657Resident EngineerS H Leung2231 4423Senior Resident EngineerS H Leung2231 4449Senior Resident EngineerS H Leung2231 4423Senior Resident EngineerS H Leung2231 4429Engineer's Representative (ER) Limit	Development Department	Senior Engineer	Phoebe Tang	2231 4423
EngineerWing Chen3894 9704Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerGloria Tang3894 9639Senior Resident EngineerDavid Li3894 9650Resident EngineerDavid Li3894 9650Resident EngineerAlvis Li3894 9558Resident EngineerAlvis Li3894 9559Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract 7)Senior EngineerPhoebe Tang2231 4423Civil Engineering and Development DepartmentSenior EngineerFrankie Fan3894 9603Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerSelior Resident EngineerSelion Resident Engineer840 9643Senior Resident EngineerSelion Resident Engineer894 96093894 9558Contract 7)Senior Resident EngineerFrankie Fan3894 9603Civil Engineering AD (AECOM Asia Company Limited)Senior Resident EngineerSelion Resident Engineer894 9604Senior Resident EngineerSenior Resident EngineerSelion Resident Engineer894 9653<		Engineer	Timothy H M Chan	2231 4473
Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603 3894 9639 Senior Resident EngineerGloria Tang3894 9639 3894 9639 Senior Resident EngineerJavid Li3894 9639 3894 9650 Resident EngineerJavid Li3894 9650 3894 9558 Resident EngineerJavid Li3894 9650 3894 9558 Resident EngineerAlvis Li3894 9558 3894 9558 Construction ManagerCheung Siu Lun2272 3680 20722 2015Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange (Contract 7)Senior EngineerFin Lin6390 0018 2211 4423 EngineerCivil Engineering and Development Department (ER) (AECOM Asia Company Limited)Senior EngineerPhoebe Tang Senior Resident EngineerSenior Resident EngineerSenior Resident EngineerSenior Resident EngineerSenior Resident EngineerS894 9651 3894 9654Contractor (Build King Civil Engineering Limited)Senior Inspector of WorksDouglas Ng3894 9554 3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9000 3109 3894 955		Engineer	Colin K C Wong	2231 4417
(EŘ) (AECOM Asia Company Limited)Chief Resident EngineerGloria Tang3894 9639 3894 9650 3894 9650 Resident EngineerLimited)Senior Resident EngineerDavid Li3894 9650 3894 9650 Resident EngineerDavid Li3894 9639 3894 9650 Resident EngineerContractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680 5025 0368 Construction ManagerContractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680 5025 0368 Construction Team LeaderContract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharge (Contract 7)Senior EngineerTim Lin6390 0018 6390 0018 24-hour Complaint HotlineCivil Engineering and Development Department (ER) (AECOM Asia Company Limited)Senior EngineerPhoebe Tang2231 4423 231 231 4423 231 231 4423 231 231 231 233 4331 231 231 231 231 231 231 23		Engineer	Wing Chen	3894 9704
(AECOM Asia Company Limited)Chier Resident EngineerGiona Taily3.994 9639Senior Resident EngineerWinston Wong3894 9640Resident EngineerDavid Li3894 9684Resident EngineerAlvis Li3894 9650Resident EngineerAlvis Li3894 9559Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Deputy Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharge6000Contract 7)Senior EngineerPhoebe Tang2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Senior EngineerFrankie Fan3894 9656Senior Resident EngineerSchior Resident EngineerSenior Resident Engineer3894 9659Senior Inspector of WorksDouglas Ng3894 9556Senior Resident EngineerSchior Kingsley Ho3894 9556Resident EngineerSchior Inspector of WorksDouglas Ng3894 9555Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9000 3109Deputy Site AgentHon	Engineer's Representative	Principal Resident Engineer	Frankie Fan	3894 9603
Limited)Senior Resident EngineerWinston Wong3894 9650Resident EngineerDavid Li3894 9684Resident EngineerAlvis Li3894 9559Resident EngineerAnson Yip3894 9559Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange5976 1853Contract 7)Senior EngineerPhoebe Tang2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9630Senior Resident EngineerKelvin Kwan3894 96558894 9655Resident EngineerScal Yu3894 9650Senior Inspector of WorksDouglas Ng3894 9655Contractor (Build King Civil Engineering Limited)Site AgentKingsley Ho3894 9555Contractor (Build King Civil Engineering Limited)Site AgentVincent Kwan9833 1313Contractor (Build King Civil Engineering Limited)Site AgentVincent Kwan9833 1313Contr		Chief Resident Engineer	Gloria Tang	3894 9639
Resident EngineerAlvis Li3894 9558Resident EngineerAnson Yip3894 9559Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharge2231 4423Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9556Resident EngineerKelvin Kwan3894 95553894 95553894 9555Resident EngineerCarl Yu3894 95553894 9555Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentHon Yee9090 31093894 9555Deputy Site AgentVincent Kwan9833 1313313Contractor (Build King Civil Engineering Limited)Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 92299810 1946	Limited)	Senior Resident Engineer	Winston Wong	3894 9650
Resident EngineerAnson Yip3894 9559Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 -Tung Chung New Town Extension - Tai Ho InterchangeContract 7)Senior EngineerS H Leung2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Senior Resident EngineerFrankie Fan3894 9550Resident EngineerKelvin Kwan3894 95513894 9551Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9556Resident EngineerCarl Yu3894 9552Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Resident Engineer	David Li	3894 9684
Senior Inspector of WorksDouglas Ng3894 9737Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharge (Contract 7)Senior EngineerPhoebe Tang2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 4449Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9556Senior Inspector of WorksDouglas Ng3894 9552Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Resident Engineer	Alvis Li	3894 9558
Contractor (Build King Civil Engineering Limited)Construction ManagerCheung Siu Lun2272 3680Site AgentPaul Lui9095 7922Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange (Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9556Senior Resident EngineerBrian Li3894 9554Senior Inspector of WorksDouglas Ng3894 9554Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Resident Engineer	Anson Yip	3894 9559
(Build King Civil Engineering Limited)Site AgentPaul Lui9095 7922 9025 0368 Construction Team LeaderAldous Lo9225 0368 9225 0368 Construction Team LeaderAldous Lo9225 0368 9225 0368 Construction Team LeaderKen Yau9197 2219 9197 2219 Environmental OfficerTim Lin6390 0018 6390 0018 24-hour Complaint Hotline-5976 1853 5376 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange (Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423 EngineerEngineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603 3894 9552 Resident EngineerContractor (Build King Civil Engineering Limited)Senior Inspector of WorksDouglas Ng3894 9554 3894 9554 Site AgentConstruction Team LeaderVincent Kwan9833 1313 Construction Team LeaderVincent Lo9883 9229 9810 1946		Senior Inspector of Works	Douglas Ng	3894 9737
Limited) Site Agent Paul Lui 9053 7522 Deputy Site Agent Aldous Lo 9225 0368 Construction Team Leader Ken Yau 9197 2219 Environmental Officer Tim Lin 6390 0018 24-hour Complaint Hotline - 5976 1853 Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange (Contract 7) Civil Engineering and Development Department Senior Engineer Phoebe Tang 2231 4443 Engineer S Representative (ER) (AECOM Asia Company Limited) Senior Resident Engineer Kelvin Kwan 3894 9603 Senior Resident Engineer Brian Li 3894 9556 Resident Engineer Carl Yu 3894 9555 Resident Engineer Carl Yu 3894 9555 Senior Inspector of Works Douglas Ng 3894 9554 Site Agent Hon Yee 9090 3109 Deputy Site Agent Vincent Kwan 9833 1313 Construction Team Leader Vincent Lo 9883 9229 Environmental Officer Nash Wong 9810 1946	Contractor	Construction Manager	Cheung Siu Lun	2272 3680
Deputy Site AgentAldous Lo9225 0368Construction Team LeaderKen Yau9197 2219Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Intercharger5976 1853Contract 7)Senior EngineerPhoebe Tang2231 4423Civil Engineering and Development DepartmentSenior EngineerS H Leung2231 4449Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 95563894 95563894 9556Resident EngineerKingsley Ho3894 95523894 9556Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313300Construction Team LeaderVincent Lo9833 92299810 1946		Site Agent	Paul Lui	9095 7922
Environmental OfficerTim Lin6390 001824-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - (Contract 7)Tung Chung New Town Extension - Tai Ho Interchange (Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9552Resident EngineerCarl Yu3894 9552Resident EngineerCarl Yu3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	Linitedy	Deputy Site Agent	Aldous Lo	9225 0368
24-hour Complaint Hotline-5976 1853Contract No. NL/2020/07 - Tung Chung New Town Extension - Tai Ho Interchange(Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9552Resident EngineerKingsley Ho3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 92299810 1946		Construction Team Leader	Ken Yau	9197 2219
Contract No. NL/2020/07 - Tung Chung New Town Extension – Tai Ho Interchange (Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9554Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Environmental Officer	Tim Lin	6390 0018
(Contract 7)Civil Engineering and Development DepartmentSenior EngineerPhoebe Tang2231 4423EngineerS H Leung2231 4449Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerKelvin Kwan3894 9556Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9554Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 92299810 1946		24-hour Complaint Hotline	-	5976 1853
Development DepartmentEngineerS H Leung2231 4449Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	Contract No. NL/2020/07 - (Contract 7)	Tung Chung New Town Exten	sion – Tai Ho Interch	ange
Engineer's Representative (ER) (AECOM Asia Company Limited)Principal Resident EngineerFrankie Fan3894 9603Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor 	Civil Engineering and	Senior Engineer	Phoebe Tang	2231 4423
(ER) (AECOM Asia Company Limited)Senior Resident EngineerKelvin Kwan3894 9641Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	Development Department	Engineer	S H Leung	2231 4449
Senior Resident EngineerRefvir Rwan3894 9041Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	Engineer's Representative	Principal Resident Engineer	Frankie Fan	3894 9603
Limited)Senior Resident EngineerBrian Li3894 9556Resident EngineerKingsley Ho3894 9552Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	(ER)	Senior Resident Engineer	Kelvin Kwan	3894 9641
Resident EngineerCarl Yu3894 9671Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946	Limited)	Senior Resident Engineer	Brian Li	3894 9556
Senior Inspector of WorksDouglas Ng3894 9554Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Resident Engineer	Kingsley Ho	3894 9552
Contractor (Build King Civil Engineering Limited)Site AgentHon Yee9090 3109Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Resident Engineer	Carl Yu	3894 9671
(Build King Civil Engineering Limited)Deputy Site AgentVincent Kwan9833 1313Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Senior Inspector of Works	Douglas Ng	3894 9554
Limited) Construction Team Leader Vincent Kwall 9853 1313 Environmental Officer Nash Wong 9810 1946	Contractor	Site Agent	Hon Yee	9090 3109
Construction Team LeaderVincent Lo9883 9229Environmental OfficerNash Wong9810 1946		Deputy Site Agent	Vincent Kwan	9833 1313
	Linited)	Construction Team Leader	Vincent Lo	9883 9229
24-hour Complaint Hotline - 5976 1853		Environmental Officer	Nash Wong	9810 1946
		24-hour Complaint Hotline	-	5976 1853



### 1.4 SUMMARY OF CONSTRUCTION WORKS

As informed by the Contractor, details of the major works carried out in this reporting period are listed below:

#### TABLE 1.2 MAJOR ACTIVITIES IN THE REPORTING PERIOD

Activities	Key Issues	Key Mitigation Measures
Contract No. NL/2017/03 - Tung Chung New	7 Town Extension – Reclamation and Advance W	orks (Contract 1)
Land-based Works		
<ul> <li>Box culvert construction</li> <li>Installation of navigation light at VS2</li> <li>Installation of security gate and fence at Seawater Intake</li> <li>Reinstatement at Berth No. 1</li> </ul>	<ul> <li>Dust emission</li> <li>Handling and storage of C&amp;D materials generated from construction activities</li> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> <li>Potential surface runoff</li> <li>Noise from plant operation during normal working hours or restricted hours</li> <li>Dust emission during storage and transfer of sand/ sorted public fill</li> </ul>	<ul> <li>Good site practices</li> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far a practicable</li> <li>Use of QPME and noise barrier/acoustic materials</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Strictly follow requirement under CNP for the use of PMEs and works within restricted period</li> <li>Use of acoustic mat and other noise mitigation measures when necessary</li> <li>Regular maintenance of engines and mechanical equipment</li> </ul>

#### Contract No. NL/2020/02 - Tung Chung New Town Extension – Salt Water Supply System (Contract 2)

#### Land-based Works

•	Construction of pumping station at Portion 6	Dust emission	Good site practices
•	Construction of service reservoir and TMF mainlaying at Portion 3	<ul> <li>Handling and storage of C&amp;D materials generated from construction activities</li> </ul>	<ul> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> </ul>
•	CLP cable duct laying works at Wong Lung Hang at Portion 3	<ul><li>Noise from plant operation</li><li>Emission of dark smoke from PMEs</li></ul>	<ul> <li>Provide tarpaulin sheets coverage on stockpiles</li> </ul>



<ul> <li>Yan Road, Man Tung Road, Yu Tung Road Planter, Tung Chung Road and inside WSD facilities</li> <li>Watermain laying works at Yi Tung Road at Portion 4</li> <li>Tree protection</li> <li>Tree protection</li> <li>Regular maintenance of PMEs</li> </ul>	Activities	Key Issues	Key Mitigation Measures
	<ul> <li>Yan Road, Man Tung Road, Yu Tung Road Planter, Tung Chung Road and inside WSD facilities</li> <li>Watermain laying works at Yi Tung Road at Portion 4</li> <li>Manhole construction and pipe laying for</li> </ul>	management	<ul> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Retain and protect all existing trees and vegetation within the study area which are</li> </ul>

#### Land-based Works

• Excavation and ELS works at Portion 104	Dust emission	Good site practices
<ul> <li>Excavation and ELS works at CUT no.1, 2, 3, 4 and supporting building</li> </ul>	<ul> <li>Handling and storage of C&amp;D materials generated from construction activities</li> </ul>	<ul> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> </ul>
<ul> <li>and supporting building</li> <li>Construction works for CUT no. 1 structure</li> <li>Back-filling works for CUT 2</li> <li>Construction works and furniture installation of PM office at WA9</li> <li>Construction works of Contractor office at WA6</li> <li>Drainage, Sewerage and watermain works at Road L4, L3, L5, L8, L9 and Portion 16</li> <li>DCS works at Road L4 and L3.</li> <li>Pipe laying works for twin rising mains/ watermain laying at Man Tung Road</li> <li>Preparation and pipe jacking works at Ying Tung Road</li> <li>Foundation and backfilling works for noise barrier at Portion 11</li> <li>Road and drainage works in Road P1</li> <li>Road D4, Road L7, ELS installation</li> </ul>	<ul> <li>generated from construction activities</li> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> </ul>	<ul> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far as practicable</li> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> </ul>



Activities	Key Issues	Key Mitigation Measures
• Excavation and ELS works at Portion 104		
Contract No. NL/2020/07 - Tung Chung New Tow	vn Extension – Tai Ho Interchange (Contra	ct 7)
<ul> <li>Land-based Works</li> <li>Open cut excavation and pipe laying for rising main and watermain at Portion 146-1 to 146-14</li> <li>Pak Mong bridge I-beam erection set up</li> <li>Trench excavation pipe laying works at Portions 32 (Sham Shui Kok Drive), Portion 34 Phase 2, and Portion 38</li> <li>excavation and pipe laying works at Portion 32 (Access Road adjacent to MTRC Siu Ho Wan Depot)</li> <li>Backfilling at Portion 33</li> <li>Establishment of pipe jacking works at Portion 32 for</li> </ul>	<ul> <li>Dust emission</li> <li>Handling and storage of C&amp;D materials generated from construction activities</li> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> <li>Tree protection</li> </ul>	<ul> <li>ct 7)</li> <li>Good site practices</li> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far as practicable</li> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Retain and protect all existing trees and vegetation within the study area which are</li> </ul>
<ul> <li>Receiving pit</li> <li>RC construction of retaining walls FR1</li> <li>RC works for Pak Mong Subway Extension Phase 1</li> <li>ELS at Casting Yard A1 and A2</li> <li>Bored piles at A1a and A2b</li> <li>ELS at RW-R6, U1, U2 and U3 RC works for RW-R2, RW-R3 and RW-R4 at Portion 146-2 to 146-4</li> <li>RC construction at RW-R7</li> <li>Mini-piles at Wall E and Wall D</li> <li>GI works for open space at Portions 147-1 &amp;2</li> <li>Bored piles at Bridge C Portion 146-12</li> <li>Site clearance and tidiness</li> </ul>		not directly affected by the works

The environmental mitigation implementation schedule is presented in *Annex B*.



# 1.5 SUMMARY OF EM&A PROGRAMME REQUIREMENTS

The status for all environmental aspects is presented in *Table 1.3*. The EM&A requirements remained unchanged during the reporting period.

# TABLE 1.3 SUMMARY OF STATUS FOR THE ENVIRONMENTAL ASPECTS UNDER THE UPDATED EM&A MANUAL

Parameters	Status
Air Quality	
Baseline Monitoring	The results of baseline air quality monitoring for TCE were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Impact Monitoring	On-going for TCE, monitoring conducted three times every six days
Noise	
Baseline Monitoring	The results of baseline noise monitoring for TCE were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Impact Monitoring	On-going for TCE, monitoring conducted once per week
Impact Monitoring for Road Traffic Noise during Operational Phase	To be conducted during operational phase
Fixed Noise Commissioning Test	To be implemented by the Contractor before operation of TCNTE
Water Quality	
Baseline Monitoring	The results of baseline water quality monitoring for TCE were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Impact Monitoring	Suspended for TCE with approval from EPD
Waste Management	
Waste Monitoring	On-going
Land Contamination	
Contamination Assessment Plan (CAP), Remediation Action Plan (RAP) and Remediation Report (RR)	To be conducted under TCW. Refer to the EM&A Reports of TCW.
Ecology	
Monitoring for Compensation Woodland	Compensation Woodland Planting was completed on 30 September 2022 On-going, monitoring conducted quarterly
Monitoring for Emergent Plant inside the future River Park	To be conducted under TCW. Refer to the EM&A Reports of TCW.
Monitoring for Translocated Amphibians of Conservation Importance	To be conducted under TCW. Refer to the EM&A Reports of TCW.
Monitoring for Preserved/Transplanted Plant Species of Conservation Importance	On-going, for preserved plant species, monitoring conducted once per month; for transplanted plant species, replacement planting was carried out on 28 April 2023 and 19 September 2023, and monitoring conducted once per month for the first year



Parameters	Status
Monitoring for Tung Chung Stream EIS and Wong Lung Hang EIS	To be conducted under TCW. Refer to the EM&A Reports of TCW. Monitoring for Wong Lung Hang was not required and the proposal was accepted by EPD on 2 September 2021
Eco-shoreline Monitoring	The dry season monitoring between December 2023 and February 2024 was completed. Wet season monitoring was in progress.
Tung Chung Bay and Tai Ho Wan Baseline Monitoring	The results of baseline soft shore ecological monitoring at Tung Chung Bay and Tai Ho Wan were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Tung Chung Bay and Tai Ho Wan Impact Monitoring	Completed
Tung Chung Bay and Tai Ho Wan Post- construction Monitoring	On-going for TCE, monitoring conducted quarterly
Landscape and Visual	
Baseline Monitoring	The results of baseline landscape and visual monitoring were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Impact Monitoring	On-going
Site Environmental Audit	
Regular Site Inspection	On-going
Dolphin Watching Plan implementation measures	Completed
Works Vessel Travel Route Plan implementation measures	Completed
Silt Curtain Deployment Plan implementation measures	All silt curtain was removed in accordance with the Silt Curtain Deployment Plan and after obtaining the acceptance from EPD
Spill Response Plan implementation measures	Completed
Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance implementation measures	Under implementation by the Contractor of Contract 2
Detailed Compensatory Woodland Planting Plan implementation measures	Under implementation by the Contractor of Contract 2
Waste Management Plan implementation measures	Under implementation by the Contractor of Contract 1, 2, 3 and 7
	Under implementation by the Contractor of
Complaint Hotline and Email Channel	Contract 1, 2, 3 and 7

Taking into account the construction works, impact monitoring of air quality, noise and waste management were carried out in the reporting period. The monitoring schedule of air quality and noise are provided in *Annex E2* and *Annex F2* respectively.

The EM&A programme also involved environmental site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report and relevant EP submissions, including Complaint Management Plan, Eco-shoreline Implementation Plan, Detailed Preservation and/or



Translocation Plan for Plant Species of Conservation Importance, Detailed Compensatory Woodland Planting Plan and Waste Management Plan.

To promote the environmental awareness and enhance the environmental performance of the contractors, environmental trainings and regular environmental management meetings were conducted during the reporting period, which are summarized as below:

- Four (4) environmental management committee meetings were held among the relevant contractors, ER, ET, IEC and CEDD on 23 and 22 May 2024 (for Contracts 1 and 2) and 14 May 2024 (for Contracts 3 and 7);
- Environmental toolbox trainings on waste management and disposal, chemical handling, dust control, mosquito control, nuisance to residence (light pollution/ sudden noise/ dusty work), site hygiene (rubbish, mosquito, rodent control), noise control, use of spill kits, site drainage management on 3, 8, 10, 14, 17, 22, 24, 29 and 31 May 2024 were conducted for Contract 1;
- Environmental toolbox trainings on site plant and machinery (operation and maintenance), breaking, drilling, cutting and polishing on 7 and 14 May 2024 were conducted for Contract 2;
- Environmental toolbox trainings on plant and machinery environmental precaustion, energy saving, site tideness for anti-mosquitos, tree protection, construction dust and suppression, construction noise and suppression, wastewater handling, discharge and treatment facilities, chemical waste and handling of chemical spillage, anti-mosquito control measures on 2, 7, 9, 14, 16, 21, 23, 28 and 30 May 2024 were conducted for Contract 3;
- Environmental toolbox trainings on cement debagging and mixing, milling, paving, plastering and painting, fixing/ fixture and glazing installation on 2, 8, 16, 22 and 29 May 2024 were conducted for Contract 7.

# 1.6 STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE ENVIRONMENTAL PERMIT

The status of statutory environmental compliance with the EP conditions under the EIAO, submission status under the EP and implementation status of mitigation measures are presented in *Annex C*.

# 1.7 STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS

The environmental licenses and permits, including environmental permit, discharge license under Water Pollution Control Ordinance, registration as chemical waste producer, construction noise permit and specified processes license, which were valid in the reporting period are presented in *Annex D*. No non-compliance with environmental statutory requirements was recorded.



# 2. EM&A RESULTS FOR TUNG CHUNG EAST

# 2.1 AIR QUALITY

### 2.1.1 MONITORING REQUIREMENTS AND EQUIPMENT

According to the Updated EM&A Manual of the Project, impact air quality monitoring in terms of 1-hour Total Suspended Particulate (TSP) was conducted three (3) times every six (6) days when the highest dust impact was expected. The Action and Limit Levels of the air quality monitoring is provided in *Table 2.1* below.

#### TABLE 2.1 ACTION AND LIMIT LEVELS FOR 1-HOUR TSP

Location	Action Level (µg/m³)	Limit Level (µg/m³)
Monitoring station for Tung Chung East	279	500

Portable direct reading dust meters were used to measure 1-hour TSP levels in undertaking the air quality monitoring for the Project. The proposed use of portable direct reading dust meters was submitted to IEC and obtained agreement from the IEC as stated in Section 5.5 of the Updated EM&A Manual. With the use of direct reading dust meter, it can allow prompt and direct results for the EM&A reporting and the implementation of the event and action plan. The portable direct reading dust meter would be calibrated every year against High Volume Sampler (HVS) to check the validity and accuracy of the results measured by direct reading method.

The monitoring location and equipment used in the impact air quality monitoring programme are summarized in *Table 2.2* and illustrated in *Figure 2.1*. Copies of the calibration certificates for the equipment are presented in *Annex E1*, which showed that the portable direct reading dust meter is capable of providing comparable results with that provided by a HVS.

#### TABLE 2.2 AIR QUALITY MONITORING DETAILS

Monitoring Station	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
DM-1	Tung Chung Area 56 – Ying Tung Estate	1-hour TSP	Three times per six days during the construction period of the Project	2, 8, 14, 20, 25 and 31 May 2024	1-hour TSP Dust Meter SIBATA LD-3B (S/N: 436553)

Note: It should be noted that impact monitoring at other construction dust monitoring locations at TCE as stated in the Updated EM&A Manual will commence after the flat intake (for Monitoring Stations DM-2, DM-3 and DM-4).


#### 2.1.2 MONITORING SCHEDULE FOR THE REPORTING MONTH

The schedule for air quality monitoring during the reporting period is provided in Annex E2.

### 2.1.3 RESULTS AND OBSERVATIONS

The monitoring results for 1-hour TSP are summarized in *Table 2.3*. The monitoring data and the graphical presentation are provided in *Annex E3*.



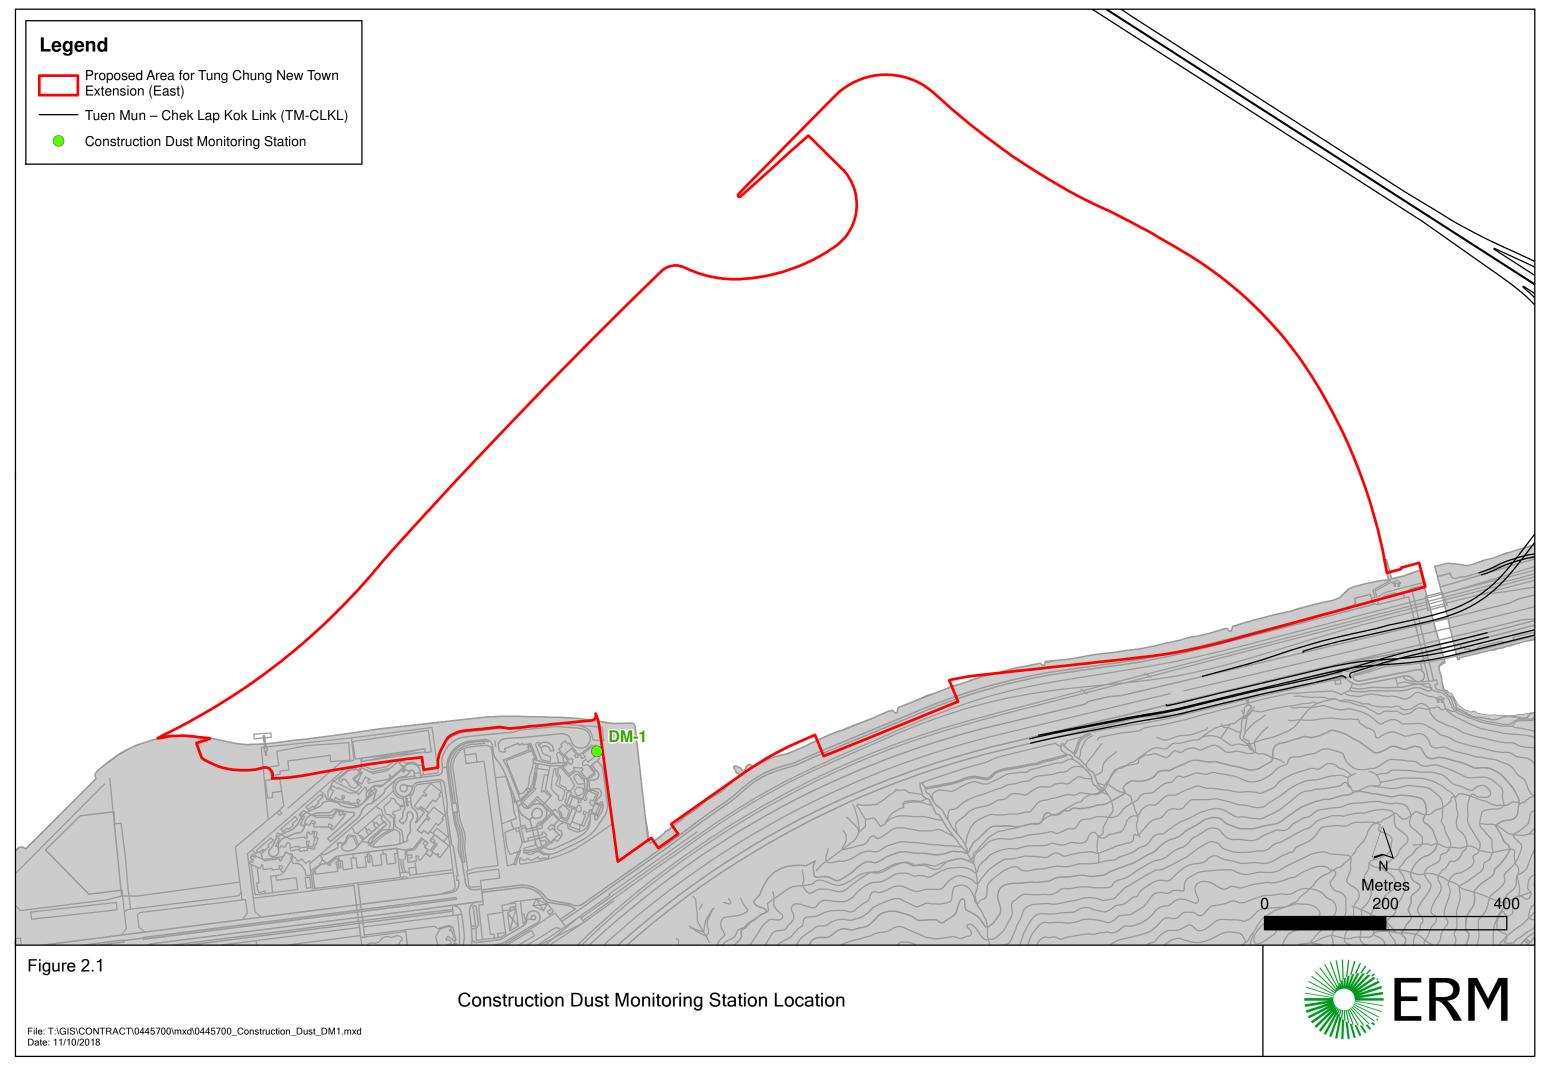

#### TABLE 2.3 SUMMARY OF 1-HOUR TSP MONITORING RESULTS IN THE REPORTING PERIOD

Monitoring	Average	Range (µg/m³)	Action Level	Limit Level
Station	(µg/m <sup>3</sup> )		(µg/m <sup>3</sup> )	(µg/m³)
DM-1	50	37-62	279	500

Major dust sources in the reporting period included haul road traffic and excavation under the Project.

No exceedance of Action and Limit Levels was recorded for construction air quality monitoring in the reporting period. No action was thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex E4*.

# 2.2 NOISE MONITORING

### 2.2.1 MONITORING REQUIREMENTS AND EQUIPMENT

According to the Updated EM&A Manual of the Project, impact noise monitoring was conducted once per week during the construction phase of the Project. The Action and Limit Level for construction noise of the Project is provided in *Table 2.4* below.

#### TABLE 2.4 ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE

Time Period	Action Level	Limit Level
0700 - 1900 hours on normal weekdays	When one documented complaint is received	75 dB(A) <sup>a, b</sup>

Note:

- a Limit level is exceeded when Leq  $\geq$  75 dB(A). If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.
- b Reduce to 70 dB (A) for schools and 65 dB (A) during school examination periods.

Noise monitoring was performed using sound level meter at the designated monitoring stations NMS-CA-1A <sup>(3) (4)</sup> and NMS-CA-4 (*Figure 2.2; Table 2.5*) in accordance with the requirements stipulated in the Updated EM&A Manual. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Details of the deployed equipment are provided in *Table 2.5*. Copies of the calibration certificates for the equipment are presented in *Annex F1*.


#### TABLE 2.5 NOISE MONITORING DETAILS

Monitoring Station <sup>a</sup>	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
NMS-CA-1A <sup>b</sup>	Residential premise in Tung Chung East – Century Link/Ying Hong Road <sup>c</sup>	30-minute measurement between 0700 and 1900 on normal	Once per week for 30 mins during the construction	2, 8, 14, 20, 25 and 31 May 2024	Sound Level Meter: Rion NL-52 (S/N: 00331806)

<sup>&</sup>lt;sup>(3)</sup> Impact monitoring at monitoring station NMS-CA-1A commenced on 19 September 2018 in view of the close vicinity of the construction works near the residential area at Century Link.

<sup>&</sup>lt;sup>(4)</sup> Due to land handover issue, NMS-CA-1A was relocated to Ying Hong Road which is located 60m away from the original location. Proposal on the relocation of NMS-CA-1A was approved by IEC on 23 November 2018. Noise monitoring at the relocated location commenced since 24 November 2018.



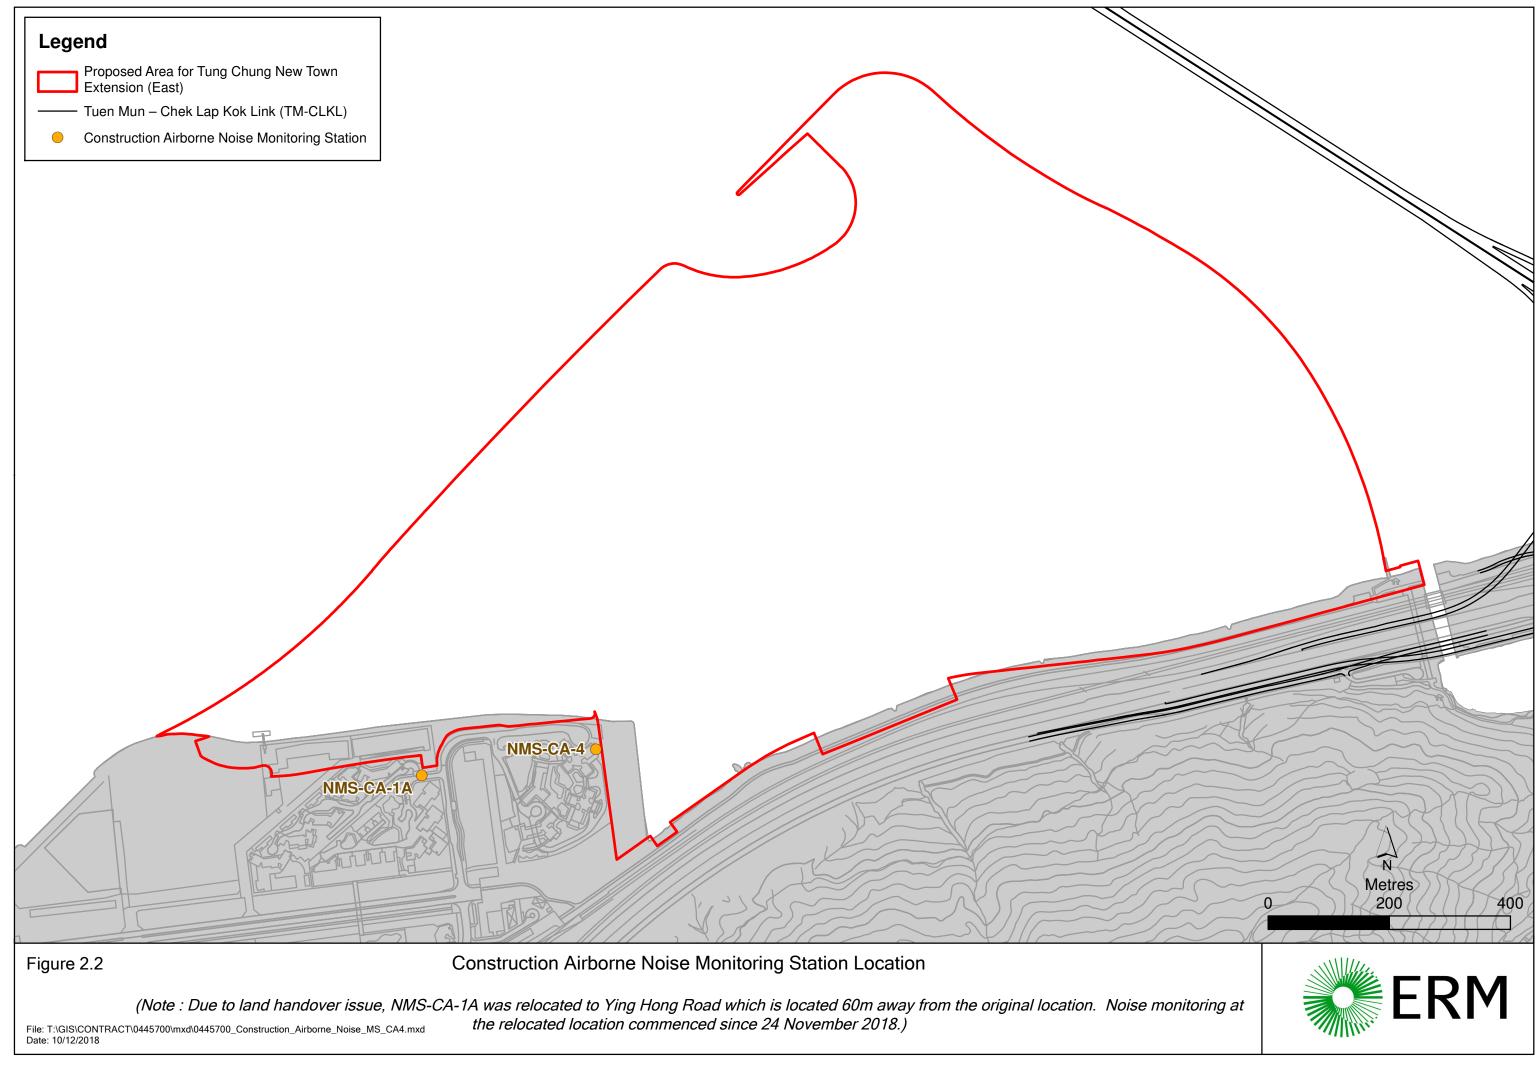

Monitoring Station <sup>a</sup>	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
NMS-CA-4	Residential premise in the reclamation area next to Tung Chung East – Ying Tung Estate	weekdays (Monday to Saturday). $L_{eq}$ , $L_{10}$ and $L_{90}$ would be recorded.	period of the Project		Acoustic Calibrator: LARSON DAVIS CAL200 (S/N: 16172)

Note:

- a It should be noted that impact monitoring at other construction noise monitoring locations at TCE as stated in the Updated EM&A Manual will commence after the flat intake of residential premise in TCE (for Monitoring Station NMS-CA-1) and operation of schools (for Monitoring Stations NMS-CA-2 and NMS-CA-3).
- b Impact monitoring at monitoring station NMS-CA-1A commenced on 19 September 2018 in view of the close vicinity of the construction works near the residential area at Century Link.
- c Due to land handover issue, NMS-CA-1A was relocated to Ying Hong Road which is located 60m away from the original location. Proposal on the relocation of NMS-CA-1A was approved by IEC on 23 November 2018. Noise monitoring at the relocated location commenced since 24 November 2018.

#### 2.2.2 MONITORING SCHEDULE FOR THE REPORTING MONTH

The schedule for noise monitoring during the reporting period is provided in *Annex F2*.

#### 2.2.3 RESULTS AND OBSERVATIONS

Results for noise monitoring are summarized in *Table 2.6*. The monitoring data and the graphical presentation are provided in *Annex F3*.

# TABLE 2.6 SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS IN THE REPORTING PERIOD

Monitoring Station	Average, dB(A), L <sub>eq (30mins)</sub>	Range, dB(A), L <sub>eq (30mins)</sub>	Limit Level, dB(A), L <sub>eq (30mins)</sub>
NMS-CA-1A	66.6	65.0-67.6	75
NMS-CA-4	69.1	66.7-71.2	75

Major noise sources during the noise monitoring included noise from plant operation, craning, piling, haul road traffic, nearby traffic and aircraft as well as nearby construction sites.

No Limit Level exceedance was recorded for construction noise monitoring in the reporting period. However, one (1) Action Level was triggered from one (1) environmental complaint related to noise nuisance in the reporting period. Investigation was conducted for the complaint in accordance with the Event and Action Plan (*Annex F4*) and the details are provided in Section 2.13.

# 2.3 WATER QUALITY MONITORING

No monitoring event for impact water quality monitoring was conducted at all designated monitoring stations during the reporting period. Water quality monitoring has been suspended since 3 October 2023 as all reclamation works and marine construction activities have been completed.



# 2.4 COMPENSATION WOODLAND MONITORING

Compensation woodland planting under Contract 2 was completed on 30 September 2022. With the approval from EPD on the monitoring proposal in August 2023, quarterly postplanting monitoring for compensation woodland was commenced in September 2023. No compensation woodland monitoring was carried out in the reporting month. Photographic record of the compensation woodland planting is provided in *Annex G*.

# 2.5 PRESERVED/TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE MONITORING

Plant species of conservation importance, including three individuals of *Aquilaria sinensis* and 33 individuals of *Gmelina chinensis*, were identified within works areas for Contract 2 during the survey conducted in August 2021. All individuals of *Aquilaria sinensis* and 31 individuals of *Gmelina chinensis* were recommended being preserved *in-situ* while two individuals of *Gmelina chinensis* (RT-07 and RT-08) were recommended being transplanted to the receptor site in accordance with the Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance approved under Condition 2.21 of EP-519/2016.

Initial tree survey was conducted in September 2021 under Contract No. NL/2020/02 before the commencement of construction works. According to the initial tree survey conducted, the *in-situ* preserved plant species of conservation importance of which one individual of *Aquilaria sinensis* and six individuals of *Gmelina chinensis* were found missing.

During the monthly monitoring of the *in-situ* preserved plant species of conservation importance in November 2023, one individual of *Aquilaria sinensis* and one individual of *Enkianthus quinqueflorus* were newly observed and recommended being preserved *in-situ*. Registration and measurement for two additional trees were conducted on 4 December 2023.

# 2.5.1 PRESERVED PLANT SPECIES OF CONSERVATION IMPORTANCE

Monthly monitoring of the *in-situ* preserved plant species of conservation importance by the Qualified Personnel (QP) appointed under Contract 2 was implemented in the reporting period. Health condition was considered fair for the majority of the *in-situ* preserved plant species of conservation importance, of which two individuals of *Gmelina chinensis* could not be monitored as a result of unsafe access to the locations, as recorded during the monitoring carried out on 23 May 2024.

Tree protection zones for the *in-situ* preserved plant species of conservation importance were demarcated. No injuries and/or damages to the individuals of the *in-situ* preserved plant species of conservation importance were reported by the QP since the previous monitoring events. Photographic record and tree schedule of the preserved plant species of conservation importance monitoring are provided in *Annex H1*.

The ET will continue to monitor the implementation of monitoring of *in-situ* preserved plant species of conservation importance.

### 2.5.2 TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE

Site visit to the receptor site for the transplanted plant species of conservation importance under Contract 2 was carried out on 20 January 2022 prior to the commencement of



transplantation works for the transplanted plant species of conservation importance on 21 January 2022.

The transplanted plant species of conservation importance were both certified as dead trees by the QP on 15 June 2022 as no living signs were observed. Replacement planting of new trees of the same species, or other species to the satisfaction of the Project Manager, at the Contractors' expense would be deemed necessary in accordance with the conditions under the approved Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance. Replacement planting of three (3) *Aquilaria sinensis* were completed on 28 April 2023. One (1) individual was certified dead by the QP as no living signs were observed on 26 July 2023. The removal of the dead tree and replanting of one (1) individual of *Aquilaria sinensis* were completed on 19 September 2023.

The establishment period of two (2) individuals of *Aquilaria sinensis* was ended on 27 April 2024 and quarterly monitoring will be commenced in July 2024.

Monthly monitoring of the replacement planting of one (1) individual *Aquilaria sinensis* was carried out on 23 May 2024 and it was in fair health condition. Photographic record and tree schedule of *Aquilaria sinensis* monitoring are provided in *Annex H2*.

The transplanted plant species of conservation importance were watered twice a week during the establishment period to keep the soil moist except in days with heavy rainfall. The ET will continue to monitor the implementation of monitoring of in-situ preserved/ transplanted plant species of conservation importance.

# 2.6 ECO-SHORELINE MONITORING

The construction of vertical eco-shoreline, mangrove eco-shoreline and rocky eco-shoreline has been substantially completed. Photographic record is provided in *Annex I*.

Monitoring of different types of eco-shorelines was conducted on 6, 8, 9 and 10 May 2024. Monitoring is conducted for at least 3 years after the completion of eco-shoreline, twice in wet season and twice in dry season. Monitoring of ichthyoplankton was conducted on 29 May 2024 while monitoring of juvenile fish was conducted on 22 and 23 May 2024. Monitoring is conducted on a monthly basis covering May to August for at least 3 years, in order to determine the effectiveness of the eco-shoreline in accordance with the Updated EM&A Manual and Eco-shoreline Implementation Plan.

# 2.7 SOFT SHORE ECOLOGICAL MONITORING

No post-construction soft shore ecological monitoring at Tung Chung Bay and Tai Ho Wan was scheduled during the reporting period. The post-construction soft shore ecological monitoring at Tung Chung Bay and Tai Ho Wan was scheduled to be conducted in June 2024 in accordance with the Updated EM&A Manual.

# 2.8 EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis with the Contractor and ER to monitor the implementation of proper environmental pollution control and mitigation measures for air quality, noise, water quality, waste management, marine ecology, landscape and visual impacts and preservation and/or transplantation of plant species of conservation importance under the Project. In the reporting period, four (4) site inspections were carried out on 9, 17, 23 and 29



May 2024 for Contract 1, five (5) site inspections were carried out on 2, 8, 14, 22 and 29 May 2024 for Contract 2, five (5) site inspections were carried out on 3, 10, 14, 24 and 31 May 2024 for Contract 3 and four (4) site inspections were carried out on 7, 14, 21 and 28 May 2024 for Contract 7.

Key observations during the site inspections are summarized in Table 2.7.

# TABLE 2.7 KEY OBSERVATIONS IDENTIFIED DURING THE SITE INSPECTION IN THIS REPORTING MONTH

Contract No.	Inspection Date	Environmental Observations	<b>Recommendations/ Remarks</b>
Contract 1	9 and 17 May 2024	C1 Site Office • No deficiency was observed.	• Nil.
	23 May 2024	Interim Open Rectangular Channel (IORC) • No deficiency was observed.	• Nil.
	29 May 2024	Tung Chung Reclamation Area •Parts of green mesh covering surcharge slope were fallen.	<ul> <li>Tung Chung Reclamation Area</li> <li>The Contractor was reminded to rectify and cover the surcharge slope properly.</li> </ul>
Contract 2	2 May 2024	<ul><li>Portion 3</li><li>Soil exposure was observed.</li></ul>	<ul> <li>Portion 3</li> <li>The Contractor was reminded to properly cover up the exposed soil and prevent potential muddy runoff from slopes during rainy season.</li> </ul>
	8 May 2024	<ul> <li>Portion 6</li> <li>Chemical containers were observed placing on the ground.</li> </ul>	<ul> <li>Portion 6</li> <li>Contractor was reminded to provide drip tray for chemicals.</li> </ul>
	14 May 2024	<ul> <li>TTA</li> <li>Chemical containers were observed placing on the ground.</li> </ul>	<ul> <li>TTA</li> <li>Contractor was reminded to provide drip tray for chemicals.</li> </ul>
		<ul> <li>Portion 3</li> <li>Proper and outstanding record was not observed on the wastewater treatment system tank checklist.</li> </ul>	<ul> <li>Portion 3</li> <li>The Contractor was reminded to provide proper checking and record on the wastewater treatment system tank checklist.</li> </ul>
	22 May 2024	<ul> <li>Portion 3</li> <li>Deficiency of site drainage system was observed.</li> </ul>	<ul> <li>Portion 3</li> <li>The Contractor was reminded to provide measures to prevent polluted runoff from entering nearby water bodies.</li> </ul>
		<ul> <li>Portion 6</li> <li>Chemical containers were observed placing on the ground.</li> </ul>	<ul> <li>Portion 6</li> <li>Contractor was reminded to provide drip tray for chemicals.</li> </ul>
	29 May 2024	<ul><li>Portion 3</li><li>Drainage blockage was observed.</li></ul>	<ul> <li>Portion 3</li> <li>The Contractor was reminded to clear the debris and keep the drainage system clean.</li> </ul>



Contract No.	Inspection Date	Environmental Observations	<b>Recommendations/ Remarks</b>		
		<ul> <li>Portion 6</li> <li>Chemical containers were observed placing on the ground</li> </ul>	<ul> <li>Portion 6</li> <li>Contractor was reminded to provide drip tray for chemicals.</li> </ul>		
Contract 3	3 May 2024	<ul><li>Portion 104</li><li>General refuse was scattered on the ground.</li></ul>	<ul> <li>Portion 104</li> <li>The Contractor was reminded to clear the refuse and maintain good housekeeping.</li> </ul>		
	10 May 2024	Portion 7. 10, 16b, 104 • No deficiency was observed	• Nil.		
	14 May 2024	<ul> <li>Portion 10</li> <li>Proper and outstanding record was not observed on the wastewater treatment system tank checklist.</li> </ul>	<ul> <li>Portion 10</li> <li>The Contractor was reminded to provide proper checking and record on the wastewater treatment system tank checklist.</li> </ul>		
	24 May 2024	CUT • General refuse was scattered on the ground. CUT	<ul> <li>CUT</li> <li>The Contractor was reminded to clear the refuse and maintain good housekeeping. CUT</li> </ul>		
		<ul> <li>Road L8</li> <li>Chemical container was observed placing on the ground.</li> </ul>	<ul> <li>Road L8</li> <li>The Contractor was reminded to provide drip tray for chemical to avoid spillage.</li> </ul>		
	31 May 2024	<ul><li>Portion 10, 16b, 104</li><li>No deficiency was observed</li></ul>	• Nil.		
Contract 7	7 May 2024	<ul> <li>Portion 32</li> <li>Appropriate Non- Road Mobile Machinery (NRMM) label was not observed on generator.</li> </ul>	<ul> <li>Portion 32</li> <li>The Contractor was reminded to affix appropriate NRMM labels in accordance with the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation.</li> </ul>		
	14 May 2024	<ul><li>Area E</li><li>Dry and dusty haul road was observed.</li></ul>	<ul> <li>Area E</li> <li>The Contractor was reminded to provide adequate dust mitigation measures, such as watering.</li> </ul>		
	21 May 2024	WA1 • No deficiency was observed.	• Nil.		
	28 May 2024	<ul> <li>Portion 32</li> <li>Appropriate Non- Road Mobile Machinery (NRMM) label was not observed on generator.</li> </ul>	<ul> <li>Portion 32</li> <li>The Contractor was reminded to affix appropriate NRMM labels in accordance with the Air Pollution Control (Non- Road Mobile Machinery) (Emission) Regulation.</li> </ul>		

The Contractors have rectified all of the observations identified during environmental site inspections in the reporting period. The Contractors were reminded to implement all relevant



mitigation measures related to construction dust, construction noise, water quality and waste management outlined in the EIA Report and Updated EM&A Manual.

# 2.9 WASTE MANAGEMENT STATUS

The Contractors of Contract 1, 2, 3 and 7 have registered as chemical waste producer. Sufficient numbers of receptacles were available for general refuse collection and sorting.

All dump trucks engaged on site was equipped with RTTM system during the reporting period. The Surveillance Team of the ET conducted regular site inspection on the dump trucks and their track records. No illegal dumping and landfilling of C&D materials was found during the reporting period.

Wastes generated during this reporting period include mainly non-inert construction wastes. Reference has been made to the waste flow tables prepared by the Contractors. The quantities of different types of wastes and imported fill materials are summarised in *Table 2.8.* 

# TABLE 2.8 QUANTITIES OF DIFFERENT WASTE GENERATED AND IMPORTED FILL MATERIALS

Contract No.	Month/ Year	Inert C&D Materials ª (m³)	Imported Fill <sup>b</sup> (sand) (m <sup>3</sup> )	Imported Fill <sup>c</sup> (public fill) (m <sup>3</sup> )	Inert Construction Waste Re- used <sup>d</sup> (m <sup>3</sup> )	Non-inert Constructi on Waste <sup>e</sup> (m <sup>3</sup> )	Recyclable Materials <sup>f</sup> (kg)	Chemical Wastes (kg)
TCNTE (East)	1 to 31 Mar 24	0.0	0.0	0.0	0.0	298.0	0.0	0.0
	1 to 30 Apr 24	0.0	0.0	0.0	0.0	238.3	0.0	0.0
	1 to 31 May 24	0.0	0.0	0.0	0.0	401.2	0.0	0.0

Note:

- a Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill.
- b Imported materials include of sand fill from any source outside of TCNTE.
- c Imported sorted public fill include all G200, G400 and glass gullet (local recycling materials) from any source outside of TCNTE.
- d Reuse of inert construction waste generated under the TCNTE contracts.
- e Non-inert construction wastes include general refuse disposed at landfill.
- f Recyclable materials include metals, paper, cardboard, plastics and others.

# 2.10 LANDSCAPE AND VISUAL MONITORING

Implementation of applicable landscape and visual mitigation measures was monitored in accordance with the Updated EM&A Manual. All measures undertaken by the Contractor during the construction phase and establishment work phase shall be audited by ET to ensure compliance with the intended aims of the measures.

The implementation status of the environmental protection measures is summarized below in *Table 2.9*. Examples of landscape and visual mitigation measures are presented in *Annex J1*. The monitoring programme for detailed design, construction and establishment stages is presented in *Table 2.10*. Event and Action Plan for Landscape and Visual impacts is stated in *Annex J2*.



Landscape and Visual Mitigation Measures during Construction	Implementation Status	Relevant Contract(s) in the Reporting Period		
MM1 – Optimization of Construction Areas & Providing Temporary Landscape on Temporary Construction	Implementation of the measures were carried out during the detailed design stage of the Project.	NA		
MM2 – Minimize Topographical Changes	Implementation of the measures were carried out during the detailed design stage of the Project.	NA		
MM3 – Preservation of Potentially Registerable OVTs,	Tree Protection Specifications were provided in the relevant Contract Specifications respectively for implementation by the Contractors under the Project.	All works contracts		
Rare and Protective Vegetation	Contractors submitted Detailed Preservation and/or Translocation Plan for Plant cies of Conservation Importance under EP condition 2.21.			
	The Contractors' performance on the implementation of the tree maintenance and protection measures were observed and checked by the ET weekly during construction period.			
MM4 – Transplanting of Existing Trees	Tree Transplanting Specifications were provided in the relevant Contract Specifications respectively for implementation by the Contractors under the Project where trees would unavoidably be affected by the construction works.	Contract 2		
	The Contractors submitted Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance under EP condition 2.21.			
	The transplanted plant species of conservation importance were both certified as dead trees by the QP on 15 June 2022 as no living signs were observed.			
MM5 – Screen Hoarding	The implementation of mitigation measures was checked by ET during weekly site inspection. Implementation of the measures by Contractors was observed.	All works contracts		
MM6 – Adopting Non-dredge Method for the Reclamation	Not applicable during the reporting period.	NA		
MM9 – Providing Natural Rock Material/ Planting for Artificial Seawall	Rock armour reused and construction of eco-shoreline (mangrove eco-shoreline, rocky eco-shoreline and vertical eco-shoreline) in progress. The implementation of mitigation measures was checked by ET during weekly site inspection. Implementation of the measures by Contractors was observed.	Contract 1		

#### TABLE 2.9 IMPLEMENTATION STATUS OF LANDSCAPE AND VISUAL MITIGATION MEASURES



Landscape and Visual Mitigation Measures during Construction	Implementation Status	Relevant Contract(s) in the Reporting Period
MM10 – Compensatory Planting	Not applicable during the reporting period.	NA
MM11 – Woodland Restoration	The implementation of mitigation measures was checked by ET during weekly site inspection. Implementation of the measures by Contractors was observed.	Contract 2
MM12 – Screen Planting	Not applicable during the reporting period.	NA
MM13 - Roadside Planting	Not applicable during the reporting period.	NA
MM14 – Aesthetic Design of Built Development	Not applicable during the reporting period.	NA
MM15 – Maximise Greening on Structures	Not applicable during the reporting period.	NA
MM16 – Noise Barrier Design	Not applicable during the reporting period.	NA
MM18 – Landscaping on Slopes	Not applicable during the reporting period.	NA
MM20 – Lighting Control	The implementation of mitigation measures was checked by ET during weekly site inspection. Implementation of the measures by Contractors was observed.	All works contracts

## TABLE 2.10 MONITORING PROGRAMME FOR LANDSCAPE AND VISUAL

Stage	Monitoring Task	Monitoring Report	Form of Approval	Frequency
Design	Monitoring of design works against the recommendations of the landscape and visual impact assessments within the EIA should be undertaken by the Engineer and Landscape Architect, to ensure that they fulfil the intentions of the mitigation measures. Any changes to the design, including design changes on site should also be checked	Report by CEDD / ER confirming that the design conforms to requirements of EP.	Approval by Project Proponent	At completion o design stage
Construction	Monitoring of the contractor's operations during the construction period.	Report on Contractor's compliance by ET	Counter-signature of report by IEC	Monthly
Establishment Works	Monitoring of the planting works during the 24-months Establishment Period after completion of the construction works.	Report on Contractor's compliance by ET	Counter-signature of report by IEC	Bi-monthly



# 2.11 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

A summary of the Environmental Mitigation Implementation Schedule is presented in *Annex B*. The necessary mitigation measures were implemented properly for the Project.

# 2.12 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

There was no notification of summons or prosecution recorded in the reporting period.

One (1) environmental complaint related to Contract 1, One (1) environmental complaint related to Contract 2 and Two (2) environmental complaints related to Contract 3. Investigations were conducted for the environmental complaints in accordance with the complaint handling process as stated in the Complaint Management Plan. Environmental complaints in the reporting period are summarized below.

	Complaint(s)	Investigation/Follow up action(s)
1	Environmental complaint related to Contract 1 regarding noise and dust nuisance from the demolition site next to the Visionary Town No. 3 was recorded on 10 May 2024 and referred by EPD on 13 May 2024.	Based on the information provided by the Contractor, demolition of Contract 1 site office was carried out at the concerned area. With confirmation from RSS, it is stated that all works were conducted within non- restricted hours and no breaking was conducted during demolition work to minimize noise generated. Hydraulic crasher was used as an alternative. Continuous water spraying was applied and temporary dust screen was erected along the site boundary to minimize dust nuisance. Nevertheless, the Contractor confirm that moveable noise barrier will be erected during demolition of transformer room in next stage to reduce noise generated from concrete breaking.
2	Environmental complaint related to Contract 3 regarding noise near the MTRC Traction Station at Man Tung Road was referred by EPD on 16 May 2024.	Based on the information provided by the Contractor, emergency work was conducted for road subsidence. The Contractor submitted an Emergency Work Record during restricted hours to EPD on 3 May 2024. A joint site inspection between Contractor and EPD was conducted on 10 May 2024 and no further comment was received. The complaint case was also reported to HKPF and the authority acknowledged the needs for restricted hours of emergency work in view of public safety on 3 May 2024. No further comment was received after record checking. Since the complaint case was due to emergency work for repairing the public work regarding the safety issue, no follow-up action was required.
3	Environmental complaint related to Contract 2 regarding noise near Ling Liang Church Sau Tak Primary School at Man Tung Road was referred by EPD on 16 May 2024.	Based on the information provided by the Contractor with confirmation from RSS, no construction work at the concerned area was conducted during restricted hours. Nevertheless, the Contractor had implemented noise mitigation measures such as wrapping sound insulation materials around breaker tip and erected noise barrier along site boundary to minimize noise nuisance.
4	Environmental complaint related to Contract 3 regarding dust at Ying Hei	Based on the information provided by the Contractor with confirmation by RSS, water trucks and road



Complaint(s)	Investigation/Follow up action(s)		
Road (South) was referred by EPD on 24 May 2024.	sweepers have been deployed to clean Ying Hei Road (between Ying Tung Road and Yi Tung Road) for dust control. Wheel washing facilities were also installed and operated at the exit gate of TCE reclamation area for a thorough cleanse of car wheel before leaving the site. The dirt mentioned was likely caused by wear and tear of road pavement. Nevertheless, the Contractor would review the effectiveness of the mitigation measures and introduce enhancement as necessary.		

Statistics on complaints, notifications of summons, successful prosecutions are summarised in *Annex K*.



## 3. FUTURE KEY ISSUES

## 3.1 CONSTRUCTION PROGRAMME FOR THE COMING MONTH

Works to be undertaken in the next monitoring period of June 2024 are summarized in *Table 3.1* below, together with the key issues and the key mitigation measures:



## TABLE 3.1 MAJOR ACTIVITIES FOR THE NEXT REPORTING PERIOD

Activities	Key Issues	Key Mitigation Measures					
Contract No. NL/2017/03 - Tung Chung New Town Extension – Reclamation and Advance Works (Contract 1)							
Land-based Works							
<ul> <li>Defect correction work at Seawall and Box Culvert.</li> <li>Installation of security gate and fence at Seawater Intake</li> <li>Reinstatement at Berth No. 1</li> </ul>	<ul> <li>Dust emission</li> <li>Handling and storage of C&amp;D materials generated from construction activities</li> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> <li>Potential surface runoff</li> <li>Noise from plant operation during normal working hours or restricted hours</li> <li>Dust emission during storage and transfer of sand/ sorted public fill</li> </ul>	<ul> <li>Good site practices</li> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far as practicable</li> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Strictly follow requirement under CNP for the use of PMEs and works within restricted period</li> <li>Use of acoustic mat and other noise mitigation measures when necessary</li> <li>Regular maintenance of engines and mechanical equipment</li> </ul>					

Contract No. NL/2020/02 - Tung Chung New Town Extension – Salt Water Supply System (Contract 2)

#### Land-based Works

<ul> <li>Construction of pumping station at Portion 6</li> <li>Construction of service reservoir and TMF mainlaying at Portion 3</li> </ul>	<ul> <li>Dust emission</li> <li>Handling and storage of C&amp;D materials generated from construction activities</li> </ul>	<ul> <li>Good site practices</li> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> </ul>
<ul> <li>CLP cable duct laying works at Wong Lung Hang at Portion 3</li> <li>Watermain laying works at Portion 3 along Chung Yan Road, Man Tung Road, Yu Tung</li> </ul>	<ul> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> </ul>	<ul> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far as practicable</li> </ul>



Activities	Key Issues	Key Mitigation Measures
<ul> <li>Road Planter, Tung Chung Road and inside WSD facilities</li> <li>Watermain laying works at Yi Tung Road at Portion 4</li> <li>Manhole construction and pipe laying for drainage works at Portion 5A</li> </ul>	Tree protection	<ul> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Retain and protect all existing trees and vegetation within the study area which are not directly affected by the works</li> </ul>

Contract No. NL/2020/03 - Tung Chung New Town Extension – Major Infrastructure Works in Tung Chung East (Contract 3)

#### Land-based Works



Activities	Key Issues	Key Mitigation Measures					
Contract No. NL/2020/07 - Tung Chung New Town Extension – Tai Ho Interchange (Contract 7)							
Land-based Works							
<ul> <li>Open cut excavation, backfilling and pipe laying for rising main and watermain at Portion 146-1 to 146-14</li> <li>Laying subbase and asphalt for temporary haul road along 146-1 to 146- 14</li> <li>Pak Mong bridge I-beam erection set up</li> <li>Trench excavation and pipe laying works at Portions 32 (Sham Shui Kok Drive) and Portion 38</li> <li>Trench excavation and pipe laying works at Portion 32 (Access Road adjacent to MTRC Siu Ho Wan Depot)</li> <li>Backfilling at Portion 33 and 34</li> <li>Establishment of pipe jacking works at Portion 33</li> <li>ELS and grout curtain at Portion 32 for Receiving pit</li> <li>RC construction of retaining walls FR1</li> <li>RC works for Pak Mong Subway Extension Phase 1</li> <li>Preparation works for falsework at casting yard A1 and A2</li> <li>ELS at A1a and A2b</li> <li>RC for RW-R2, RW-R3 and RW-R4 at Portion 146-2 to 146-4</li> <li>RC construction at RW-R7 at Portion 31</li> <li>Pile Load test and Mini-piles at Wall E</li> <li>Predrill works at Wall D</li> </ul>	<ul> <li>Dust emission</li> <li>Handling and storage of C&amp;D materials generated from construction activities</li> <li>Noise from plant operation</li> <li>Emission of dark smoke from PMEs</li> <li>Efficiency of wastewater and drainage management</li> <li>Tree protection</li> </ul>	<ul> <li>Good site practices</li> <li>Regular water spraying on stockpiles, unpaved haul road and land filling area</li> <li>Provide tarpaulin sheets coverage on stockpiles</li> <li>Sorting and reuse of C&amp;D materials as far as practicable</li> <li>Use of QPME and noise barrier/acoustic mat</li> <li>Regular maintenance of PMEs</li> <li>Implementation of wastewater and drainage management</li> <li>Retain and protect all existing trees and vegetation within the study area which are not directly affected by the works</li> </ul>					

• Bored piles at Bridge C Portion 146-12

Activities	Key Issues	Key Mitigation Measures
<ul> <li>U channel and chain link fence construction at Portion 147-1 and 147-2</li> <li>Site clearance and tidiness</li> </ul>		



The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures. The ET will also recommend to the Contractors about the environmental toolbox topics on the abovementioned key issues for the next reporting period.

## 3.2 MONITORING SCHEDULE FOR THE COMING MONTH

The tentative schedules for environmental monitoring in June 2024 are provided in Annex L.



## 4. CONCLUSION AND RECOMMENDATION

This EM&A Report presents the findings of the EM&A activities undertaken for the TCE Project during the period from 1 to 31 May 2024 in accordance with the Updated EM&A Manual and the requirements of the Environmental Permit (*EP-519/2016*).

Air quality (1-hour TSP), noise, eco-shoreline, in-situ preserved plant species of conservation importance and transplanted plant species of conservation importance were carried out in the reporting period.

The monitoring results for air quality monitoring (1-hour TSP) complied with the Action/ Limit levels in the reporting period.

No exceedance of Limit Level was recorded for construction noise monitoring in the reporting period. However, one (1) Action Level was triggered from one (1) environmental complaint related to noise nuisance in the reporting period.

Water quality monitoring was suspended in the reporting period.

Mangrove eco-shoreline, rocky eco-shoreline and vertical eco-shoreline were completed. Wet season monitoring was conducted during the reporting period.

No post-construction soft shore ecological monitoring at Tung Chung Bay and Tai Ho Wan was scheduled during the reporting period.

No compensation woodland monitoring was carried out in the reporting month.

Monitoring of the *in-situ* preserved plant species of conservation importance and monitoring of the transplanted plant species of conservation importance were carried out in the reporting period.

Environmental site inspections were carried out during the reporting period. Recommendations on remedial actions were given to the Contractors for the deficiencies identified during the site inspections.


There were no notification of summons or prosecution recorded in the reporting period. One (1) environmental complaint related to Contract 1, one (1) environmental complaint related to Contract 2 and two (2) environmental complaints related to Contract 3. Investigations were conducted for the environmental complaint in accordance with the complaint handling process as stated in the Complaint Management Plan.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.





## ANNEX A PROJECT ORGANISATION

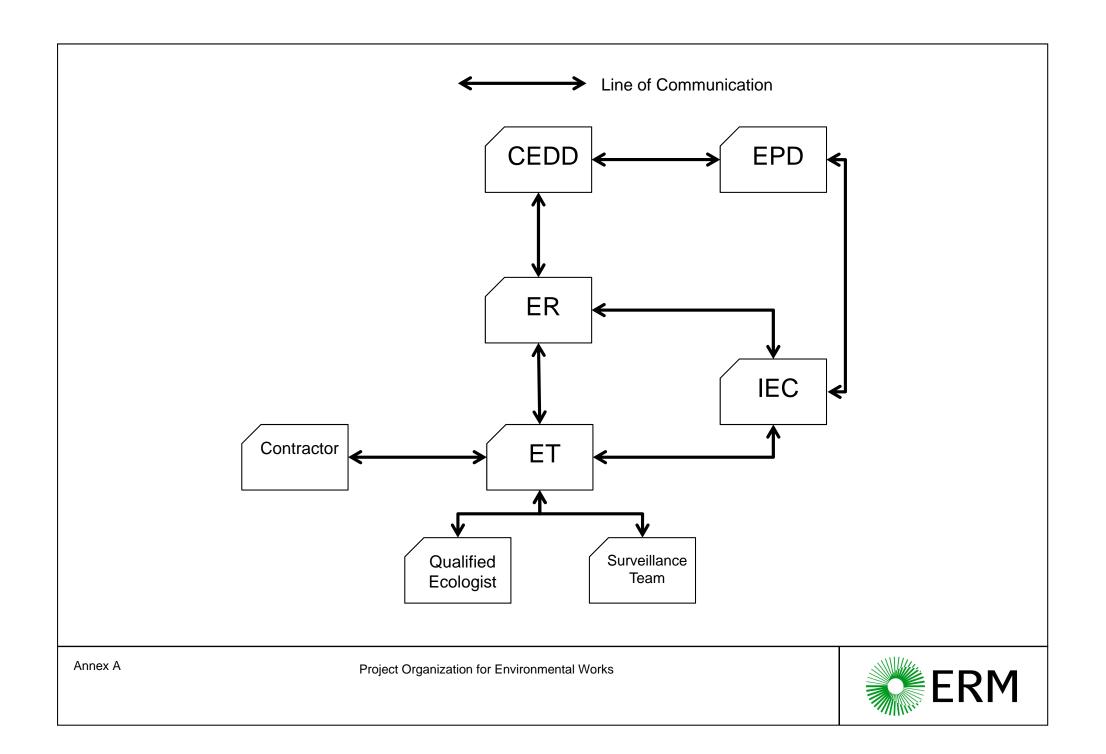



## ANNEX B

# ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

Note: Chapters 1 to 2 of the EIA report present the background information of the Project, identified concurrent projects, objectives and scope for various environmental aspects, and description on alternative options and construction description. Chapters 3 to 12 of the EIA report present the EIA findings and mitigation measures are described below with cross-reference to the EIA report. Chapters 13 to 15 describe the environmental monitoring requirements, summary of environmental outcomes and conclusion.

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	
Common	ommon Mitigation Measures (Applicable to ALL Project Components, including DPs and Non-DPs)							
Construc	tion Dust In	npact						
S3.4.6	D1	Water spraying every hour on exposed worksites and haul road.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	<ul> <li>APCO</li> <li>To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>	
S3.4.6	D2	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	<ul> <li>APCO</li> <li>To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>	
\$3.4.6	D3	<ul> <li>The following dust suppression measures should be incorporated to control the dust nuisance throughout the construction phase:</li> <li>Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;</li> <li>Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;</li> </ul>	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	<ul> <li>APCO</li> <li>To control the dust impact to meet HKAQO and TM-EIAO criteria</li> </ul>	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	ObjectivesoftheRecommendedMeasures&MainConcerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		• A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones;					
		• The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;					
		• Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;					
		• When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;					
		• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;					
		• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;					
		• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;					
		• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens,					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;					
		• Any skip hoist for material transport should be totally enclosed by impervious sheeting;					
		• Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;					
		• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;					
		• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and					
		• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.					
\$3.4.6	D4	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected dust monitoring stations	Construction stage	• TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Construc	tion Noise						
S4.3.4	N1	<ul> <li>Implement the following good site management practices:</li> <li>only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme;</li> <li>machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;</li> <li>silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works;</li> <li>mobile plant should be sited as far away from NSRs as possible and practicable;</li> <li>material stockpiles, site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.</li> </ul>	Control construction airborne noise	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO
S4.3.4	N2	Use of quiet plant which should be made reference to the Powered Mechanical Equipment (PME) listed in the Technical Memorandum or the Quality Powered Mechanical Equipment (QPME) / other commonly used PME listed in Environmental Protection Department (EPD) web pages as far as possible which includes the Sound Power Level (SWLs) for specific quiet PME.	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO
S4.3.4	N3	Install movable temporary noise barriers (typical design is wooden framed barrier with a small-cantilevered upper portion of superficial density no less than $7 \text{kg/m}^2$ on a skid	items to be used at all		All construction sites where	Construction stage	• Annex 5, TM- EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		footing with 25mm thick internal sound absorptive lining), and full enclosure, screen the noisy plants including air compressors, generators etc.	construction sites		practicable		
S4.3.4	N4	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected noise monitoring stations	Construction stage	• TM-EIAO
Operatio	nal Noise (H	Road Traffic Noise)					
S4.5.4	N5	<ul> <li>Provide a series of noise mitigation measures including low noise surfacing material, noise barriers, facades with no openable window, school boundary walls and architectural fins before occupation of the protected NSRs. Locations of noise mitigation measures are stated as following:</li> <li>Year 2023:</li> <li>Facade with no openable window at B1-1 and B1-2 for TCE; TCV-6 for TCW</li> <li>1.5m long architectural fin at B1-1 and B1-2 for TCE</li> <li>Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39</li> <li>Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24</li> <li>Approx. 160m long LNRS along Road L24</li> <li>Approx. 160m long LNRS along Road L30</li> <li>Year 2025:</li> <li>Facade with no openable window at B1-1, B1-2, D1-1,</li> </ul>	Reduce operation noise from road traffic	government	Refer to Figure 6.1, Figure 6.1a- b, Figure 6.2, Figures 6.2a-b, Figure 6.3, Figures 6.3a-d, Figure 6.4, and Figures 6.4a-e		• TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		D1-2, D2-3 and D2-4 for TCE; TCV-6 for TCW					
		• 1.5m long architectural fin at B1-1, B1-2 and D2-4 for TCE; TCV-1 for TCW					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39					
		• Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24					
		• Approx. 210m long LNRS along Chung Mun Road					
		• Approx. 160m long LNRS along Road L24					
		• Approx. 160m long LNRS along Road L30					
		Year 2027:					
		• Facade with no openable window at A1-1, A1-2, A2-1, A2-2, A2-3, A2-4, B1-1, B1-2, D1-1, D1-2, D2-3 and D2-4 for TCE; TCV-6 for TCW					
		• 1.5m long architectural fin at A2-1, A2-4, B1-1, B1-2 and D2-4 for TCE;					
		• 1.8m long architectural fin at A1-1, A1-2, A2-1 and A2-4					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 50m long, 4m high school boundary wall at					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		possible school development near Tung Chung Area 39					
		• Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24					
		• Approx. 210m long LNRS along Chung Mun Road					
		Approx. 160m long LNRS along Road L24					
		• Approx. 160m long LNRS along Road L30					
		Year 2045:					
		• Facade with no openable window at A1-1, A1-2, A2-1, A2-2, A2-3, A2-4, B1-1, B1-2, C1-1, C2-1, C2-2, D1-1, D1-2, D2-3, D2-4, E1-4 and E1-5 for TCE; TCV-1 and TCV-6 for TCW					
		• 1.5m long architectural fin at A2-1, A2-4, B1-1, B1-2, C1- 1 and D2-4 for TCE; TCV-1 for TCW					
		• 1.8m long architectural fin at A1-1, A1-2, A2-1, A2-4 and C1-1					
		• Approx. 100m long, 5m high absorptive vertical barrier along Road D3					
		• Approx. 50m long, 5m high absorptive vertical barrier with 3m cantilevered arm at 45° along Road L7					
		• Approx. 60m long, 5m high school boundary wall along Road L3					
		• Approx. 70m long, 5m high school boundary wall with 3m cantilevered arm at 45° along Road L3					
		• Approx. 80m long, 4m high school boundary wall along Road L2					
		• Approx. 40m long, 3m high school boundary wall along Road L2					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		• Approx. 50m long, 4m high school boundary wall at possible school development near Tung Chung Area 39					
		• Approx. 120m long, 5m high vertical barrier with 3m cantilevered arm at 45° at the corner at junction between Chung Mun Road and Road L24					
		• Approx. 210m long LNRS along Chung Mun Road					
		• Approx. 160m long LNRS along Road L24					
		• Approx. 160m long LNRS along Road L30					
Operatio	nal Noise (I	Fixed Noise)					
S4.6.4	N6	<ul> <li>For existing and planned NSRs which are located near to the proposed noise sources, the following tentative noise mitigation measures are considered:</li> <li>All the pumps should be enclosed inside building structures;</li> <li>Proper selection of quiet plant to reduce the tonality at NSRs;</li> <li>Installation of silencer / acoustic enclosure / acoustic louvers for the exhaust of ventilation system.</li> <li>For underground train stations, sound attenuators with sufficient attenuations can be installed to the ventilation shafts.</li> <li>Openings of ventilation system should be located away from NSRs.</li> </ul>	Reduce operation fixed noise	Relevant government departments / Future Operator	All plant rooms where practicable	Prior to operation of the Project	• Noise Control Ordinance and its TM, TM- EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S4.8.4	N7	<ul> <li>Before Phase 1 is occupied:</li> <li>Facade with no openable windows for residential block at B1-2</li> <li>1.5m long architectural fin at B1-2</li> <li>Before Phase 3 is occupied:</li> <li>It should be noted that Railway Stations at TCE and TCW and its associated railway system is a Designated Project under Item A.2 of Schedule 2 of TM-EIAO. Hence, the proposed mitigation measures are tentative for cumulative assessment purpose in this EIA and all the mitigation measures will be revised by the railway operator during their Schedule 2 EIA.</li> <li>Approx. 325m long, semi enclosure along the tracks of Tung Chung Line facing A1-2 and C1-1</li> <li>Approx. 390m long, semi enclosure along the track of Tung Chung Line to Tung Chung direction facing C1-1 to C2-1</li> <li>Approx. 630m long, semi enclosure along the track of Tung Chung Line to Hong Kong direction facing C1-1 and C2-1</li> </ul>	Reduce operation rail noise	Relevant government departments / Future Operator	Refer to Figure 6.1, Figure 6.1a- b, Figure 6.2, Figures 6.2a-b, Figure 6.3, Figure 6.3, Figure 6.4, and Figures 6.4a-e	population intake	• Noise Control Ordinance and its TM, TM- EIAO

EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
uality (Const	ruction Phase)					
W1	<u>General Construction Activities</u> In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below:	To minimize water quality impact from construction site runoff and general construction activities	Contractor	All construction sites where applicable	Construction stage	<ul> <li>Water Pollution Control Ordinance</li> <li>ProPECC PN1/94</li> <li>TM-EIAO</li> </ul>
	• At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.;				• TM-DSS	
	• Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;					
	• The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates;					
	uality (Const	Log Ref       General Construction Activities         W1       General Construction Activities         In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PNI/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below:         • At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.;         • Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;         • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to	Log Ket       Measures & Main Concerns to address         Measures & Main Concerns to address         Multical Construction Phase)         W1       General Construction Activities In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below:       To minimize water quality impact from activities         • At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.;       Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;         • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates;    <	Log Ker       Measures & Main Concerns to address       Agent         Measures & Main Concerns to address         Multical Construction Phase)         W1       General Construction Activities         In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (Pr-DECC PN1/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below:       To minimize water quality impact from constructed off-site water around the site should be constructed off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.;       To minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;         • The dikes or embankments for flood protection should be incorporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates;	Log Ker       Pressures & Main Agent Construction Phase       Pressure Set Main Concerns to address         will (Construction Phase)       General Construction Activities In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PNI/94), best management practices should be implemented on site as far as practicable. The best practices are detailed below:       To minimize vater Contractor ageneral construction sites where applicable       All construction sites where applicable         • At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels, earth bunds or sand bag barriers should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;       The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates;       The dikes or embankment for logs	Log Ref     Agent     Timing     Stage       Measures & Avian Concerns to address     Agent     Timing     Stage

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the contractor prior to the commencement of construction;					
		• Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;					
		• All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;					
		• If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;					
		• All open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;					
		• Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		directed into foul sewers;					
		• Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events;					
		<ul> <li>All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains;</li> </ul>					
		• Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain;					
		• Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts;					
		• All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		<ul> <li>receivers nearby;and</li> <li>Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, mangroves and open sea.</li> </ul>					
S5.4.3	W2	<ul> <li>Sewage from workforce</li> <li>Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance;</li> <li>Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project;</li> <li>Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site.</li> </ul>	To minimize water quality from sewage effluent in construction phase	Contractor	All construction sites where practicable	Construction stage	<ul> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>
\$5.4.3	W3	<ul> <li><u>Construction Works and Bridge Works near Tung Chung</u> <u>Stream</u></li> <li>Use precast structures or other similar approaches</li> </ul>	To prevent any construction works in river and avoid any direct water quality impact to Tung Chung Stream	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
S5.4.3	W4	<ul> <li><u>Construction Works of Sewage Pumping Stations</u></li> <li>A buffer zone of about 20m or about 30m will be zoned to</li> </ul>	To avoid any direct water quality impact to Tung Chung Stream	Contractor	All construction sites where	Construction stage	• ProPECC PN1/94

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		prevent any construction works near river.			practicable		
S5.4.3	W5	<ul> <li><u>Construction Work of Fresh Water and Salt Water Reservoirs</u></li> <li>Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage.</li> </ul>	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
S5.4.3	W6	<ul> <li><u>Construction of Storm Water Management Facilities and</u> <u>Polder Scheme</u></li> <li>Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage.</li> </ul>	To avoid any direct water quality impact to Tung Chung Stream	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
\$5.4.3	W7	<ul> <li><u>Groundwater and Runoff for Tunnel Works</u></li> <li>Cut-and-Cover method for the underpass at Road D1 in Tung Chung East to minimise the intrusion of groundwater. Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters or drainage.</li> </ul>	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94
S5.5.8	W8	<ul> <li><u>Good Management Practice in Construction Phase</u></li> <li>The following good site management practices shall be adopted for the filling works:</li> <li>Water quality monitoring shall be implemented to ensure effective control of water pollution and recommend additional mitigation measures required;</li> <li>The decent speed of grabs shall be controlled to minimize the seabed impact and to reduce the volume of overdredging;</li> <li>A perimeter silt curtain shall be installed during the entire</li> </ul>	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• ProPECC PN1/94

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		reclamation periods;					
		• Barges or hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation;					
		• Excess materials shall be cleaned from the decks and exposed fittings of barges before the vessels are moved;					
		• Plants should not be operated with leaking pipes and any pipe leakages shall be repaired quickly;					
		• Adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action;					
		• All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and					
		• The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site.					
\$5.5.8	W9	• The recovered C&D materials for filling would be ensured no floating or non-inert material by visual inspection, quality assurance, etc.	To avoid water quality impact	Contractor	All construction sites where practicable	Construction stage	• Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Water Qu	ality (Opera	tional Phase)					
S5.6.10	W10	<ul> <li>The following mitigation measures will be implemented to TCV East, North and West SPS, upgraded CMRSPS, proposed TCE West SPS and TCE East SPS</li> <li>100% standby pump capacity with spare pump of 50% pump capacity</li> <li>Dual-feed power supply</li> <li>Wet well storage providing up to 6-hours ADWF capacity (equivalent to about 4 hours of response time during peak flow condition); and</li> <li>Emergency communication mechanism amongst relevant government departments.</li> </ul>	To prevent the impact due to the emergency discharge at TCW and TCE		Proposed Sewage Pumping Station at TCW and TCE	Operational Stage	• DSD's Sewerage Manual
S5.6.10	W11	<ul> <li>The following mitigation measures will be implemented to gravity sewers and rising mains</li> <li>Adopt high density polyethylene (HDPE) pipe for proposed gravity sewers and rising mains.</li> <li>Further protection on proposed rising mains with concrete surround will be provided to mitigate the risk of bursting.</li> </ul>	To minimize the risk of bursting and hence bursting discharge from gravity sewers and rising mains	DSD	Proposed rising mains within TCE and TCW	Operational Stage	-
S5.6.10	W12	<u>Maintenance Dredging for the Proposed Marina</u> Silt curtain should be deployed to reduce the sediment dispersion from the dredging inside the marina.	To reduce the sediment dispersion	Future operator	Proposed marina at TCE	Operational Stage	-

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Sewage d	und Sewerag	e Treatment Implications					
S6.5.4	SS1	<ul> <li>Emergency Discharge of Proposed TCV West SPS, TCV East SPS, TCV North SPS and Upgraded CMRSPS</li> <li>The following mitigation measures will be implemented to TCV East, North and West SPS, and upgraded CMRSPS:</li> <li>100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use</li> <li>Twin rising mains</li> <li>Dual-feed power supply</li> <li>Emergency storage facilities up to 6-hours ADWF capacity; and</li> <li>Emergency communication mechanism amongst relevant government departments.</li> </ul>	To prevent the impact due to the emergency discharge at TCW	DSD	Proposed Sewage Pumping Station at TCW	Operational stage	N/A
S6.5.4	SS2	<ul> <li><u>Emergency Discharge of Proposed TCE West SPS and TCE</u> <u>East SPS</u></li> <li>In order to minimize the impact due to the emergency discharge, the following precautionary measures shall be included in the design of sewage pumping station:</li> <li>100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use</li> <li>Twin rising mains</li> <li>Dual-feed power supply</li> <li>Emergency storage facilities up to 6-hours ADWF capacity; and</li> <li>Emergency communication mechanism amongst relevant</li> </ul>	To minimize the impact due to the emergency discharge at TCE	DSD	Proposed Sewage Pumping Station at TCE	Operational stage	N/A

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		government departments.					
S6.5.4	SS3	<ul> <li>The following mitigation measures will be implemented to prevent pipe bursting on Rising Mains within TCE and TCW:</li> <li>Strong pipe – use HDPE pipe with welded joints</li> <li>Concrete encasement – concrete surround all rising mains</li> </ul>	To minimize the risk of bursting and hence bursting discharge from gravity sewers and rising mains	DSD	Proposed rising mains within TCE and TCW	Operational stage	N/A

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Waste Ma	anagement (	Construction Waste)					
S7.4.1	WM1	<ul> <li><u>Good Site Practices</u></li> <li>The following good site practices are recommended throughout the construction activities:</li> <li>nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling;</li> <li>provision of sufficient waste disposal points and regular collection for disposal;</li> <li>imposition of penalty system on Contractors' improper behaviours when illegal dumping and landfilling outside their respective construction sites, i.e. on nearby farmlands and riverbanks, are reported;</li> <li>appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and</li> <li>the contractor should prepare a Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP) in accordance with the ETWB TC(W) No. 19/2005 for construction phase. The EMP should be submitted to the Engineer for approval. Mitigation measures proposed in the EIA Report and the EM&amp;A Manual should be adopted.</li> </ul>	Minimize waste generation during construction	Contractor	All construction sites	Construction stage	• Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S7.4.1	WM2	<ul> <li><u>Waste Reduction Measures</u></li> <li>Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction:</li> <li>segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>proper storage and site practices to minimize the potential for damage and contamination of construction materials;</li> <li>plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste;</li> <li>sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.);</li> <li>provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling.</li> </ul>	Reduce waste generation	Contractor	All construction sites	Construction stage	• Waste Disposal Ordinance
S7.4.1	WM3	<ul> <li><u>Storage of Waste</u></li> <li>The following recommendation should be implemented to minimize the impacts:</li> <li>waste such as soil should be handled and stored well to ensure secure containment; and</li> <li>Depends on actual site activities, certain locations within the site area would be used for storage of waste to enhance reuse. However, there would not be any designated location for storage of waste, and the storage locations would need to be adjusted to suite actual site conditions;</li> </ul>	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	<ul> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> <li>ETWB TCW No. 19/2005</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
S7.4.1	WM4	<ul> <li><u>Collection and Transportation of Waste</u></li> <li>The following recommendation should be implemented to minimize the impacts:</li> <li>remove waste in timely manner;</li> <li>employ the trucks with cover or enclosed containers for waste transportation;</li> <li>obtain relevant waste disposal permits from the appropriate authorities; and</li> <li>disposal of waste should be done at licensed waste disposal facilities.</li> </ul>	Minimize waste impacts from storage	Contractor	All construction sites	Construction stage	• Waste Disposal Ordinance
S7.4.1	WM5	<ul> <li><u>Excavated and C&amp;D Materials</u></li> <li>Wherever practicable, C&amp;D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public fill reception facilities or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&amp;D materials:</li> <li>maintain temporary stockpiles and reuse excavated fill material for backfilling;</li> <li>carry out on-site sorting;</li> <li>make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; and</li> <li>implement a trip-ticket system for each works contract to ensure that the disposal of C&amp;D materials are properly documented and verified, so as to avoid the illegal dumping and landfilling of C&amp;D materials on farmlands/ riverbanks at TCW;</li> </ul>	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction Stage	<ul> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> <li>ETWB TCW No. 19/2005</li> <li>Project Administrative Handbook for Civil Engineering Works, 2012 Edition</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		On-site sorting of C&D materials					
		<ul> <li>Reuse of C&amp;D materials</li> <li>Use of Standard Formwork and Planning of Construction Materials purchasing</li> </ul>					
S7.4.1	WM6	<u>Provision of Wheel Wash Facilities</u> Wheel wash facilities have to be provided at the site entrance before the trucks leaving the works area. Dust disturbance due to the trucks transportation to the public road network could be minimized by such arrangement.	Minimize waste impacts from trucks transportation	Contractor	All construction sites	Construction Stage	N/A
S7.4.1	WM7	Excavated Contaminated Soil As a precaution, it is recommended that standard good site practice should be implemented during the construction phase to minimize any potential exposure to contaminated soils or groundwater.	Remediate contaminated soil	Contractor	All construction sites where applicable	Construction stage	• Practice Guide for Investigation and Remediation of Contaminated Land
S7.4.1	WM8	<ul> <li><u>Excavated Marine Sediments</u></li> <li>Reference has been made to the sediment testing results. Possible mitigation measures to handle the contaminated/ uncontaminated sediment are summarized as follows.</li> <li>All construction plant and equipment shall be designed and maintained to minimise the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location.</li> <li>All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.</li> <li>Adequate freeboard shall be maintained on barges to</li> </ul>	Handle excavated sediment	Contractor	All construction sites where applicable	Construction stage	• ETWB-TCW 34/2002

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		ensure that decks are not washed by wave action.					
S7.4.1	WM9	<ul> <li>Dumping of excavated sediment</li> <li>Keep and produce logs and other records to demonstrate compliance and ensure journeys are consistent with designated locations</li> <li>Comply with the conditions in the dumping permit.</li> <li>All bottom dumping vessels (hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material.</li> <li>The excavated sediment shall be placed into the disposal pit by bottom dumping.</li> <li>Contaminated marine mud shall be transported by split barge of not less than 750m<sup>3</sup> capacity and capable of rapid opening and discharge at the disposal site.</li> <li>Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Sediment adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site.</li> <li>For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping into designated mud pit. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containres and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal.</li> </ul>	Handle excavated sediment	Contractor	All construction sites where applicable	Construction stage	• ETWB-TCW 34/2002
S7.4.1	WM10	Chemical Waste	Control the chemical waste and ensure proper	Contractor	All construction	Construction stage	• Waste Disposal

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste collector. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	storage, handling and disposal.		sites		<ul> <li>(Chemical Waste) General) Regulation</li> <li>Code of Practice on the Packaging, Labelling and Storage of Chemical Waste</li> </ul>
S7.4.1	WM11	<ul> <li><u>General Refuse</u></li> <li>General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling.</li> <li>Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean.</li> <li>A reputable waste collector should be employed to remove general refuse on a daily basis.</li> </ul>	Minimize production of the general refuse and avoid odour, pest and litter impacts		All construction sites	Construction stage	• Waste Disposal Ordinance
\$7.4.1	WM12	<u>Floating Refuse accumulated along the seawall</u> The floating refuse along seawall should be collected to avoid accumulation. In addition, proper seawall design should be employed, and regular checking and cleaning of floating refuse should be implemented.	Control floating refuse and ensure proper disposal	Contractor	Construction sites along seawall	Construction stage	• Waste Disposal Ordinance
Waste Ma	anagement (	(Operational Waste)					
S7.4.2	WM13	Illegal dumping and landfilling	Prevent waste from	Relevant	All	Operational stage	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		As a Development Permission Area (DPA) plan will be issued by the Town Planning Board as a temporary measure before the formal Outline Zoning Plan (OZP) for Tung Chung New Town Extension is adopted, statutory right to guide and control the development and use of land would be authorised. Should there be illegal dumping and landfilling observed/ reported on nearby farmlands and riverbanks, the government authority should take all necessary actions including but not limited to prosecution to remediate the circumstances.	illegal dumping and landfilling	government departments	construction sites		
S7.4.2	WM14	<ul> <li><u>Municipal Solid Waste</u></li> <li>A reputable waste collector should be employed to remove general refuse on a daily basis.</li> <li>A 4-bin recycling system for paper, metals, plastics and glass should be adopted together with a general refuse bin. They should be placed in prominent places to promote waste separation at source. All recyclable materials should be collected by recyclers.</li> </ul>	Remove general refuse generated from the proposed development	FEHD/ Relevant Operators	All construction sites	Operational stage	• Waste Disposal Ordinance
S7.4.2	WM15	<ul> <li><u>Chemical Waste</u></li> <li>Localized chemical waste storage areas should be located close to the source of waste generation for temporary storage. Drum-type containers with proper labelling should be used to collect chemical wastes for storage at the designated areas.</li> <li>A licensed collector should be employed for the chemical waste collection and the chemical wastes should be disposed at an appropriate facility, such as Chemical Waste Treatment Centre (CWTC) in Tsing Yi.</li> <li>Collection receipts issued by the licensed collector showing the quantities and types of chemical waste taken off-site and details of the treatment facility should be kept for record.</li> </ul>	Reduce chemical waste due to waste handling	Contractors/ Relevant Operators	All construction sites	Operational stage	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
\$7.4.2	WM16	<ul> <li>Floating Refuse accumulated along seawall</li> <li>The floating refuse along seawall should be collected to avoid accumulation.</li> </ul>	Control floating refuse and ensure proper disposal		Along seawall	Operational stage	• Waste Disposal Ordinance
\$7.4.2	WM17	<ul> <li><u>Floating Refuse inside Marina</u></li> <li>Floating refuse at the marina will be collected and disposed by the licensed waste collector and as required.</li> </ul>	Reduce floating refuse washing up onto marina by currents and wind	-	Marina	Operational stage	• Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Land Cor	ntamination						
S8.4.1	LC1	Undertaking environmental Site Inspection (SI) for all potentially contaminated sites as listed in the Contamination Assessment Plan (CAP).	contamination potential before the		All potentially contaminate d sites as listed in the CAP	Prior to the construction stage	<ul> <li>Annex 19 of the TM-EIAO, Guidelines for Assessment of Impact On Sites of Cultural Heritage and Other Impacts (Section 3 : Potential Contaminated Land Issues);</li> <li>Guidance Manual for Use of Risk- Based Remediation Goals (RBRGs) for Contaminated Land Management;</li> <li>Guidance Notes for Contaminated Land Assessment and Remediation; and</li> <li>Practice Guide for Investigation and Remediation of Contaminated Land</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
							• Recommendation s in Health Risk Assessment
\$8.4.2	LC2	Re-appraisal would be required for the surveyed sites, other remaining areas of the PDAs and the works areas for the associated infrastructures because the development of these sites/ areas would only commence a number of years later, which may allow changes in the land usage of these sites and may give rise to potential land contamination issues. The Project Proponent's appointed consultant would prepare a supplementary CAP presenting the findings of the re- appraisal and strategy of the recommended SI, if required, and submit to EPD for review and approval.	To assess the latest site situation and identify any potential additional hot spots and contaminated sites.	5 1		Prior to the construction stage	Ditto
S8.5	LC3	After approval of the supplementary CAP and upon completion of the SI works, the PP should prepare and submit a Contamination Assessment Report (CAR) for all potentially contaminated sites listed in the CAP to EPD for agreement.	Present the findings of SI and evaluate the level and extent of potential contamination	Project Proponent / Detailed Design Consultant / Private developer	All the surveyed sites as listed in the CAP, other remaining areas of the PDAs and works areas for the associated infrastructu res	Prior to the construction stage	Ditto
S.8.5	LC4	Preparation and submission of Remediation Action Plan (RAP) to EPD for agreement if land contamination is confirmed.		Detailed Design	All the surveyed sites as listed in the CAP, other remaining	Prior to the construction stage	Ditto

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			assessment if remediation is required		areas of the PDAs and works areas for the associated infrastructu res		
S.8.5	LC5	Preparation and submission of Remediation Report (RR) to EPD for agreement.	Demonstrate that the decontamination work is adequate and is carried out in accordance with the endorsed CAR and RAP	Detailed Design Consultant /	All the surveyed sites as listed in the CAP, other remaining areas of the PDAs and works areas for the associated infrastructu res	Prior to the construction stage	Ditto

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Ecology	( Design Ph	ase)	•				
S9.8.1	EC1	Development under the Project have avoided all the recognised sites of conservation importance, including Country Parks,	To protect the recognised sites of conservation importance and habitats inside	PlanD	TCW	RODP	• Not available
S9.8.1	EC2	About 30m buffer zone at the two main branches and the joined outlet section of Tung Chung Stream; and about 20m buffer for the major tributary at Ngau Au of Tung Chung Stream	To protect the Tung Chung Stream	PlanD	Tung Chung Stream	RODP	• Not available
S9.8.2	EC3	Detailed designs should avoid the encroachment of important habitats (e.g. Fung Shui Wood) within the Project Site	To protect the important habitats within Project Site	PlanD	TCW	Design Phase	• Not available
S9.8.2	EC4	Detailed designs of noise barriers to prevent bird collision	To prevent bird collision	HyD	Noise barriers	Design Phase	Guidelines on Design of Noise Barriers
\$9.8.2	EC5	<ul> <li>Measures and suitable designs of sewage pumping stations to prevent emergency discharge accidents in TCE and TCW</li> <li>100% standby pumping capacity within each SPS, with spare pump up to 50% pumping capacity stockpiled in each SPS for any emergency use</li> <li>Twin rising mains</li> <li>Dual-feed power supply</li> <li>Emergency storage facilities up to 6-hours ADWF capacity; and</li> <li>Emergency communication mechanism amongst relevant government departments.</li> </ul>	To protect the water bodies from impacts due to emergency discharge in TCE and TCW	DSD	Proposed and Upgraded Sewage pumping stations at TCE and TCW	Design Phase	• DSD standards

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Ecology (	Constructio	on Phase)					
\$9.8.2	EC6	Adoption of non-dredged reclamation method	To maintain the marine water quality	Contractor	Reclamation area of TCE and Road P1	Construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.8.3	EC7	Compensation woodland planting	To compensate loss of woodland, fung shui wood and orchard	Contractor	Uphill of Sheung Lei Pai FSW and Tung Chung Road	phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
\$9.8.3	EC8	Planting of emergent plant	To provide habitats for this Jhora Scrub Hopper, and to compensate the loss of their habitats (wet abandoned agricultural land) in northern section of Fong Yuen	DSD / Contractor	Inside the future River Park	Construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.8.3	EC9	Capture-and-translocation exercise	Minimize the potential impact to amphibian species of conservation importance including Romer's Tree Frog and Chinese Bullfrog due to site formation	For public works, provided by the government departments responsible for the construction of those public works or the site formation works . For TCV-1 and	Public works near the eastern branch of Tung Chung Stream, in particular 1) the River Park, 2) the Distributor Road along	Capture-and- translocation exercise before commencement of site formation	<ul> <li>EIA</li> <li>Contractual requirements</li> <li>Explanatory statement of the OZP (for private lots)</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
				TCV-5, where the lands within mostly belong to private lots, the future project proponents of those private lots, via the established mechanism for land transaction application.	branch of Tung Chung Stream, 3) the road upgrade along the existing Shek Mun		
S9.8.3	EC10	Preservation and/or Transplantation of plant species of conservation importance and the following monitoring of preserved/transplanted plant individuals	Protection of plant species of conservation importance	For public works, provided by the government departments responsible for the construction of those public works or the site formation works.	Within construction sites All areas for public works Also be required in private lands	For preservation and/or transplantation, before commencement of site formation.	<ul> <li>Contractual requirements</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
				For TCV-1, where the lands within mostly belong to private lots, the future project proponents of those private lots, via the established mechanism for land transaction application.	in TCV-1.		
S9.8.3	EC11	Defining and maintaining construction site boundaries (including erection of site hoarding, fences etc.)	Screen construction disturbance to the nearby habitats	Contractor	Along the boundary of construction sites and buffer zones of Tung Chung Streams, along the boundary of mature woodland and Fung Shui Wood, and along the boundary between TCV-6 and the middle section of Fong Yuen	commencement of site formation	• EIA • Contractual requirements
S9.8.3	EC12	Protection of Tung Chung Stream	Minimize the potential water pollution due to	Contractor	Within construction	Construction	• EIA

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			construction of road crossings or other works near Tung Chung Stream		sites	phase	Contractual requirements
S9.8.3	EC13	Implementation of standard site practices	Minimize the potential impact due to dust, noise and runoff during construction phase	Contractor	Within construction sites	Construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.8.4	EC14	Adopting Eco-shoreline design	To mitigate the impact of the marine loss	CEDD	Along future seawall	Construction stage	<ul><li>EIA</li><li>Contractual requirements</li></ul>
S9.8.4	EC15	Strict enforcement on no-dumping	Minimise the potential impact to marine habitats	Contractor	In reclamation area as well as all works area and travel route of works vessels	Before and during construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.8.4	EC16	Spill response plan	Minimise the potential impact to marine habitats	Contractor	In reclamation area as well as all works area and travel route of works vessels	Before and during construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S.9.8.4	EC17	Control and minimization of marine traffic by including using larger-sized barges, land transportation of materials, reuse of excavation and C&D materials and speed limits &	Reduce marine traffic	Contractor	In reclamation area as well	Construction phase	• EIA • Contractual

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
		regular routes of works vessels			as all works area and travel route of works vessels		requirements
\$9.8.4	EC18	Dolphin exclusion zone and dolphin watching plan	Protection of CWD	Contractor	In reclamation area as well as all works area	Construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
\$9.8.4	EC19	Speed limits and regular routes of works vessels; Prepare and submit a "Works Vessel Travel Route Plan"	Protection of CWD	Contractor	In reclamation area as well as all works area	Construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.11.1	EC20	Monitoring of compensatory planting woodland	Monitor the survival of trees and establishment of the woodland	CEDD/ Contractor	Areas of compensator y woodland planting	Quarterly for 3 years after completion of planting works	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S9.11.1	EC21	Monitoring of translocated amphibians	Monitor the effectiveness of the translocation programme	Public works: Responsible government departments / Contractor Private lots: Private developers	Release sites for translocated amphibians	After translocation exercise. At least three surveys in each release site during the breeding season, preferably monthly between April and June,	<ul> <li>EIA</li> <li>Contractual requirements</li> <li>Explanatory statement of the OZP (for private lots)</li> </ul>
\$9.11.1	EC22	Monitoring of preserved / transplanted plant species	Monitor and evaluate	Public works:	Construction	After	• EIA

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
			the effectiveness of the preservation and transplantation programme.	Responsible government departments / Contractor Private lots: Private developers	sites for preserved plants; recipient sites for transplanted plants	transplantation or preservation. For transplanted individuals, for two years, monthly for the first year, and then quarterly for the second year. For the preserved individuals, monthly throughout the construction.	<ul> <li>Contractual requirements</li> <li>Explanatory statement of the OZP (for private lots)</li> </ul>
S9.11.1	EC23	Monitoring of Tung Chung Stream and Wong Lung Hang Stream EISs	Protect the EISs	Contractor	Tung Chung Stream and Wong Lung Hang Stream	Construction phase and post- construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
9.11.2	EC24	Monitoring of Tung Chung Bay and Tai Ho Wan	Protect Tung Chung Bay and Tai Ho Wan	Contractor	Tung Chung Bay and Tai Ho Wan	Construction phase and post- construction phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
Ecology (	Operationa	l Phase)					
S9.11.1	EC25	Monitoring of emergent plant inside River Park	Monitor the survival of emergent plant	DSD/ Contractor	Three months after completion of planting in future River Park	Quarterly for 2 years after completion of planting works	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures		Implementation Agent		Implementation Stage	Requirements and / or standards to be achieved
9.11.2	EC26	Eco-shoreline monitoring	Monitor the colonisation and establishment of fauna and/or flora, water quality, and recruitments of fisheries species	CEDD/ Contractor	Eco- shoreline at TCE PDA reclamation	nhase twice in	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
Fisheries	5						
S10.8	F1	Good Site Practices	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	<ul><li>EIA</li><li>Contractual requirements</li></ul>
S10.8	F2	No dumping	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	<ul><li>EIA</li><li>Contractual requirements</li></ul>
S10.8	F3	Spill response plan	To protect the fisheries resources	Contractor	In reclamation area	Construction phase	<ul><li>EIA</li><li>Contractual requirements</li></ul>
S10.9	F4	Follow the mitigation measures proposed in the water quality assessment for the construction and operation phases of the project.	To protect the fisheries resources	Contractor	Waters in Northern Lantau	Construction phase and operation phase	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S10.9	F5	Follow the mitigation measure of eco-shoreline in ecology chapter for the construction and operation phases of the project.	To enhance the fisheries resources	Contractor	Eco- shorelines	Construction phase and operation phase	<ul><li>EIA</li><li>Contractual requirements</li></ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
Landsca	oe and Visua	l (Construction Phase)					
S11.7 MM1	LV1	Optimisation of Construction Areas & Providing Temporary Landscape on Temporary Construction – Construction areas' control shall be enforced, where possible, to ensure that the landscape and visual impacts arising from the construction activities are minimised. It includes reduction of the extent of working areas and temporary works areas, management on storing and using	Minimise the landscape and visual impacts arising from the construction activities	Relevant Government Departments / Private Sector	Through-out Tung Chung West (TCW) area and Tung Chung East (TCE) area	Construction Phase	
		the construction equipment and materials, and consideration of detailed schedules to shorten the construction period. Temporary landscape treatments are considered to be adopted such as applying hydro-seeding on temporary stockpiles and reclamation areas to alleviate the potential impacts.					
S11.7 MM2	LV2	Minimize Topographical Change – The footprint of construction elements and temporary works areas should be optimised to reduce topographical/ landform changes, as well as reduce land take and interference with natural terrain. Where there is a need to significantly cut into the existing landform, retaining walls and cut slopes should be considered as appropriate. To minimize landform changes and land resumption,	Reduce topographical changes and minimize land resumption	Relevant Government Departments / Private Sector	Through-out TCW area	Prior to Construction & Construction Phase	• GEO Publication No/1/2011, Technical Guidelines on Landscape Treatment for Slopes
		earthworks and engineered slopes should be designed to be a visually interesting, compatible with the surrounding landscape and to mimic the natural contouring and terrain as appropriate.					
S11.7 MM3	LV3	Preservation of Potentially Registerable OVTs, Rare and Protective Vegetation – Exiting trees to be retained within the Project Site should be carefully protected during construction. In particular Potentially Registerable OVTs are considered to be preserved according to ETWB	Protect and Preserve Trees	Relevant Government Departments / Private Sector	Onsite, particularly for TCW area	Prior to Construction & Construction Phase	• ETWB TC(W) No.29/2004 and DEVB TC(W)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		Technical Circular (Works) No. 29/2004. Rare and Protective Vegetation shall be protected following Forestry Regulations (Cap.96) and Protection of Endangered Species of Animals and Plants Ordinance (Cap.586). Detailed Tree Protection Specification shall be provided in the Contract Specification according to DEVB TCW No. 10/2013 Tree Preservation. Following DEVB (GLTM) Guidelines for Tree Preservation during Development, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained.					No.10/2013. • Greening, Landscape and Tree Management Section (GLTM) of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)
S11.7 MM4	LV4	Transplanting of Existing Trees – Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor locations within the site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with DEVB TCW 10/2013 and LAO PN 7/2007 and final locations of transplanted trees should be agreed prior to commencement of the work. For trees associated with highways e.g. roadside planting	Transplant Trees where suitable for transplantation	Relevant Government Departments / Private Sector	Onsite where possible, otherwise consider offsite locations	Prior to Construction & Construction Phase	<ul> <li>DEVB TC(W) No.10/2013 and LAO PN7/2007</li> <li>HyD HQ/GN/13 Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		along highways, that are unavoidably affected and should be transplanted. HyD HQ/GN/13 'Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit' should be referred to.					Ambit • GLTM of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)
S11.7 MM5	LV5	Screen hoarding – To reduce negative visual impact, construction site hoarding should be erected around the site to screen pedestrian level views into the construction area from visual sensitive receivers. Hoarding design should consider greening measures such as colour and form should be adopted to improve its visual appearance.	To screen undesirable views of the work site.	Relevant Government Departments / Private Sector	Through-out TCW and TCE areas	Construction Phase	
S11.7 MM6	LV6	Adopting Non-dredge Method for the Reclamation – In order to minimize the potential adverse impacts caused by the reclamation, a number of alternative construction methodologies has been critically examined. After considering all the options such as fully dredged, partially dredged and non-dredged methods for seawall construction and reclamation, non-dredged method for both the seawall construction and reclamation are recommended so as to minimize the generation of dredged sediment.	Minimize the potential adverse impacts caused by the reclamation	Relevant Government Departments / Private Sector	Through-out TCE area	Construction Phase	• Foreshore and Sea-bed (Reclamations) Ordinance (Cap.127)
S11.7 MM7	LV7	Protection of Natural Rivers and Streams – For all the natural rivers and streams inside the development area, in accordance with ETWB TCW 5/2005, consideration of protection measures should be made to minimize any impacts from the construction works, especially those	Protection of Natural Rivers and Streams Minimize the impacts from the construction works	Relevant Government Departments / Private Sector	Through-out TCW area	Prior to Construction & Construction Phase	<ul> <li>EPD ProPECC PN1/94 Construction Site Drainage.</li> <li>DSD Technical</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		development near Tung Chung Stream. According to the latest RODP, a 30m buffer zone will be zoned as "CA". Precast structures or other similar approaches will be used to prevent / minimise any construction works in river and thus to avoid any direct water quality impact. Good site management as stipulated in ProPECC PN1/94 will be fully implemented to avoid polluted liquid or solid wastes from falling into the river waters.					Circular No. 2/2004. • ETWB TC(W) No.5/2005 Protection of natural streams/rivers from adverse impacts arising from construction works
S11.7 MM8	LV8	Preservation of Natural Coastline – The natural coastline along the proposed "RO" of the RODP in TCW should be preserved. The remaining natural shorelines in Tung Chung Bay including sandy shores close to the Tung Chung old pier will be conserved as a Waterfront Park according to the latest RODP.	Preservation of Natural Coastline	Relevant Government Departments	Onsite where possible	Prior to Construction & Construction Phase	
S11.7 MM9	LV9	Providing Natural Rock Material/ Planting for Artificial Seawall – There would be inevitable permanent losses of marine waters (seabed and water column), and direct impacts on existing artificial seawalls due to the reclamation. To minimize the impacts, the design of the future seawall like 'eco-shoreline' could be improved to provide high ecological functions and mitigate the impact of the loss.	Mitigate the impacts on existing artificial seawalls	Relevant Government Departments	Onsite where possible	Prior to Construction & Construction Phase	
		An 'eco-shoreline' is any shoreline which provides beneficial functions to the local ecosystem through a range of active or passive solutions, whilst providing coastal protection. By means of using natural rock materials for artificial seawall and considering to introduce a native vegetation buffer directly behind the top of seawalls as appropriate to create habitat, shelter and a source of food					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		for benefiting both terrestrial and aquatic species along the foreshore, these measures can help to enhance the ecological functions and 'natural-look' of the shoreline, and the potential impacts will be mitigated.					
Landscap	e and Visua	l (Operational Phase)					
S11.7 MM10	LV10	Compensatory Planting – Compensatory planting for felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Removal Application process under DEVB TCW No. 10/2013 and LAO PN 7/2007. The location of compensatory planting is proposed at the potential open areas such as open spaces, amenity areas, open areas of the streetscapes including roadside planting, as well as the open areas within development lots. The species to be planted should be all native species, taken "Characteristics of Major Local Tree Species Propagated by AFCD" as a reference. A search of species to be planted will be conducted in a further detailed stage.	Compensate for trees and shrubs lost due to the Project	Relevant Government Departments / Private Sector	Onsite where possible, particular-ly for TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	<ul> <li>DEVB TC(W) No.10/2013 and LAO PN 7/2007.</li> <li>GLTM of the Development Bureau, Guidelines on Tree Preservation during Development (April, 2015)</li> </ul>
S11.7 MM11	LV11	Woodland Restoration – A search of area to mitigate the loss of woodland has been conducted. Priority has been given to the practicability of compensation of woodland within the boundary of RODP. Given the nature of the project is to provide development opportunities to satisfy the needs for the society in general and the aspirations of local communities, compensation of woodland is only possible for the areas beyond the RODP. It is considered that the areas adjoining the woodlands near the existing services reservoirs, and hillsides to the east of Tung Chung Road, would be suitable locations. The advantage of these locations is that there are existing woodlands immediately	Reprovide areas of woodland to compensate for those areas of quality woodland lost	CEDD /AFCD	In areas identified and as agreed with AFCD	Prior to Construction, Construction Phase & Maintenance in Operation Phase	<ul> <li>DEVB Technical Circular Works 10/2013- Tree Preservation</li> <li>GLTM of the Development Bureau, Guidelines on Tree Preservation</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		downhill to the location and the Sheung Ling Pei Fung Shui Wood is further downhill behind Sheung Ling Pei Village, planting new woodland areas adjoining existing woodlands would form an ecological linkage and increase the overall habitat size, and hence would help to enhance the ecological and landscape values in the long run.					during Development (April, 2015)
		It is noted that the compensation trees for landscape impacts will also be planted near the future service reservoirs. The tree species to be planted should be all native species for woodland compensation, and the two areas uphill to Sheung Ling Pei should also make reference to the existing tree species reported in Fung Shui Woods habitat.					
S11.7 MM12	LV12	Screen Planting – Tall screen/buffer trees and shrubs should be planted to screen proposed structures such as roads and buildings. This measure will form part of the compensatory planting and will improve compatibility with the surrounding environment and create a pleasant pedestrian environment.	To screen proposed structures Improve compatibility with the surrounding environment	Relevant Government Departments	Through-out the working sites of the TCW and TCE areas	Prior to Construction, Construction Phase & Maintenance in Operation Phase	• HyD HQ/GN/15– Guidelines for Greening Works along Highways.
S11.7 MM13	LV13	Roadside Planting – Roadside greening is proposed alongside all roads within the possible developments. It will enhance local identity, if theme planting is used, and reduce visual impact through screening. At-grade road planting should be considered along central dividers and on road islands e.g. in the middle of roundabouts.	Soften the hard, straight edges and provide greening along the roads; Improve the visual amenity	Relevant Government Departments	Along new roads, and On appropriate viaducts	Prior to Construction, Construction Phase & Maintenance in Operation Phase	<ul> <li>HyD HQ/GN/15– Guidelines for Greening Works along Highways.</li> <li>Development Bureau Technical Circular Works No.2/2012 – Allocation of Space for Quality</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	-	Location	Implementation Stage	Requirements and / or standards to be achieved
							Greening on Roads

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
S11.7 MM14	LV14	Aesthetic Design of Built Development – The planning of the revised RODP has considered reducing potential visual impacts, enhancing visual amenity and keeping visual corridors. The proposed development will ensure the building massing is compatible with its surroundings. To improve visual amenity, natural building materials could be used on building facades. For example, stone and timber should be considered for architectural features; light earthy tone colours such as shades of green, shades of grey, shades of brown and off-white should be considered for the façade treatment to reduce the visibility of the development components. The form, textures, finishes and colours of the proposed development components should aim to be compatible with the existing surroundings. It would only be implemented for public developments/projects.	Improve visual amenity of the new buildings, keep visual corridors and integrate as possible into the surrounding landscape	Relevant Government Departments	Through-out the TCW and TCE areas	Prior to Construction, Maintenance in Operation Phase	<ul> <li>Hong Kong Planning Standards and Guidelines (HKPSG) issued by the Planning Department (As at Aug 2011);</li> <li>PNAP APP- 152, Sustainable Building Design Guidelines</li> </ul>
S11.7 MM15	LV15	<ul> <li>Maximise Greening on Structures – The Government has been actively promoting greening in buildings and structures such as bridges to improve the environment. This includes actively implementing rooftop greening or vertical greening, as where practicable to enhance the cityscape and mitigate the heat island effect in urban areas. For the new built forms in TCW and TCE, it is considered the implementation of the following greening measures could alleviate the landscape and visual impacts of new development and help the development blend in with its surrounding landscape:</li> <li>Sky Garden: Refuge floors or voids in building mass formed by partial removal of floor plates on certain building storeys provise opportunities for sky gardens for the proposed built development. It can allow views through the development to the background formed by the natural hillsides and</li> </ul>	Maximise Greening coverage Enhance visual amenity, create visual corridors and integrate as possible into the surrounding landscape	Relevant Government Departments	On appropriate buildings and structures	Prior to Construction, Construction Phase & Maintenance in Operation Phase	<ul> <li>Development Bureau Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects</li> <li>PNAP APP- 152, Sustainable Building Design Guidelines</li> </ul>

<ul> <li>developmen Circular (C Greenery Developme private dev with inade implemente Design Gui</li> <li>Green Roo completed Hong Kon concepts at recommend application into accoun and TCE. alleviated a enhanced. applicable to and should Sustainable 152. Releva (Works) No</li> </ul>	d Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
completed Hong Kom concepts an recommend application into accoun and TCE. alleviated a enhanced. applicable t and should Sustainable 152. Releva (Works) No	the visual amenity effectively. For public ents, relevant technical document Technical (Works) No. 3/2012 Site Coverage of for Government Building Projects by nent Bureau in 2011 shall be referred to. For evelopments, it is only applicable to sites lequate greening coverage and should be tted in accordance with Sustainable Building uidelines PNAP APP-152.					
Bureau in developmen Circular ( Greenery Developme private dev with inade implemente Design Gui	bof: The Architectural Services Department d the Study on Green Roof Application in ong in 2007 which reviewed the latest and design technology of green roof and nded technical guidelines suitable for in in Hong Kong. The study will be taken out to the new buildings to be built in TCW d. Landscape and visual impact can be and the landscape and visual value can be . For private development, it is only e to sites with inadequate greening coverage ild be implemented in accordance with le Building Design Guidelines PNAP APP- want technical document Technical Circular No. 3/2012 Site Coverage of Greenery for ent Building Projects by Development in 2011 shall be reference. For public ents, relevant technical document Technical (Works) No. 3/2012 Site Coverage of for Government Building Projects by nent Bureau in 2011 shall be referred to. For evelopments, it is only applicable to sites dequate greening coverage and should be ited in accordance with Sustainable Building uidelines PNAP APP-152. Green: Planting of climbers to grow up					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		<ul> <li>vertical surfaces where appropriate (e.g. building edges), to soften hard structures and facilities. Relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be observed. For public developments, relevant technical document Technical Circular (Works) No. 3/2012 Site Coverage of Greenery for Government Building Projects by Development Bureau in 2011 shall be reference. For private development, it is only applicable to sites with inadequate greening coverage and should be implemented in accordance with Sustainable Building Design Guidelines PNAP APP-152.</li> <li>Greening on infrastructure: Planting could be provided on infrastructure such as bridges where appropriate to enhance greenery to soften its built edges. Screen planting could be provided near infrastructure to reduce any undesirable visual impacts.</li> </ul>					
S11.7 MM16	LV16	Noise barrier design – The visual impact of noise mitigation measures will be mitigated by appropriate detailed design, including suitable combination of transparent and sound absorbent materials, appropriate colour selection of panels and supporting structures, or provision of at-grade planting of trees, shrubs and/or climbers camouflage to the barriers, as well as design of supporting structures to incorporate a high level of quality and aesthetics. A combination of transparent panels at top and solid panels at bottom would lighten the visual impact, and at the same time maintain the attractiveness by using colourful panels. The noise barriers would be implemented for District Distributor Roads and Local Distributor Roads at both TCE and TCW area.	Minimize the visual impact from the structures of noise barriers	HyD	Noise barriers within the TCW and TCE areas	Prior to Construction, Construction Phase & Maintenance in Operation Phase	<ul> <li>GLTM of the Development Bureau's Guidelines on Greening of Noise Barriers (April 2012).</li> <li>Guidelines on Design of Noise Barriers by HyD and EPD in 2003</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
S11.7 MM17	LV17	Landscape Treatment for Polders & Attenuation Ponds – There would be polders and attenuation ponds in TCW. While they are primarily used for receiving and treating surface runoff and alleviating the flood risk during heavy rainfall, the design of those has provided an opportunity to have a synergy to enhance both the ecological and landscape values together.	Enhance the landscape and visual value	DSD	Polders & Attenuation Ponds where possible	Prior to Construction, Construction Phase & Maintenance in Operation Phase	
		Depending on detailed design, part of these attenuation ponds (mainly the biofiltration zone) could be refined in an appropriate manner, without compromising its primary functions of treating surface runoff and flood protection, to incorporate ecological and landscape design such as planting of aquatic plants and butterfly foodplant for providing the landscape and ecological enhancement.					
Landscape	e and Visua	l (Construction & Operational Phase)					
S11.7 MM18	LV18	Landscaping on Slopes – Hydro seeding of modified slopes should be done as soon as grading works are completed to prevent erosion and subsequent loss of landscape resources and character. Woodland tree seedlings and/ or shrubs should be planted where gradient and site conditions allow. In addition, landscape planting should be provided for the retaining structures associated with modified slopes where	Enhance landscape value, plant diversity and their visual appearance	CEDD	Onsite, particularly in TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	GEO     Publication     No.1/2011     Technical     Guidelines on     Landscape     Treatment for     Slopes by     CEDD in 2011
S11.7 MM19	LV19	condition allow. Landscape Treatment on Channelized Watercourses – For the channelized watercourses in Tung Chung Stream that will be dechannelized, the Drainage Services Department Practice Note No.1/2005 – Guidelines on Environmental Considerations for River Channel Design, should be considered and appropriate measures included ensuring the new watercourses match the existing as far as possible.	Avoid direct impacts on the watercourse Improve the visual amenity	CEDD	The channelized watercourses throughout the TCW area	Prior to Construction, Construction Phase & Maintenance in Operation Phase	• Drainage Services Department Practice Note No.1/2005 – Guidelines on Environmental

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementati on Agent	Location	Implementation Stage	Requirements and / or standards to be achieved
		Measures can include enhancement planting to upgrade the channels as appropriate, including consideration of wetland planting along embankments where appropriate; as well as consideration of the best materials for the channel lining (e.g. gabion).					Considerations for River Channel Design
S11.7 MM20	LV20	Light Control – Construction day and night time lighting should be controlled to minimize glare impact to adjacent VSRs during the construction stage. Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase.	Minimize negative glare impact to adjacent VSRs	Relevant Government Departments / Private Sector	Through-out the TCW and TCE areas	Construction Phase & Operation Phase	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Cultural I	Heritage Im	pact (Construction and Operational Phase)					
S.12.5	CHI	<ul> <li><u>Terrestrial Archaeology</u></li> <li>Implement rescue excavations/ survey-cum-rescue excavations/ further surveys after land resumption and prior to any construction works (see Figure 14.1 for the locations of rescue excavations/survey-cum-rescue excavations/further survey)</li> </ul>	<ol> <li>Rescue excavations to salvage archaeological data and cultural materials</li> <li>Survey-cum-rescue excavations to better locate and design the follow up rescue excavations</li> <li>Further surveys to obtain sufficient data for formulation of appropriate mitigation measures</li> </ol>	Future Private	After land resumption and prior to any construction works	resumption and prior to any construction works	<ul> <li>Guidelines for Cultural Heritage Impact Assessment</li> <li>TM-EIAO Annex 10 and Annex 19</li> <li>Antiquities and Monuments Ordinance</li> </ul>
S.12.5	CH2	<ul> <li><u>Terrestrial Archaeology</u></li> <li>Implement watching brief during construction phase (see Figure 14.1 for the locations of watching brief)</li> </ul>	To identify and record any archaeological material or features revealed during construction phase	Future Private	During construction phase	During construction phase	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
EM&A P	roject						
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control EM&A Performance	Project Proponent	All constructi on sites		<ul> <li>EIAO Guidance Note No.4/2010</li> <li>TM-EIAO</li> </ul>
S13.2 – 13.4	EM2	<ol> <li>An Environmental Team needs to be employed as per the EM&amp;A Manual.</li> <li>Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures.</li> <li>An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&amp;A Manual are fully complied with.</li> </ol>	Perform environmental monitoring & auditing	Project Proponent	All constructi on sites		<ul> <li>EIAO Guidance Note No.4/2010</li> <li>TM-EIAO</li> </ul>

Docum ent Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Works Ve	essel Travel	Routes (Extracted from Works Vessel Travel Route Plan subm	itted under Condition 2.13 of	f the EP)			
S3.2	WVTR1	All works vessels shall be equipped with Global Positional System (GPS) or equivalent automatic identification system (AIS) for real time tracking and monitoring of their travel routing, speed and anchorage points. The system shall be capable to record and analyse the travel routing, speed and anchorage points.	Control EM&A Performance	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S3.3.1	WVTR2	<ol> <li>Once approaching or leaving the entrance of the silt curtain, all vessels will travel at a speed no greater than 8 knots between the site and boundary of The Brothers Marine Park. The vessels can then navigate at normal speed (8-12 knots) after that distance unless other restrictions are imposed.</li> <li>If any dolphins are sighted within 250m of a vessel then the vessel will slow down to a speed no greater than 5 knots for at least 3 minutes after the last sighting.</li> </ol>	Protection of CWD	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
\$3.3.2	WVTR3	All captains and the supervising staff should undergo training to learn about local dolphins and porpoises. They should be trained to be aware of the protocol for dolphin friendly" vessel operation (refer to the Code of Conduct for Dolphin Watching Activities from AFCD).	Protection of CWD	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
\$3.3.2	WVTR4	Training on the requirements of the WVTRP would be provided for construction vessels' personnel to follow, which should include the details of the normal operational routings of the construction works vessels and reporting of deviations from the normal operational routings of the construction works vessels. The training course will be given to the licensed vessel captains by the trainers before commencement of work and refreshment course will be provided every quarter.	Protection of CWD	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>

Docum ent Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Deploym	ent of Silt C	urtain(s) (Extracted from Silt Curtain Deployment Plan submit	tted under Condition 2.16 of t	the EP)			
S4	SCD1	Before the start of the installation work, Qualified Ecologists with dolphin monitoring experience shall scan the exclusion zone for at least 30 minutes. If dolphins are observed in the exclusion zone, the installation work shall be delayed until the dolphins left the area.	Protection of CWD	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S4	SCD2	If dolphins are observed within the exclusion zone during the installation work, the relevant part of the work shall cease until the dolphins left the area.	Protection of CWD	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S5	SCD3	On-board supervisors will be assigned to check the condition of the silt curtain before commencement of works every day. An inspection checklist will be kept on site for record purpose.	Silt Curtain Integrity	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S5	SCD4	For the tentative arrangement of silt curtain under adverse weather, the silt curtain will not be temporary removed during adverse weather. However, related works will be suspended immediately if silt curtain is found any damaged.	Silt Curtain Integrity	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S5	SCD5	Diver inspection shall be carried out if necessary to inspect the installation and decommission of silt curtain to ensure proper installation and functioning of the silt curtain according to the design drawings. Nearby marine works will resume after repairing of the damaged silt curtains.	Silt Curtain Integrity	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>
S5	SCD6	Refuse around the silt curtain will be collected at regular intervals on a daily basis so that water behind the silt curtains will be kept free from floating debris.	Waste Management	Contractor	All marine constructi on sites	Construction stage	<ul> <li>EIA</li> <li>Contractual requirements</li> </ul>

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
Post-plan	ting Monito	oring and Maintenance (Details to be provided after the submiss	sion of Detailed Compensato	ry Woodland Plantin	eg Plan as re	equired under EP Co	ndition 2.22)

EIA Ref.EM&A Log RefRecommended Mitigation MeasuresObjectives of the Recommended Measures & Mai Concerns to address	Implementation		Implementation Stage	Requirements and / or standards to be achieved
--	----------------	--	-------------------------	---

Use of New Low Noise Road Surfacing Material(s) (Details to be provided after the submission of Plan for Review of Use of New Low Noise Road Surfacing Material(s) as required under EP Condition 2.23)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved
	-	be taken by the Contractor and Dump Truck Drivers in case dition 2.24 of the EP)	of Illegal Dumping and La	ndfilling of C&D M	aterials (Ex	tracted from Waste	Management Plan
\$5.4	WM1	Investigation report will be prepared by the Contractor and submit to ER within 2 working days.	Control EM&A Performance	Contractor	All constructi on sites	Construction stage	• EP • Contractual requirements
S5.4	WM2	The Contractor will discuss with ER for the follow up actions (e.g. warning letter, cease operation, etc.) if required.	Control EM&A Performance	Contractor	All constructi on sites	Construction stage	• EP • Contractual requirements



# ANNEX C

STATUS OF SUBMISSIONS AND IMPLEMENTATION STATUS OF MITIGATION MEASURES UNDER EP

EP Conditio	Submission / Implementation Status n	Status
2.1	Set up of Community and Professional	Community and Professional Liaison
	Liaison Groups	Groups were set up.
2.1	Complaint Management Plan (for	Updated Plan was accepted by EPD or
	Contracts 1, 2, 3 and 7)	19 January 2023
2.5	Employment of Qualified Ecologist(s)	Qualified Ecologists have been
	, , , , , , , , , , , , , , , , , , ,	employed to carry out work relating to ecological aspects.
2.6	Employment of Surveillance Team	Surveillance Team has been employed to conduct regular site inspection.
2.11	Management Organizations (for Contracts 1, 2, 3 and 7)	Updated Submission was submitted to EPD on 1 June 2022 and accepted by EPD on 7 June 2022
2.12	Construction Works Schedule and Location Plans (for Contracts 1, 2, 3 and 7)	Updated Plan was accepted by EPD or 3 March 2023
2.13	Works Vessel Travel Route Plan (for Contract 1)	Accepted by EPD
2.14	Eco-shoreline Implementation Plan (for Contract 1)	Updated Plan was accepted by EPD or 24 July 2023
2.15	Dolphin Watching Plan (for Contract 1)	Updated Plan was submitted on 21 September 2018 and accepted by EPD on 12 October 2018
2.16	Silt Curtain Deployment Plan (for Contract 1)	Updated Plan was accepted by EPD o 24 April 2023
2.17	Spill Response Plan (for Contract 1)	Accepted by EPD
2.18	Plan on Provision of Buffer Zones	To be prepared no later than 3 months before the commencement of construction works at Tung Chung Valley. Refer to the EM&A Reports of
2.19	River Park Plan	TCW. To be prepared no later than 3 months before the commencement of construction works at Tung Chung Valley. Refer to the EM&A Reports of TCW.
2.20	Habitat Enhancement and Translocation Plan for Amphibian Species of Conservation Importance	To be prepared no later than 3 months before the commencement of construction works at Tung Chung Valley. Refer to the EM&A Reports of TCW.
2.21	Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance	Accepted by EPD on 9 December 2021
2.22	Detailed Compensatory Woodland Planting Plan	The Plan was submitted to EPD on 10 June 2022 and accepted with condition by EPD on 23 June 2022
2.23	Plan for Review of Use of New Low Noise Road Surfacing Material(s)	The revised Plan was submitted to EP on 20 December 2023
2.24	Waste Management Plan (for Contracts 1, 2, 3 and 7)	Updated Plan was accepted by EPD o 18 May 2023

## Annex C Status of Submissions and Implementation Status of Mitigation Measures under EP

EP	Submission / Implementation Status	Status
Condition	, I	
2.25	(i) no dredging of marine sediment shall	Completed
	be carried out for the Project	
	(ii) all reclamation filling works shall be	Completed
	carried out within a leading seawall of	
	at least 200m; and	
	(iii) silt curtains surrounding the	Completed
	reclamation area shall be deployed in	
	accordance with the Silt Curtain	
	Deployment Plan	
2.26	Implement Silt Curtain Deployment Plan	Completed
	and Spill Response Plan	
2.27	Implement dolphin exclusion zone of	Completed
	250m around the reclamation site at Tung	
	Chung East during the installation of the	
	perimeter silt curtains and any re-	
	deployment of the perimeter silt curtains	
2.20	by Qualified Ecologist(s)	Completed
2.28	Once the perimeter silt curtains are	Completed
	installed or re-deployed, the Dolphin Watching Plan shall be implemented as	
	part of the EM&A programme	
2.29	(i) no underwater blasting and	Completed
2.2)	percussive piling shall be carried out for	completed
	the Project; and	
	(ii) air compressors and other noisy	Completed
	equipment mounted on works vessels	I
	shall be acoustically-decoupled	
2.30	Implement Works Vessel Travel Route	Completed
	Plan	
	Implement Eco-shoreline Implementation	Under implementation
	Plan	
	Implement Dolphin Watching Plan	Completed
2.31	Implement Plan on Provision of Buffer	Detailed Preservation and/or
	Zones, River Park Plan, Habitat	Translocation Plan for Plant Species of
	Enhancement and Translocation Plan for	Conservation Importance and Detailed
	Amphibian Species of Conservation	Compensatory Woodland Planting Plan
	Importance, Detailed Preservation and/or	are under implementation
	Translocation Plan for Plant Species of	
	Conservation Importance and Detailed	
	Compensatory Woodland Planting Plan	
2.32	Implement Plan for review of the use of	To be implemented
	new road surfacing material(s)	The low inclusion of the second
<b>n</b> 22	Implement Waste Management Plan	Under implementation
2.33	Install noise barriers and low noise road	To be implemented
	surfacing at the extended Chung Mun	
	Road and Road D3	
	All noise mitigation measures implemented shall be properly	
	maintained during the operation of the	
	above roads	
	a	

EP	Submission / Implementation Status	Status
Condition		
2.34	Implement a deodouriser with an odour removal efficiency of at least 95% shall be installed, operated and maintained within each sewage pumping station. The exhaust of the deodouriser shall be oriented away from sensitive receivers; and all odourous facilities of each sewage pumping station shall be enclosed and negative pressure shall be maintained within the facilities.	To be implemented
2.35	Enclose all the pumps inside a building structure	To be implemented
2.36	(i) a 100% standby pumping capacity shall be installed and maintained	To be implemented
	(ii) a 50% spare pumping capacity shall be installed and maintained	To be implemented
	(iii) dual-feed power supply shall be installed and maintained; and	To be implemented
	(iv) an emergency facility with a 6-hour storage capacity of average dry weather flow shall be installed and maintained.	To be implemented



### ANNEX D

STATUS OF STATUTORY ENVIRONMENTAL REQUIREMENS

Contract No.	Description	Location	Ref No.	Status
General	Environmental Permit	TCNTE Works Area	EP-519/2016	Granted on 9 Aug 2016
Contract No. NL/2017/03 (Contract 1)	Discharge License under Water Pollution Control Ordinance	Area WA1, near Ying Tung Road, Tung Chung	WT00034715-2019	Validity from 21 Jan 2020 to 31 Jan 2025
	Billing Account for Disposal of Construction Waste	-	Application No. 7029877	Approved on 22 January 2018
	Registration as Chemical Waste Producer	Site Office for TCE	WPN-5213-950- B2528-01	Issued on 28 Feb 2018
	Tiotucci	TCE Site Area	WPN-5213-950- B2528-02	Issued on 20 Apr 2018
		Area WA3, near To Kau Wan, Tung Chung	WPN-5213-974- B2528-03	Issued on 9 April 2019
Contract No. NL/2020/02 (Contract 2)	Billing Account for Disposal of Construction Waste	-	Application No. 7040975	Approved on 29 Jul 2021
	Registration as Chemical Waste Producer	Working site of Contract No. NL/2020/02	WPN-5213-950- C4323-04	Issued on 17 Aug 2021
	Discharge License under Water Pollution Control Ordinance	Portion 3	WT00040695-2022	Validity from 14 Jun 2022 to 30 Jun 2027
	Ordinance	Portion 5A and 6	WT00040696-2022	Validity from 14 Jun 2022 to 30 Jun 2027
		HDD Area	WT00042688-2022	Validity from 2 Feb 2023 to 29 Feb 2028
Contract No. NL/2020/03 (Contract 3)	Billing Account for Disposal of Construction Waste	-	Application No. 7041004	Approved on 13 Jul 2021
	Registration as Chemical Waste Producer	Working site of Contract No. NL/2020/03	WPN-5213-950- B2500-07	Issued on 25 Aug 2021

### Annex D Status of Statutory Environmental Requirements

Contract No.	Description	Location	Ref No.	Status
	Construction Noise Permit	Main Reclamation Area and MDN Areas	GW-RS0253-24 <sup>(1)</sup>	Validity from 28 Mar 2024 to 27 Sep 2024
			GW-RS0458-24	Validity from 18 May 2024 to 27 Oct 2024
		General Works in To Kau Wan	GW-RW0864-23	Validity from 20 Dec 2023 to 19 Jun 2024
		Trucks Mobilization	GW-RS0324-24	Validity from 28 Apr 2024 to 27 Oct 2024
		24 Hours Twin Rising Mains Pipe Jacking Operation at Ying Tung Road	GW-RS0154-24	Validity from 25 Feb 2024 to 24 May 2024
		Percussive Piling Works at CUT Area	PP-RS0008-24	Validity from 8 May 2024 to 27 Sep 2024
	Discharge License under Water Pollution Control Ordinance	Construction Site of Contract No. NL/2020/03	WT00039577-2021	Validity from 1 Dec 2021 to 31 Dec 2026
	Crummite	Construction Site of Contract No. NL/2020/03 (Man Tung Road)	WT10001265-2023	Validity from 13 Oct 2023 to 31 Oc 2028
		Construction Site of Contract No. NL/2020/03 (Yi Tung Road)	WT10001296-2023	Validity from 19 Oct 2023 to 31 Oc 2028
	Licence for the conduct of a Specified Process (SP Licence)	TCNTE Works Area	L-3-264 (1)	Validity from 12 Aug 2020 to 11 Aug 2024
Contract No. NL/2020/07 (Contract 7)	Billing Account for Disposal of Construction Waste	-	Application No. 7041997	Approved on 26 Oct 2021
	Registration as Chemical Waste Producer	Working site of Contract No. NL/2020/07	WPN-5213-961- B2500-08	Issued on 30 Nov 2021
	Construction Noise Permit	Portion 32 Sea Wall	GW-RS0108-24	Validity from 23 Feb 2024 to 22 Aug 2024

Contract No.	Description	Location	Ref No.	Status
		C7 Site Office	GW-RS0403-23	Validity from 2 May 2024 to 28 Oct 2024
		Portion 32 Receiving Pit	GW-RS0228-24	Validity from 16 Apr 2023 to 15 Oct 2024
		Portion 34 Pipe Laying	GW-RS1019-23	Validity from 23 Nov 2023 to 20 May 2024
		Portion 31 Bored Pile	GW-RS1074-23	Validity from 18 Dec 2023 to 17 Jun 2024
		Portion 33 Jacking Pit	GW-RS0330-24	Validity from 12 Apr 2024 to 8 Oct 2024
		Portion 146	GW-RS0276-24	Validity from 3 Apr 2024 to 2 Oct 2024
	Discharge License under Water Pollution Control Ordinance	Contract No.	WT00041756-2022	Validity from 27 Oct 2022 to 31 Oct 2027
		Working site of Contract No. NL/2020/07 (Portion 33, 36- 38)	WT00040693-2022	Validity from 31 May 2022 to 31 May 2027
		Working site of Contract No. NL/2020/07 (Portion 30, 31)	WT0043124-2023	Validity from 2 Mar 2023 to 31 Mar 2028
		Working site of Contract No. NL/2020/07 (Portion 146)	WT00043119-2023	Validity from 2 Mar 2023 to 31 Mar 2028

(1) GW-RS0253-24 was replaced by GW-RS0458-24 since 18 May 2024.



ANNEX E AIR QUALITY



### ANNEX E1

CALIBRATION CERTIFICATES FOR AIR QUALITY

# ALS Technichem (HK) Pty Ltd

### **ALS Laboratory Group**

ANALYTICAL CHEMISTRY & TESTING SERVICES



#### SUB-CONTRACTING REPORT

CONTACT	: MR MAGNUM FAN	WORK ORDER HK2342916
CLIENT	ENVIROTECH SERVICES CO.	
ADDRESS	: RM 712, 7/F, MY LOFT 9 HOI WING ROAD,	SUB-BATCH : 1
	TUEN MUN, N.T. HK	DATE RECEIVED : 26-OCT-2023 DATE OF ISSUE : 2-NOV-2023
PROJECT	: ·	NO. OF SAMPLES : 1 CLIENT ORDER +

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Result(s) of sample(s) is/are reported on as received basis, unless otherwise specified. The result(s) is/are related only to the item(s) tested.
- Calibration was subcontracted to Envirotech Services Company.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories	Position	
Rulard Frag.		0
Richard Fung	Managing Director	
and for the station of the state of the stat		

This report supersedes any previous report(s) with the same work order number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd Part of the ALS Laboratory Group

11/F Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com WORK ORDER

: HK2342916

1 ENVIROTECH SERVICES CO.

: -----

CLIENT PROJECT

SUB-BATCH



3

ALS Lab	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.	
HK2342916-001	Sibata LD-3B (436553)	Equipments	21-Oct-2023	S/N: 436553	



### Envirotech Services Co.

Rm. 712, 7/F Rm. /12, //F My Loft, 9 Hol Wing Road, Tuen Mun, H.K. Tel: 2560 8450 Fax: 2560 8553 E-mail: environation

#### **Equipment Verification Report (TSP)**

### **Equipment Calibrated:**

Туре:	Laser Dust Monitor	
Manufacturer:	Sibata LD-3B	
Serial No.:	436553	
Equipment Ref.:	N/A	
ALS Job Order:	НК2342309	

#### **Standard Equipment**


Standard Equipment:	High Volume Sampler (TSP)		
Location :	Envirotech Room (Calibration Room)		
Equipment Ref.:	HVS 8162		
Last Calibration Date:	21-Oct-2023		

#### **Equipment Verification Results:**

Verification Date:

14-Oct-2023

Hour	Time	Mean Temp <sup>o</sup> C	Mean Pressure (hpa)	Concentration in µg/m <sup>3</sup> (Standard Equipment) (Y-Axis)	Concentration in µg/m <sup>3</sup> (Calibrated Equipment) (X-Axis)
1hr 00mins	0910-1010	21.8	1019	10	17
2hr 00mins	1015-1215	21.8	1019	30	38
3hr 00mins	. 1410-1710	23.5	1019	71	67



Factor <u>1.0622 (µg/m<sup>3</sup>)/CPM</u> should be applied for TSP monitoring


\*If R<0.5, repair or verification is required for the equipment

Operator:	P.F.Yeung	Signature	Fai	Date:	26 October 2023
QC Reviewer:	K.F.Ho	Signature	Fat	Date:	26 October 2023

### TSP SAMPLER CALIBRATION CACULATION SPREADSHEET

Location : HVS ID:	Rm. 712 8162	2, My Lo	oft, Tuen M	un <sup>-</sup>		Date of Cali Next Calibra		3-Oct-23
Name and	3.7	TISCH	HVS Mode	TE_51	70	Operator:		-Dec-23
	110001.	10011	1110 111000	CONDI		Operator.	F.1	F.Yeung
				00101	.110140			
	Sea Lev	el Pressi	ure (hpa)	10	)15	Corrected Pr	essure (mm Hg)	762.1
	Tempera	ature (°C	)	2	8.9	Temperature	(K)	293
and the second								
				CALIB	RATION	ORIFICE		
			Make:	TISC	CH	Qstd Slope		2.06918
			Model:	TE-502	5A	Qstd Interce		0.04220
			Serial#:	24	54			
an a				CALIBI	RATION			9998 - Balance Berry, Company, Company, Company, Company, Company, Company, Company, Company, Company, Company
Plate	H2O(L)	H20(R)	H2O	Qstd	I	IC	LINE	EAR
No.	(in)	(in)	(in)	(m3/mi	1	and the second second		RESSION
18	6.5	6.5	13.0	1.806	62	. 63.54	Slope= 32.84	13
13	4.7	4.7	9.4	1.539	56	57.39	Intercept= 5.518	3
10	3.4	3.4	6.8	1.312	49	50.22	Corr. Coeff.= 0.993	39
7	2.3	2.2	4.5	1.071		40.99		
5	1.6	1.5	3.1	0.892	33	33.82		
Calulations:					IC		Flow Rate	
		Pa/Pstd)(	[[std/Ta])-b]		70			
C = I[Sqrt(]					65			
					60			
Qstd = stand	ard flow ra	ate			55			
C = corrector	ed chart re	sponse			F			
= actual ch					50		>/	
n = calibrat	1000 CO. 100 C				45	NTRACTORARY THE BEAU AND A MARK OF A MARK		
$\phi = \text{calibrate}$					40 -			
			alibration (d	and the second	35			
'a = actual p	pressure du	ring calib	oration (mm ]	dg)	30	•		
For subseque	ent calcula	tion of sa	impler flow:		25			
1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)					20			
					÷.			
n = sample	20230			and the state of the state	15			
= sampler		1		and all second as	10	0 0 0 1 0 1	1 1.2 1.3 1.4 1.5 1.	
= chart re:	122				0.7 0		1 1.2 1.3 1.4 1.5 1. 2std( m3/min)	0 1./ 1.8 1.9
av = daily a						(		
av = daily a	iverage pre	ssure		a tan				and a set of the set of

4

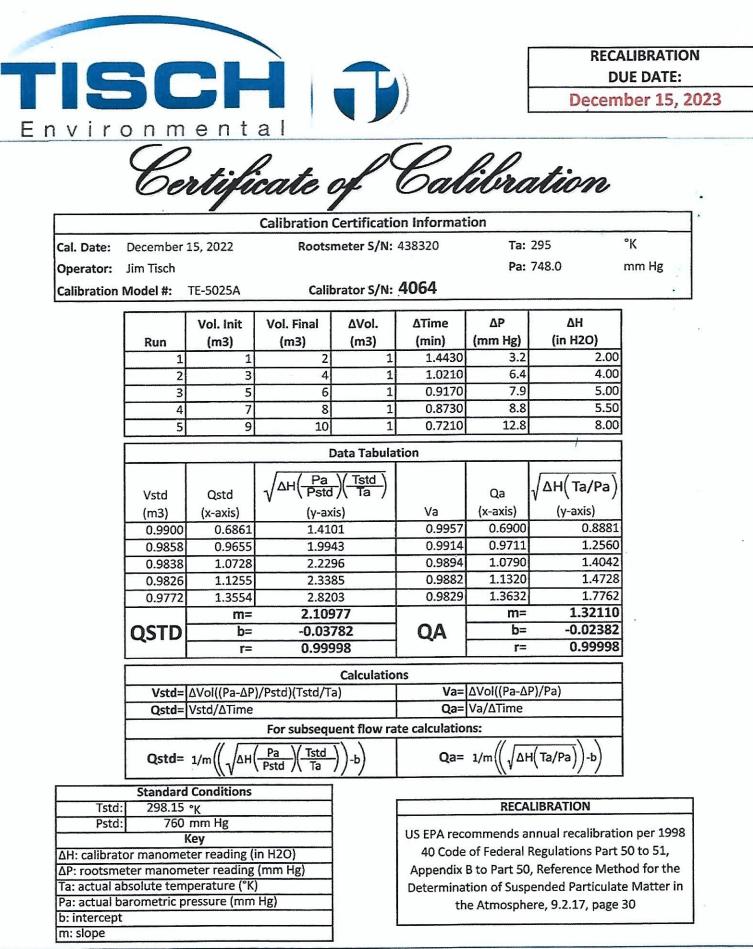

Tisch Environmental, Inc.

145 South Miami Avenue

Village of Cleves, OH 45002

<u>www.tisch-env.con</u> TOLL FREE: (877)263-7610 FAX: (513)467-900!



### ANNEX E2

MONITORING SCHEDULE FOR AIR QUALITY

### Tung Chung New Town Extension (East) Air Quality Monitoring Schedule (May 2024)


			Monitoring Ocheu			
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1-May	2-May	3-May	4-May
				Air Quality Monitoring		
5-May	6-May	7-May	8-May	9-May	10-May	11-May
			Air Quality Monitoring			
12-May	13-May	14-May	15-May	16-May	17-May	18-May
		Air Quality Monitoring				
19-May	20-May	21-May	22-May	23-May	24-May	25-May
	Air Quality Monitoring					Air Quality Monitoring
26-May	27-May	28-May	29-May	30-May	31-May	
					Air Quality Monitoring	



# ANNEX E3 MONITORING RESULTS FOR AIR QUALITY

Date	Start Time	Finish Time	Weather	1-hour TSP (µg/m³)
5/2/2024	10:02	11:02	Cloudy	57
5/2/2024	9:02	10:02	Cloudy	54
5/2/2024	11:02	12:02	Cloudy	53
5/8/2024	9:00	10:00	Cloudy	60
5/8/2024	10:00	11:00	Cloudy	62
5/8/2024	11:00	12:00	Cloudy	61
5/14/2024	13:45	14:45	Sunny	37
5/14/2024	14:45	15:45	Sunny	41
5/14/2024	15:45	16:45	Sunny	49
5/20/2024	9:02	10:02	Cloudy	44
5/20/2024	10:02	11:02	Cloudy	46
5/20/2024	11:02	12:02	Cloudy	47
5/25/2024	13:08	14:08	Cloudy	46
5/25/2024	14:08	15:08	Cloudy	48
5/25/2024	15:08	16:08	Cloudy	51
5/31/2024	13:11	14:11	Cloudy	47
5/31/2024	14:11	15:11	Cloudy	49
5/31/2024	15:11	16:11	Cloudy	46

### Table E3Data for 1-hr TSP Monitoring at Station DM-1

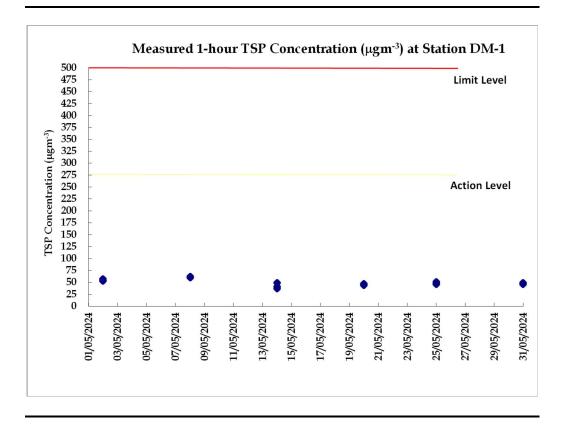



## ANNEX E4

EVENT AND ACTION PLAN FOR AIR QUALITY

Encet	Action						
Event	ET	IEC	ER	Contractor			
Action level exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform IEC and ER;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily.</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method.</li> </ol>	1. Notify Contractor.	<ol> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate.</li> </ol>			
Action level exceedance for two or more consecutive samples	<ol> <li>Identify source;</li> <li>Inform IEC and ER;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and ER;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>Supervise Implementation of remedial measures.</li> </ol>	<ul><li>failure in writing;</li><li>2. Notify Contractor;</li><li>3. Ensure remedial measures properly implemented.</li></ul>	<ol> <li>Submit proposals for remedial to ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ol>			

### Annex E4 Event and Action Plan for Air Quality

E	Action						
Event	ET	IEC	ER	Contractor			
Limit level exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform ER, Contractor and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Supervise implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ol>			
Limit level exceedance for two or more consecutive samples	<ol> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>			



# ANNEX F NOISE



# ANNEX F1 CALIBRATION CERTIFICATES FOR NOISE



Sun Creation Engineering Limited Calibration & Testing Laboratory


# Certificate of Calibration 校正證書

Certificate No.: C240423 證書編號

	<ul> <li>【目 (Job No. / 序引編號: IC24-0020)</li> <li>Precision Acoustic Calibrator</li> <li>LARSON DAVIS</li> <li>CAL200</li> <li>16172</li> <li>Envirotech Services Co. Room 712, 7/F, My Loft, 9 Hoi Wing New Territories, Hong Kong</li> </ul>	Date of Receipt / 收件日期:5 January 2024
TEST CONDITIONS / / Temperature / 溫度 : Line Voltage / 電壓 :	$(23 \pm 2)^{\circ}C$	Relative Humidity / 相對濕度 : (50 ± 25)%
TEST SPECIFICATIO Calibration check	NS / 測試規範	a)
DATE OF TEST / 測試	日期 : 24 January 2024	×
<b>TEST RESULTS / 測試</b> The results apply to the part The results do not exceed sp These limits refer to manufa The results are detailed in th	icular unit-under-test only. ecified limits. cturer's published tolerances as requested by the	e customer.
- The Government of The H		
Tested By : 測試	K/C Lee Engineer	
Certified By : 核證		ate of Issue : 24 January 2024 簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C240423 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

Equipment IDDescriptionCertificate No.CL130Universal CounterC233799CL281Multifunction Acoustic CalibratorCDK2302738TST150AMeasuring AmplifierC221750

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Limit	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	93.90	± 0.2	$\pm 0.20$
114 dB, 1 kHz	113.90		

#### 5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Limit	(Hz)
1	1.000	$1 \text{ kHz} \pm 1 \%$	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C234378 證書編號

ITEM TESTED / 送檢項目 Description / 儀器名稱 : Manufacturer / 製造商 : Model No. / 型號 : Serial No. / 編號 : Supplied By / 委託者 :	(Job No. / 序引編號: IC23-1403) Sound Level Meter Rion NL-52 00331806 Envirotech Services Co. Room 712, 7/F, My Loft, 9 Hoi Wing New Territories, Hong Kong	Date of Receipt / 收件日期:11 July 2023
TEST CONDITIONS / 測記 Temperature / 溫度 : (2 Line Voltage / 電壓 :		Relative Humidity / 相對濕度 : (50±25)%
TEST SPECIFICATIONS Calibration check	/ 測試規範	
DATE OF TEST / 測試日期	月 : 30 July 2023	
The results are detailed in the su The test equipment used for call	ar unit-under-test only. fied limits. rer's published tolerances as requested by th absequent page(s). bibration are traceable to National Standards g Kong Special Administrative Region Stan oration Laboratory, Denmark ght Technologies	via :
Tested By : 測試	H T Wong Assistant Engineer	
Certified By : 核證		Date of Issue : 31 July 2023 簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C234378 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C230306
CL281	Multifunction Acoustic Calibrator	CDK2302738

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

	UUT Setting			Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Limit (dB)
30 - 130	LA	A	Fast	94.00	1	93.1	$\pm 1.1$

#### 6.1.2 Linearity

	UUT Setting			Applied Value		UUT
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.1 (Ref.)
	A			104.00		103.1
	•			114.00		113.1

IEC 61672 Class 1 Limit :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

#### 6.2 Time Weighting

ine weigh		Setting		Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level Freq. (dB) (kHz)		Reading (dB)	Class 1 Limit (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.1	Ref.
	-A		Slow			93.1	$\pm 0.3$

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



輝創工程有限公司 Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C234378 證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

it weighting	UUT Setting				Applied Value UUT		IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Limit (dB)
30 - 130 L <sub>A</sub>	A	Fast	94.00	63 Hz	66.8	$-26.2 \pm 1.5$	
					125 Hz	76.9	$-16.1 \pm 1.5$
					250 Hz	84.4	$-8.6 \pm 1.4$
					500 Hz	89.8	$-3.2 \pm 1.4$
					1 kHz	93.1	Ref.
				2 kHz	94.3	$+1.2 \pm 1.6$	
					4 kHz	94.1	$+1.0 \pm 1.6$
				8 kHz	92.0	-1.1 (+2.1 ; -3.1)	
					16 kHz	85.1	-6.6 (+3.5 ; -17.0)

#### 6.3.2 C-Weighting

UUT Setting				Appli	lied Value UUT		IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Limit (dB)
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	92.2	$-0.8 \pm 1.5$
	-				125 Hz	92.9	$-0.2 \pm 1.5$
					250 Hz	93.0	$0.0 \pm 1.4$
					500 Hz	93.1	$0.0 \pm 1.4$
					1 kHz	93.1	Ref.
					2 kHz	92.9	$-0.2 \pm 1.6$
					4 kHz	92.3	$-0.8 \pm 1.6$
					8 kHz	90.1	-3.0 (+2.1;-3.1)
					16 kHz	83.2	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準・局部複印本證書需先獲本實驗所書面批准。



# Certificate of Calibration 校正證書

Certificate No. : C234378 證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 10446

- Mfr's Limit : IEC 61672 Class 1

- Uncertainties of Applied Value :	94 dB :	63 Hz - 125 Hz	: ± 0.35 dB
		250 Hz - 500 Hz	: ± 0.30 dB
		1 kHz	$\pm 0.20 \text{ dB}$
		2 kHz - 4 kHz	$\pm 0.35 \text{ dB}$
		8 kHz	: ± 0.45 dB
		16 kHz	$\pm 0.70 \text{ dB}$
	104 dB:	1 kHz	$\pm 0.10 \text{ dB}$ (Ref. 94 dB)
	114 dB:	1 kHz	$\pm 0.10 \text{ dB}$ (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



ANNEX F2 MONITORING SCHEDULE FOR NOISE

### Tung Chung New Town Extension (East) Noise Monitoring Schedule (May 2024)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday			
			1-May	2-May	3-May	4-May			
				Noise Monitoring					
5-May	6-May	7-May	8-Mav	9-May	10-May	11-May			
			Noise Monitoring						
12-May	13-May	14-May	15-May	16-May	17-May	18-May			
		Noise Monitoring							
19-May	20-May	21-May	22-May	23-May	24-May	25-May			
	Noise Monitoring					Noise Monitoring			
26-May	27-May	28-May	29-May	30-May	31-May Noise Monitoring				




# ANNEX F3 MONITORING RESULTS FOR NOISE

Date & Time	L <sub>eq (5min)</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq (30min)</sub>
5/2/2024 9:03	67.1	69.3	61.1	
5/2/2024 9:08	67.8	71.0	61.2	
5/2/2024 9:13	68.3	71.3	61.7	67.1
5/2/2024 9:18	66.5	69.6	60.8	07.1
5/2/2024 9:23	65.7	68.8	60.1	-
5/2/2024 9:28	66.4	69.8	60.7	
5/8/2024 9:05	65.0	67.1	61.5	
5/8/2024 9:10	67.9	68.7	63.2	
5/8/2024 9:15	67.5	69.6	62.8	67.3
5/8/2024 9:20	66.8	69.2	62.4	07.5
5/8/2024 9:25	69.8	70.9	61.1	
5/8/2024 9:30	64.5	67.2	61.1	1
5/14/2024 14:51	63.9	66.3	60.2	
5/14/2024 14:56	63.0	65.3	58.9	
5/14/2024 15:01	64.1	66.9	59.2	05.0
5/14/2024 15:06	67.3	70.6	61.2	65.0
5/14/2024 15:11	65.4	67.6	61.3	1
5/14/2024 15:16	65.1	67.8	60.4	
5/20/2024 9:08	66.9	69.7	61.9	
5/20/2024 9:13	65.5	68.3	61.4	
5/20/2024 9:18	66.6	69.6	61.4	00.0
5/20/2024 9:23	66.4	68.4	62.1	66.6
5/20/2024 9:28	68.1	70.6	62.4	
5/20/2024 9:33	65.3	68.0	61.4	
5/25/2024 13:36	66.2	68.6	63.5	
5/25/2024 13:41	66.9	68.4	62.4	
5/25/2024 13:46	68.2	71.2	62.3	00.0
5/25/2024 13:51	65.4	67.9	61.6	66.2
5/25/2024 13:56	65.1	67.2	61.7	1
5/25/2024 14:01	64.0	65.9	61.2	1
5/31/2024 14:50	67.4	70.7	61.9	
5/31/2024 14:55	67.2	70.5	61.1	1
5/31/2024 15:00	67.0	69.6	62.7	1 07.0
5/31/2024 15:05	68.4	71.9	63.5	67.6
5/31/2024 15:10	67.5	70.8	61.9	1
5/31/2024 15:15	67.7	70.5	62.4	1

# Table F3.1Data for Noise Monitoring at Station NMS-CA-1A during Normal Working<br/>Hours (0700-1900 hours)


Figure F3.1 Graphical Presentation for Noise Monitoring at Station NMS-CA-1A

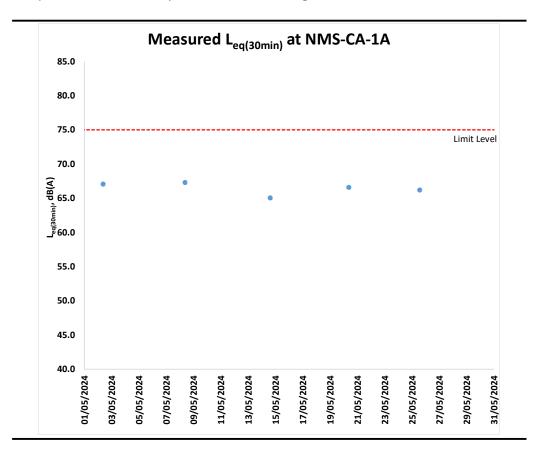

Date & Time	L <sub>eq (5min)</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq (30min)</sub>
5/2/2024 9:51	67.0	69.4	63.7	
5/2/2024 9:56	69.1	71.1	66.6	
5/2/2024 10:01	68.4	70.0	66.3	69.2
5/2/2024 10:06	69.0	70.4	67.1	
5/2/2024 10:11	69.1	71.1	66.9	
5/2/2024 10:16	71.3	73.4	68.4	
5/8/2024 9:41	68.6	71.1	65.1	
5/8/2024 9:46	69.7	71.3	65.8	
5/8/2024 9:51	68.0	69.9	65.6	68.4
5/8/2024 9:56	68.6	70.9	65.5	00.4
5/8/2024 10:01	67.2	69.0	65.0	
5/8/2024 10:06	67.7	69.9	65.1	
5/14/2024 14:08	69.4	71.4	65.6	
5/14/2024 14:13	71.1	72.9	66.3	
5/14/2024 14:18	70.9	73.9	64.5	70.4
5/14/2024 14:23	69.9	71.3	67.5	70.1
5/14/2024 14:28	69.2	70.8	66.2	
5/14/2024 14:33	69.7	71.4	66.7	
5/20/2024 9:50	68.2	70.8	64.7	
5/20/2024 9:55	68.9	71.1	66.0	
5/20/2024 10:00	69.0	71.0	66.0	68.8
5/20/2024 10:05	68.5	70.4	66.4	00.0
5/20/2024 10:10	69.3	71.7	66.1	
5/20/2024 10:15	68.9	71.0	66.5	
5/25/2024 13:00	65.8	68.3	62.9	
5/25/2024 13:05	65.8	67.9	63.2	
5/25/2024 13:10	66.7	68.6	64.4	66.7
5/25/2024 13:15	67.2	69.0	64.8	00.7
5/25/2024 13:20	67.4	69.1	65.0	
5/25/2024 13:25	67.1	69.1	65.2	
5/31/2024 13:49	70.5	72.7	66.4	
5/31/2024 13:54	69.1	71.6	65.8	]
5/31/2024 13:59	70.4	73.5	66.7	71.2
5/31/2024 14:04	72.0	74.6	67.0	] /1.2
5/31/2024 14:09	71.7	74.5	65.9	
5/31/2024 14:14	72.6	74.7	67.4	

# Table F3.2Data for Noise Monitoring at Station NMS-CA-4 during Normal Working<br/>Hours (0700-1900 hours)

Figure F3.2 Graphical Presentation for Noise Monitoring at Station NMS-CA-4

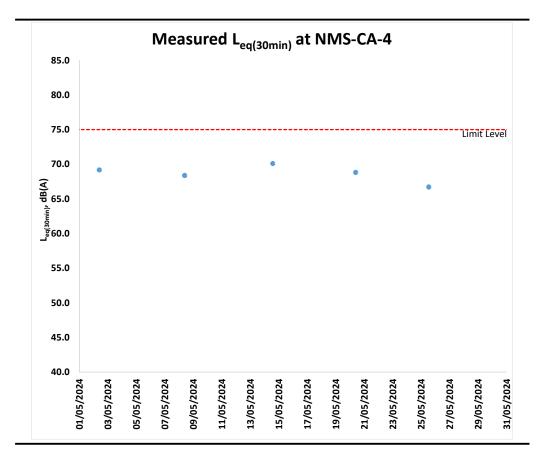



### ANNEX F4 EVENT AND ACTION PLAN FOR NOISE

Event	Action							
Event	ET	IEC	ER	Contractor				
Action Level Exceedance	<ol> <li>Notify IEC, ER and Contractor;</li> <li>Carry out investigation;</li> </ol>	1. Review the analysed results submitted by the ET;	1. Confirm receipt of notification of failure in writing;	1. Submit noise mitigation proposals to IEC and ER;				
	<ol> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the Contractor and formulate remedial measures;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Notify Contractor;</li> <li>Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>Ensure remedial measures are properly implemented</li> </ol>	2. Implement noise mitigation proposals.				
Limit Level Exceedance	<ol> <li>Identify source;</li> <li>Inform IEC, ER, EPD and Contractor;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>				

### Annex F4 Event and Action Plan for Construction Noise



# ANNEX G COMPENSATION WOODLAND MONITORING



Photo 1 - General view of compensation woodland in Portion 1



Photo 2 – General view of compensation woodland in Portion 2



ANNEX H

PRESERVED/TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE MONITORING



# ANNEX H1

#### PRESERVED PLANT SPECIES OF CONSERVATION IMPORTANCE



G01\_30-R001



G01\_30-R002



G01\_30-R004

G01\_30-R003



G01\_30-R005



G01\_39-R01\_Inaccessible



G01\_39-R02\_Inaccessible




G01\_81-RT-01



G01\_81-RT-02 (T1535)



G02\_29-R007

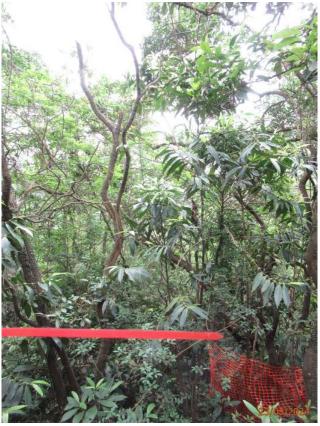

G02\_29-R013



G03\_44-R014



G03\_44-R015



G03\_44-R017



G04\_21-R03



G04\_45-R011



G04\_83\_84\_85-R04 (T1788)



G04\_83\_84\_85-R05 (T1572)



G04\_83\_84\_85-R06



G04\_83\_84\_85-R07



G04\_83\_84\_85-R08



G04\_83\_84\_85-R09



G04\_83\_84\_85-R010



G04\_83\_84\_85-R011



G05\_9-R04



G05\_67-R008



G06\_66-R009



R04 *Enkianthus quinqueflorus* Observed since November 2023



WLH\_T047

Aquilaria sinensis Observed since November 2023

Drawing no.	Tree group no.	Tree No.	Botanical Name	Chinese Name		SIZE		Amenity Value	Form	Health	Structural Condition	Conservation Status	Recommendation in Detailed Preservation and/or Translocation Plan for Plant Species of Conservation	Justification	Remarks
					Height (m)	DBH (mm)	Spread (m)		(Good/ I	Fair/ Poor)			Importance for Tung Chung East (Retain/ Transplant/ Fell)		
	C01/20	R01	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	On Slope, Inaccessible
	G01/39	R02	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	On Slope, Inaccessible
	G06/59	R018	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
	G03/61	R019	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
	G05/62	RT06	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Transplant	Direct conflict wit proposed works	Missing
	G01/01	RT-01	Gmelina chinensis	石梓	5	160	3	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Strangled by Epiphytes
	G01/81 -	RT-02 (T1535)	Gmelina chinensis	石梓	8	110	3	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Co-dominant Branches, Strangled by Epiphytes.
	-	WLH/T047	Aquilaria sinensis	土沉香	10	230	6	Good	Fair	Fair	Fair	Yes	Retain	-	On slope, Observed since November 2023
	G02/82	RT03	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Transplant	Direct conflict wit	h Missing
60507694/C2/1721		R04 (T1788)	Gmelina chinensis	石梓	9	260	8	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Multiple Trunks
		R05 (T1572)	Gmelina chinensis	石梓	8	120	5	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Broken branch
		R05	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
		R06	Gmelina chinensis	石梓	5	100	3	Good	Fair	Fair	Fair	Yes	Retain	-	On slope
	G04/83/84/85	R07	Gmelina chinensis	石梓	8	166	5	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Co-dominant Trunks
		R08	Gmelina chinensis	石梓	7	160	5	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Broken Leader, Epicormics, Imbalanced Crown
		R09	Gmelina chinensis	石梓	5	140	4	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Broken Leader wih Epiphyte, Broken Leader with Epicormics
		R010	Gmelina chinensis	石梓	8	110	3	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Broken Leader with Epicormics
		R011	Gmelina chinensis	石梓	9	130	4	Good	Poor	Fair	Poor	Yes	Retain	-	On slope, Multiple Branches, Leaning without Self- correction
	G04/21	R03	Gmelina chinensis	石梓	5	120	2	Good	Fair	Fair	Fair	Yes	Retain	-	Undersized, On Slope
60507694/C2/1722	_	R04	Enkianthus quinqueflorus	吊鐘花	2	130	3	Good	Fair	Fair	Fair	Yes	Retain	-	On slope, Observed since November 2023
	G05/9	R04	Gmelina chinensis	石梓	5	100	2	Good	Fair	Fair	Fair	Yes	Retain	-	On Slope
	G01/30	R001	Gmelina chinensis	石梓	7	110	2	Good	Poor	Fair	Fair	Yes	Retain	-	On Slope
		R002	Gmelina chinensis	石梓	8	120	5	Good	Poor	Poor	Fair	Yes	Retain	-	On slope, Co-dominant Branches, Root Flare was Partially
		R003	Gmelina chinensis	石梓	5	140	2	Good	Poor	Poor	Fair	Yes	Retain	-	Buried, Dead Stub On slope, Bulge at Trunk, Root Flare was Partially Buried,
		R004	Aquilaria sinensis	土沉香	10	150	3	Good	Fair	Fair	Fair	Yes	Retain	-	Climber On slope
		R005	Aquilaria sinensis	土沉香	8	130	3	Good	Fair	Fair	Fair	Yes	Retain	-	On slope
		R006	Aquilaria sinensis	土沉香	-	-	-	-	-	-	-	Yes	Retain	-	Missing
		R007	Gmelina chinensis	石梓	10	170	5	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Co-dominant Branches with Included Bark,
	G02/29	R013	Gmelina chinensis	石梓	8	150	7	Good	Poor	Fair	Fair	Yes	Retain	-	Crossed Branches, Old termite tracks on trunk On slope, Co-dominant Branches, Epicormics at Branch, Braken Leader with Epiphyte
60507694/C2/1732		R014	Gmelina chinensis	石梓	7	160	5	Good	Poor	Fair	Fair	Yes	Retain	-	Broken Leader with Epiphyte On slope, Co-dominant Branches
		R015	Gmelina chinensis	石梓	6	110	2	Good	Poor	Poor	Fair	Yes	Retain	_	On slope, Broken Leader, Epiphytes
	G03/44	R016	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
		R017	Gmelina chinensis	石梓	8	130	4	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Broken Leader with Epicormics
		R010	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
	G04/45	R011	Gmelina chinensis	石梓	8	140	7	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Co-dominant Branches
		R012	Gmelina chinensis	石梓	-	-	-	-	-	-	-	Yes	Retain	-	Missing
	G05/67	R008	Gmelina chinensis	石梓	6	120	4	Good	Fair	Fair	Fair	Yes	Retain	-	On slope
	G06/66	R009	Gmelina chinensis	石梓	7	120	5	Good	Poor	Fair	Fair	Yes	Retain	-	On slope, Epicormic at Broken Stump



## ANNEX H2

# TRANSPLANTED PLANT SPECIES OF CONSERVATION IMPORTANCE









RP04-Whole view of tree



Tree No.	Botanical Name	Chinese Name	SIZE		Amenity Value	Form	Health	Structural Condition	Conservation Status	Recommendation in Detailed Preservation and/or Translocation Plan for Plant Species of Conservation Importance for Tung Chung	Justification	Remarks	
			Height (m)	DBH (mm)	Spread (m)		(Good/ F	air/ Poor)			East (Retain/ Transplant/ Fell)		
RP04	Aquilaria sinensis	土沉香	4 -	81	2	Fair	Fair	Fair	Fair	Yes	Retain	-	Replacement Planting



# ANNEX I ECO-SHORELINE MONITORING

Photographic Records for Mangrove, Vertical and Rocky Eco-shoreline in May 2024



General View of Mangrove Eco-shoreline at Upper Terrace



General View of Rocky Eco-shoreline



General View of Mangrove Eco-shoreline at Lower Terrace



General View of Vertical Eco-shoreline



# ANNEX J LANDSCAPE AND VISUAL MONITORING



# ANNEX J1 EXAMPLES OF LANDSCAPE AND VISUAL MITIGATION MEASURES



Photo 1 – Tree protection zone for preserved plant species of conservation importance



Photo 2 - General view of compensation woodland



Photo 3 – Erection of site hoardings in unobtrusive colours

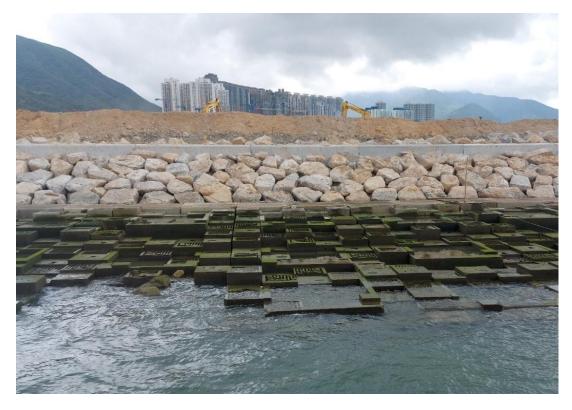


Photo 4 - Natural Rock Material/Planting for Artificial Seawall



Photo 5 - Orientation of night time lighting to minimize glare impact



#### ANNEX J2 EVENT AND ACTION PLAN FOR LANDSCAPE AND VISUAL MITIGATION MEASURES

Event	Action						
Event	ET	IEC	ER	Contractor			
Design Check	1. Check final design conforms to the requirements of EP and prepare report.	<ol> <li>Check report.</li> <li>Recommend remedial design if necessary.</li> </ol>	1. Undertake remedial design if necessary.				
Non-conformity on one occasion	<ol> <li>Inform the IEC, ER and the Contractor</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ol>	<ol> <li>Check report.</li> <li>Check Contractor's working method</li> <li>Discuss with ET, ER and Contractor on possible remedial measures.</li> <li>Advise ER on effective of proposed remedial measures.</li> <li>Check implementation of remedial measures</li> </ol>	<ol> <li>Confirm receipt of notification of non-conformity in writing</li> <li>Review and agree on the remedial measures proposed by the Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ol>	<ol> <li>Identify source and investigate the non-conformity</li> <li>Amend working methods agreed with ER as appropriate</li> <li>Rectify damage and undertake any necessary replacement</li> </ol>			
Repeated Non-conformity	<ol> <li>Identify sources</li> <li>Inform the Contractor, IEC and ER</li> <li>Discuss inspection frequency</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If non-conformity stops, cease additional monitoring</li> </ol>	<ol> <li>Check inspection report</li> <li>Check Contractor's working method</li> <li>Discuss with ET, ER and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures</li> </ol>	<ol> <li>Notify the Contractor</li> <li>In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented</li> <li>Supervise implementation of remedial measures</li> </ol>	<ol> <li>Identify source and investigate the non-conformity</li> <li>Amend working methods agreed with ER as appropriate</li> <li>Rectify damage and undertake any necessary replacement. Stop relevant portion of works as determined by ER until the non- conformity is abated.</li> </ol>			

#### Annex J2 Event and Action Plan for Landscape and Visual



### ANNEX K

CUMULATIVE STATISTICS ON EXCEEDANCES, ENVIRONMENTAL COMPLAINTS, NOTIFICATION OF SUMMONS AND STATUS OF PROSECUTIONS

#### Table K1Cumulative Statistics on Exceedances

		Total No. recorded in this reporting period (1)	Total No. recorded since project commencement
Air Quality (1-hr TSP)	Action	0	0
	Limit	0	0
Noise	Action	1	81
	Limit	0	0
Water Quality	Action	0	0
	Limit	0	0
Marine Ecology	Action	0	0
	Limit	0	0

Remark:

(1) Exceedances, which are not project related, are not shown in this table.

# Table K2Cumulative Statistics on Complaints, Notifications of Summons and<br/>Successful Prosecutions

Contract No.	<b>Reporting Period</b>		Cumulative Statistic	5
		Complaints	Notifications of	Prosecutions
		_	Summons	
Contract 1	This Reporting	1	0	0
	Period (1 - 31			
	May 2024)			
	Total no. received	111	0	0
	since project			
	commencement			
Contract 2	This Reporting	1	0	0
	Period (1 - 31			
	May 2024)			
	Total no. received	3	0	0
	since project			
	commencement			
Contract 3	This Reporting	2	0	0
	Period (1 - 31			
	May 2024)			
	Total no. received	63	0	0
	since project			
	commencement			
Contract 7	This Reporting	0	0	0
	Period (1 - 31			
	May 2024)			
	Total no. received	0	0	0
	since project			
	commencement			



# ANNEX L

### MONITORING SCHEDULE FOR THE NEXT REPORTING PERIOD

#### Tung Chung New Town Extension (East) Air Quality and Noise Monitoring Schedule (June 2024)

			olse Monitoring 3			
Sunday	Monday	Tuesdav	Wednesdav	Thursdav	Fridav	Saturday
						01-Jun
02-Jun	03-Jun	04-Jun	05-Jun	06-Jun	07-Jun	08-Jun
				Air Quality and Noise		
				Monitoring		
				monitoring		
09-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun
			Air Quality and Noise			
			Monitoring			
			Monitoring			
16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun	22-Jun
		Air Quality and Noise				
		Monitoring				
		wonitoning				
23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun	29-Jur
	Air Quality and Noise					Air Quality and Noise
	Monitoring					Monitoring
	Wontoning					Wontoning
30-Jun						

#### Tung Chung New Town Extension (East) Post-Construction Soft Shore Ecological Monitoring Schedule (June 2024)

Sunday	Monday		Wednesday		Friday	Saturday
						1-Jun
2-Jun	3-Jun	4-Jun	5-Jun	6-Jun	7-Jun	8-Jun
		Soft Shore Monitoring at	Soft Shore Monitoring at			
		Tung Chung Bay	Tai Ho Bay			
9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun
16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun	22-Jun
				Coff Chave Manifaring of	Coff Chang Manifering of	
				Soft Shore Monitoring at Tung Chung Bay	Soft Shore Monitoring at Tung Chung Bay	
				rung chung bay		
23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun	29-Jun
23-Jun	24-Juli	20-Juli	20-Juli	Z7-JUII	20-Juli	29-Juli
30-Jun						



# ERM HAS OVER 160 OFFICES ACROSS THE FOLLOWING COUNTRIES AND TERRITORIES WORLDWIDE

Argentina	The Netherlands
Australia	New Zealand
Belgium	Peru
Brazil	Poland
Canada	Portugal
China	Puerto Rico
Colombia	Romania
France	Senegal
Germany	Singapore
Ghana	South Africa
Guyana	South Korea
Hong Kong	Spain
India	Switzerland
Indonesia	Taiwan
Ireland	Tanzania
Italy	Thailand
Japan	UAE
Kazakhstan	UK
Kenya	US
Malaysia	Vietnam
Mexico	
Mozambique	

#### ERM

2507 One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong T: +852 22713000 F: +852 3015 8052

#### www.erm.com

